

MAINTENANCE OF TRAFFIC STAGE 1A (THIS SHEET)

SEQUENCE OF CONSTRUCTION

1. PROVIDE TEMPORARY AGGREGATE SURFACE COURSE WIDENING PER PROJECT DETAIL: CONSTRUCTING CULVERT UNDER TRAFFIC. CONSTRUCT 24" PIPE AT STA 680+54.
2. CONSTRUCT TEMPORARY SHOULDER ALONG EXISTING U.S. 45.
3. CONSTRUCT PROPOSED PERMANENT U.S. 45 EMBANKMENT AND PAVEMENT
4. CONSTRUCT PROPOSED TEMPORARY TRANSITION #1
5. CONSTRUCT PROPOSED PERMANENT GARNER RD. EMBANKMENT AND PAVEMENT

TRAFFIC PLACEMENT

1. MAINTAIN TRAFFIC ON EXISTING U.S. 45
2. ALL SIDEROADS SHALL REMAIN OPEN AND SHALL BE CONSTRUCTED UNDER TRAFFIC
3. ALL ENTRANCES SHALL REMAIN OPEN AND SHALL BE CONSTRUCTED UNDER TRAFFIC
4. TRAFFIC CONTROL DEVICES USED FOR TRAFFIC CONTROL SHALL BE PLACED IN THE WIDENING ALONG THE EDGE OF PAVEMENT WHEN NO WORK OPERATIONS ARE PRESENT AT THE END OF EACH WORK DAY AND WEEKENDS.

TRAFFIC CONTROL STANDARDS


701006, 701326, 701901

TRAFFIC CONTROL PAYMENT

TRAFFIC CONTROL AND PROTECTION, LUMP SUM AS PER TRAFFIC CONTROL STANDARD USED

NOTE:

ALT A & ALT B OPTION BEGINS AT STATION 449+88.13 AND CONTINUES TO THE END OF THE PROJECT.

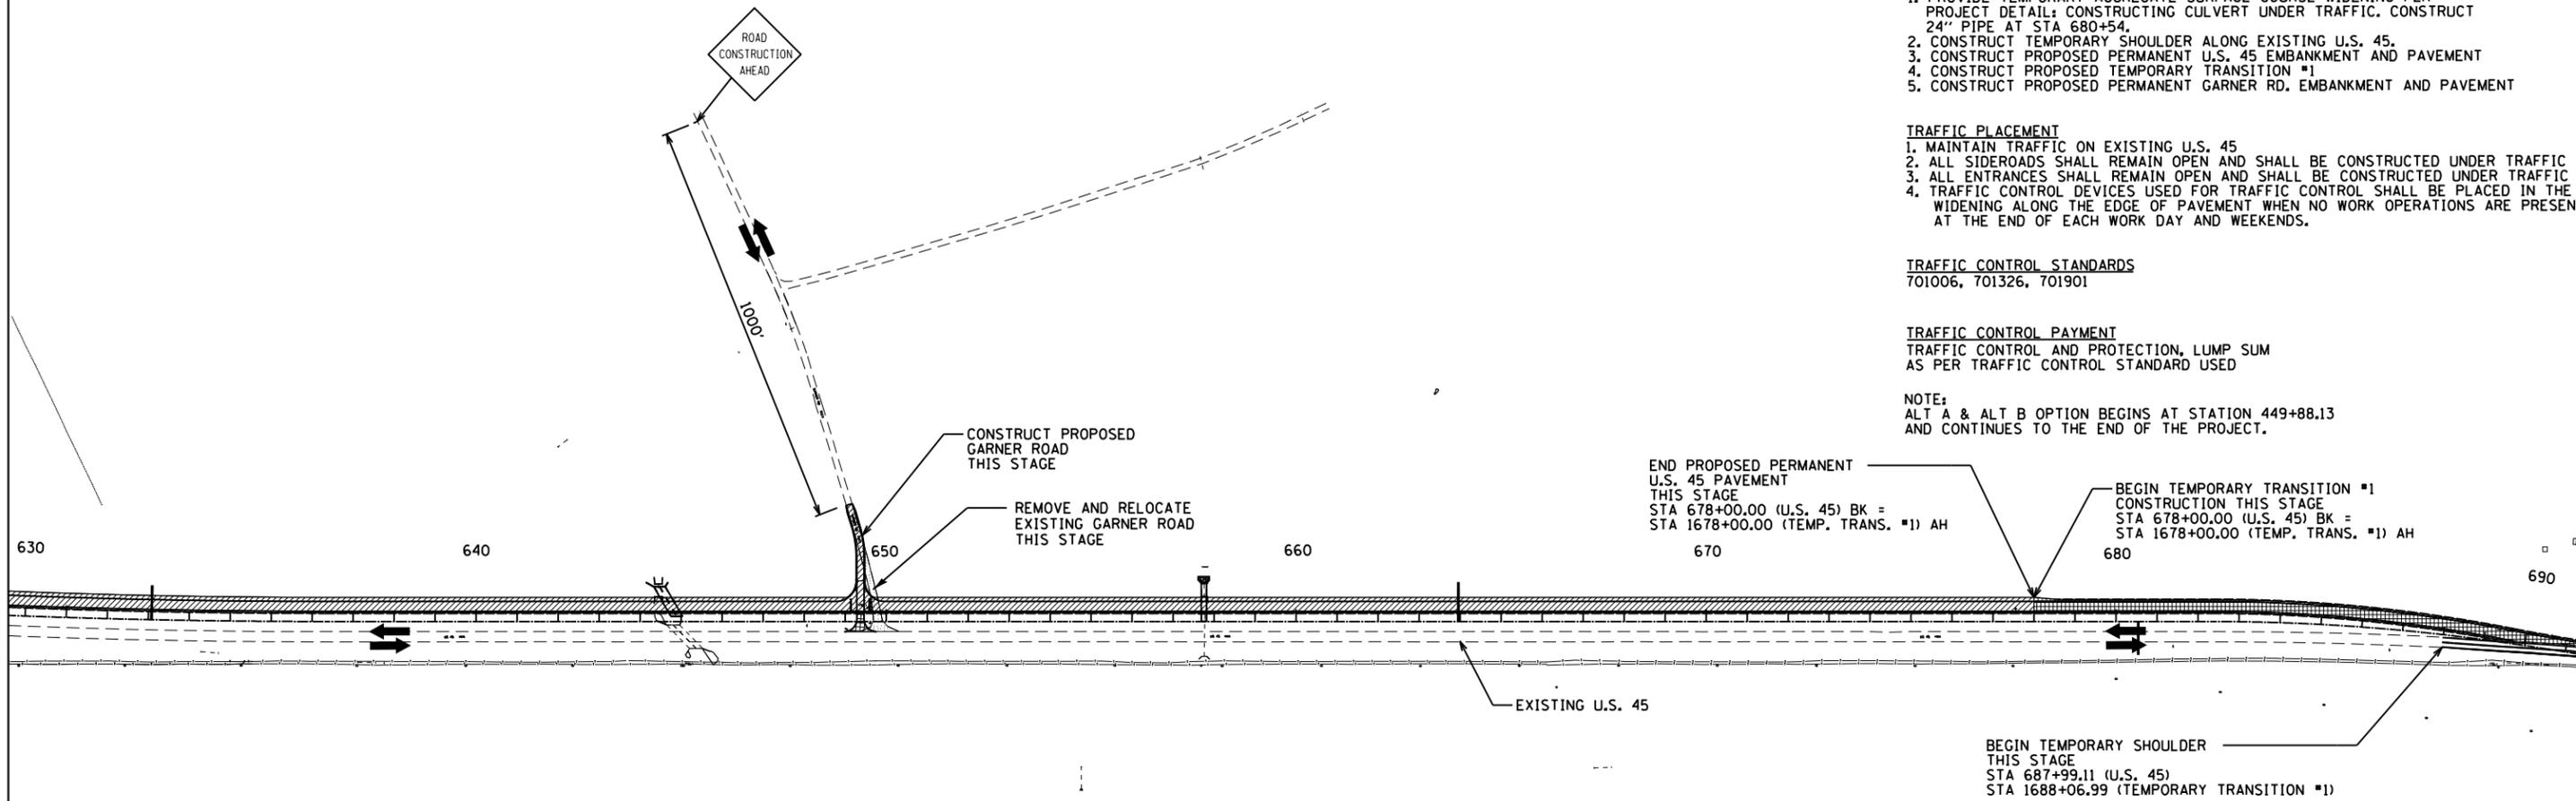

NOTES:

ALL SIDEROADS / ENTRANCES ARE TO REMAIN OPEN AND BE CONSTRUCTED WITH MINIMAL TEMPORARY SHUTDOWNS AT THE DIRECTION OF THE ENGINEER.

LEGEND	
	TEMPORARY PAVEMENT CONSTRUCTED AS NOTED
	PERMANENT PAVEMENT CONSTRUCTED THIS STAGE
	PERMANENT PAVEMENT CONSTRUCTED IN PREVIOUS STAGE
	PAVEMENT REMOVAL THIS STAGE
	DIRECTION OF TRAFFIC FLOW
	CONSTRUCTION SIGN
	TYPE III BARRICADE
	DRUMS WITH STEADY BURNING MONODIRECTIONAL LIGHTS 25' CENTERS
	SIGN PANEL/BARRICADE ASSEMBLY (INCLUDED IN THE COST FOR TRAFFIC CONTROL AND PROTECTION, LUMP SUM)

FILE NAME =	USER NAME = bemery	DESIGNED -	REVISED -
P:\Projects\2011 Projects\11297 - IDOT US 45 Ph2\CV\CADD Sheets\0978077-sht-Stage1A.dwg		DRAWN -	REVISED -
Default	PLOT SCALE = 400.0000' / in.	CHECKED -	REVISED -
	PLOT DATE = 4/30/2014	DATE -	REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**CONSTRUCTION STAGING PLAN
STAGE 1A**

SCALE: 1" = 200' SHEET OF SHEETS STA. 630+00.00 TO STA. 690+00.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
332	(29,30)R-1	SALINE	745	198
CONTRACT NO. 78077				
ILLINOIS FED. AID PROJECT				
