STAGE 3 GENERAL NOTES

STAGE 3 CONSTRUCTION


- 1. CONSTRUCT WESTBOUND LANE WIDENING (SUBGRADE AND BINDER COURSE) FROM STA. 290+10.10 TO STA. 294+67.90.
- 2. CONSTRUCT SHOULDER FROM STA. 288+89.85 LT. TO STA. 296+41.45 LT.
- 3. SHIFT LEFT DITCH TO FINAL LOCATION.
- 4. CONSTRUCT SURFACE COURSES ON ALL LANES FROM STA. 290+10.10 TO STA. 294+67.90.

STAGE 3 GENERAL NOTES

- 1. ALL TEMPORARY PAVEMENT MARKINGS PLACED IN STAGE 3 SHALL BE WET TEMPORARY PAVEMENT MARKING TAPE TYPE III
- 2. THE CONTRACTOR SHALL PROVIDE AND MAINTAIN ACCESS TO ALL PUBLIC AND PRIVATE ENTRANCES AND TO ALL SIDEROADS AT ALL TIMES.
- 3. THE CONTRACTOR SHALL PROVIDE ALL SIGNS, VERTICAL PANELS, TYPE II BARRICADES OR DRUMS, AND ALL OTHER TRAFFIC CONTROL DEVICES NECESSARY FOR THE MAINTENANCE OF TRAFFIC, OR AS DIRECTED BY THE ENGINEER.
- 4. ALL SIGNS SHOWN ON THE MAINTENANCE OF TRAFFIC PLANS SHALL BE INCLUDED IN THE CONTRACT LUMP SUM PRICE FOR TRAFFIC CONTROL AND PROTECTION (SPECIAL).

STAGE 3 TRAFFIC

- 1. SHIFT TRAFFIC TO STAGE 3 MAINTENANCE OF TRAFFIC AS SHOWN IN THE PLANS.
- 1. CLOSE LANES AS NECESSARY TO RESURFACE U.S. ROUTE 30 FROM STA. 290+10.10 TO STA. 294+67.90. USE IDOT TRAFFIC CONTROL STANDARD 701306.

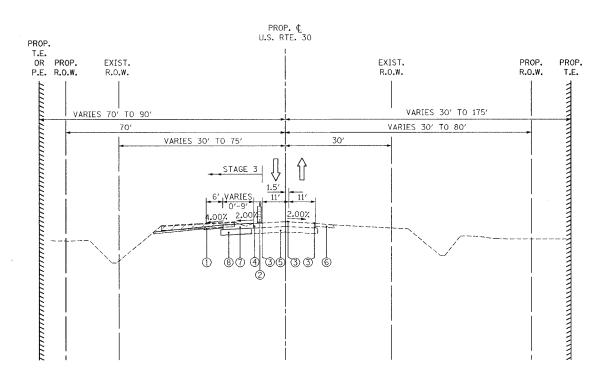

STAGE 3 TYPICAL SECTION

REMOVAL

- ① PROPOSED AGGREGATE SHOULDER, TYPE B, 6"
- ② BARRICADES OR DRUMS
- 3 PAVEMENT MARKING TAPE TYPE III, SPECIAL
- 4 CONSTRUCTED BITUMINOUS CONCRETE BINDER COURSE, SUPERPAVE, IL-19, N70, 11 $^{1}\!\!/_{2}$ "
- 5) CONSTRUCTED AGGREGATE SUBGRADE, 12"
- 6 CONSTRUCTED AGGREGATE SHOULDER, TYPE B, 6"
- \bigcirc BITUMINOUS BASE COURSE, WIDENING, SUPERPAVE, 11\(^1/_2\)''
- AGGREGATE SUBGRADE, 12"

REVISIONS	ILLINOIS DEPARTMENT OF TRANSPORTATION
NAME DATE	U.S. RTE. 30 OVER STREAM 0.3 MI. W. OF WOLF RD. SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL
	TYPICAL SECTIONS STA. 270+00 TO STA. 315+00
	SCALE : 1" = NTS DRAWN BY : BAE DATE : 06/17/05 CHECKED BY : GB
