


RTE.	SECTI	ON	COUNTY		SHEETS	NO.
336	99-00232-00-WR		KANE		97	24
STA. TO STA.						
FED. RO	AD DIST. NO.	ILLINOIS	FED.	AIĐ	PROJECT	

CONTRACT NO.: 83738

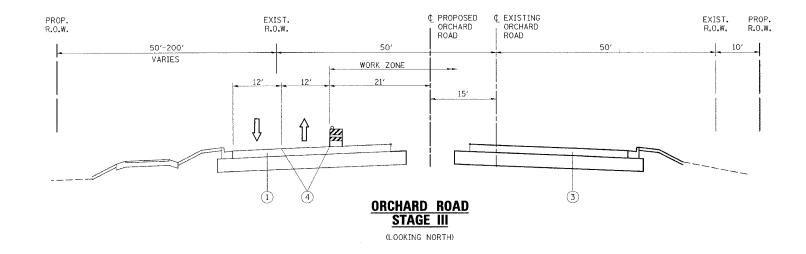



STAGE III (LOOKING EAST)



STAGE III (LOOKING EAST) STA. 305+08 TO STA. 311+30 PROJECT CONSTRUCTION STAGE III

TRAFFIC MAINTENANCE:

ORCHARD ROAD - TRAFFIC SHALL BE MAINTAINED ON THE NEW ORCHARD ROAD PAVEMENT BUILT IN STAGE II WITH ONE LANE OF TRAFFIC IN EACH DIRECTION. SOUTHBOUND LEFT TURN LANES SHALL BE PROVIDED AT JERICHO ROAD. TRAFFIC CONTROL SHALL BE INSTALLED AS DETAILED IN THESE PLANS.

JERICHO ROAD - MAINTAIN ONE LANE OF TRAFFIC IN EACH DIRECTION, TRAFFIC CONTROL SHALL BE INSTALLED AS DETAILED IN THESE PLANS.

CORNELL AVENUE - TRAFFIC SHALL BE MAINTAINED ON THE EXISTING AND TEMPORARY SIDE STREET PAVEMENT WITH ONE LANE OF TRAFFIC IN EACH DIRECTION, TRAFFIC CONTROL SHALL BE INSTALLED AS DETAILED IN THESE PLANS

THE FOLLOWING WORK ITEMS ARE TO BE COMPLETED DURING STAGE III:

- TRAFFIC CONTROL ITEMS, TEMPORARY PAVEMENT MARKING AND OTHER TRAFFIC CONTROL DEVICES SHALL BE INSTALLED TROUGHOUT THE CONSTRUCTION AREA PRIOR TO WORK COMMENCING.
- GRADING AND EMBANKMENT CONSTRUCTION SHALL BE COMPLETED FOR ORCHARD ROAD NORTHBOUND LANES.

- LANES.
  STORM SEWER LATERALS SHALL BE EXTENDED FOR ORCHARD ROAD NORTHBOUND LANES.
  CONSTRUCT ORCHARD ROAD NORTHBOUND PAVEMENT LANES AND OUTSIDE CURB AND GUTTER.
  CONSTRUCT ORCHARD ROAD NORTHBOUND PAVEMENT FROM STA. 165+00 TO 190+47 FIRST IN
  PREPARATION FOR SUBSEQUENT TEMPORARY LANE TRAFFIC CHANGES
  CONSTRUCT SOUTHERN PORTION OF SIDE STREETS CONCRETE PAVEMENT AS SHOWN IN THESE PLANS
  CONSTRUCT SOUTHEAST PORTION OF THE INTERSECTION OF ORCHARD ROAD AND JERICHO ROAD
  INSTALL PERMANENT TRAFFIC SIGNALS AND LIGHTING FOUNDATIONS ALONG NORTHBOUND PAVEMENTS
  COMPLETE FINAL RESTORATION OF EAST EMBANKMENT SLOPES

ALL TEMPORARY PAVEMENT MARKING, ON FINAL PAVEMENT SURFACES, SHALL BE PAVEMENT MARKING TAPE, TYPE III UNLESS NOTED OTHERWISE

SEE SHEET 33 FOR ADDITIONAL MAINTENANCE OF TRAFFIC NOTES.

## LEGEND

- 1 EXISTING PAVEMENT
- (2) TEMPORARY PAVEMENT, 10"
- (3) PROPOSED PAVEMENT
- 4 TEMPORARY PAVEMENT MARKING
- (5) TEMPORARY PAVEMENT RAMP

DATE **rjn**group Excellence through Ownership 200 West Front Street Wheaton, II 60187

ILLINOIS DEPARTMENT OF TRANSPORTATION KANE COUNTY DIVISION OF TRANSPORTATION ORCHARD ROAD RECONSTRUCTION MAINTENANCE OF TRAFFIC

TYPICAL SECTIONS AND NOTES STAGE III

SCALE: VERT. DATE: 11/04/05

DRAWN BY: RJN CHECKED BY: SPF
