


STAGE I
TYPICAL SECTION

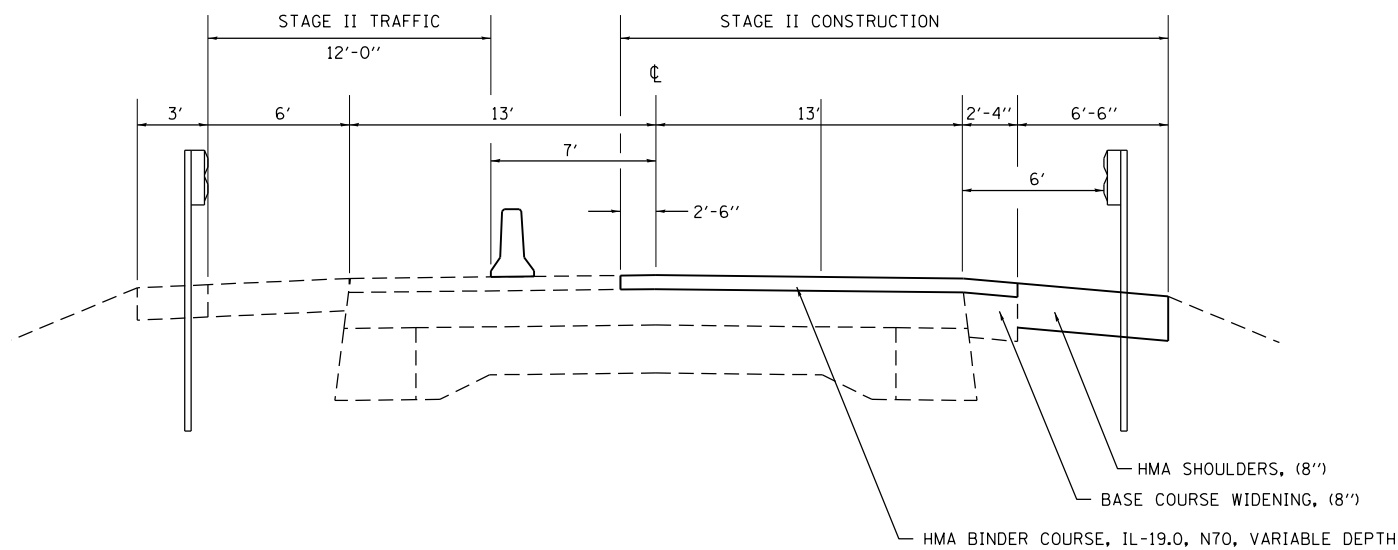

STAGE II
TYPICAL SECTION

BOX CULVERT REPLACEMENT

SUGGESTED SEQUENCE OF OPERATIONS

PRE-STAGE 1

- 1) CONSTRUCT BASE COURSE WIDENING FROM RT STA. 288+15 TO RT STA 292+08 TO PREPARE FOR STAGE 1 CONSTRUCTION/TRAFFIC CONTROL

STAGE 1

- 1) SETUP STAGE 1 TRAFFIC CONTROL
- 2) CONSTRUCT STAGE 1 BOX CULVERT AND WINGWALLS
- 3) CONSTRUCT HMA FULL-DEPTH PAVEMENT (EXCEPT SURFACE COURSE)
- 4) CONSTRUCT WIDENING FROM LT STA. 287+65 TO LT STA. 292+47 FOR STAGE 2 CONSTRUCTION/TRAFFIC CONTROL
- 5) CONSTRUCT SHOULDER
- 6) INSTALL GUARDRAIL FOR STAGE 2 TRAFFIC

STAGE 2

- 1) SETUP STAGE 2 TRAFFIC CONTROL
- 2) CONSTRUCT STAGE 2 BOX CULVERT AND WINGWALLS
- 3) CONSTRUCT HMA FULL-DEPTH PAVEMENT (EXCEPT SURFACE COURSE)
- 4) CONSTRUCT SHOULDER
- 5) INSTALL GUARDRAIL
- 6) CONSTRUCT HMA SURFACE COURSE ON BOTH STAGES

FILE NAME =	USER NAME = teasleyck	DESIGNED -	REVISED -
ct:\pwork\pwork\teasleyck\d0121473\0774156-sht-typicals.dgn		DRAWN -	REVISED -
	PLOT SCALE = 100.0000' / 1in.	CHECKED -	REVISED -
	PLOT DATE = 10/30/2012	DATE -	REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**BOX CULVERT REPLACEMENT
STAGE CONSTRUCTION TYPICAL SECTIONS**

SCALE: SHEET 1 OF 1 SHEETS STA. TO STA.

F.A. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
••	•	Macon, Platt	44	22
CONTRACT NO. 74156			ILLINOIS FED. AID PROJECT	

*(125,126,126R)RS-2&(126BR)B
**FAS 1536 & FAU 7464
