

SUGGESTED SEQUENCE OF CONSTRUCTION

PRE - STAGE I:

REMOVE EXISTING HMA SHOULDERS/HMA BASE COURSE (RIGHT) TO THE LIMITS DEFINED IN THE REMOVAL SCHEDULE.

CONSTRUCT ± 4'-7" HMA BASE CSE 9" IN THE SOUTHWEST AND SOUTHEAST QUADRANTS AS SHOWN ON THE PLANS. HMA BASE COURSE SHALL BE CONSTRUCTED WITHOUT DISTURBING THE EXISTING GUARDRAIL.

TRAFFIC CONTROL SHALL BE IN ACCORDANCE WITH TRAFFIC CONTROL AND PROTECTION, STANDARD 701326.

STAGE I:

PLACE STOP BARS AS SHOWN ON PLANS.

REMOVE CONFLICTING SKIP-DASH PAVEMENT MARKING BETWEEN STOP BARS.

PLACE 1037.5 FOOT TEMPORARY CONCRETE BARRIER AND IMPACT ATTENUATORS, TEMPORARY.

SEE STANDARD 701321 FOR DETAILS NOT SHOWN ON PLANS.

REMOVE EXISTING HMA SHOULDERS/HMA BASE COURSE (LEFT) TO THE LIMITS DEFINED IN THE REMOVAL SCHEDULE.

CONSTRUCT ± 4-1" HMA BASE CSE 9" IN THE NORTHWEST AND NORTHEAST QUADRANTS AS SHOWN ON PLANS. HMA BASE COURSE SHALL BE CONSTRUCTED WITHOUT DISTURBING THE EXISTING GUARDRAIL.

PERFORM ALL STRUCTURAL WORK FOR STAGE I. SEE STRUCTURE PLANS.

PERFORM ANY ADDITIONAL NECESSARY WORK FOR STAGE I CONSTRUCTION.

STAGE II:

RELOCATE 1037.5 FT TEMPORARY CONCRETE BARRIER AND IMPACT ATTENUATORS, TEMPORARY. PLACE IMPACT ATTENUATOR, TEMPORARY.

SEE STANDARD 701321 FOR DETAILS NOT SHOWN ON PLANS.


PERFORM ALL STRUCTURAL WORK FOR STAGE II. SEE STRUCTURE PLANS.

PERFORM ANY ADDITIONAL NECESSARY WORK FOR STAGE II CONSTRUCTION.



POST - STAGE II:

APPLY PAVEMENT MARKINGS UTILIZING TRAFFIC CONTROL AND PROTECTION, STANDARD 701311.

PERFORM ANY ADDITIONAL WORK REQUIRED.



SAND MODULE IMPACT ATTENUATOR LAYOUT
(IF OPTION USED)

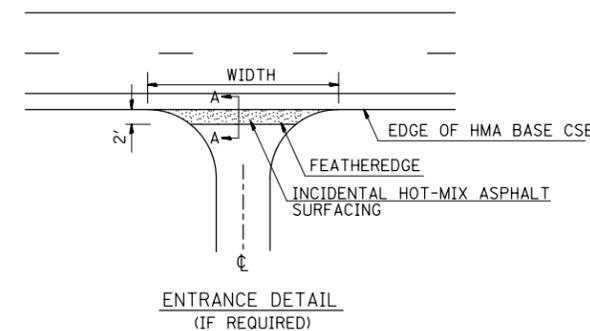

FILE NAME =	USER NAME = tharpr1	DESIGNED -	REVISED -
ct:\pw_work\p1dot\tharpr1\d0297154\08768	75-shit-staging1.dgn	DRAWN -	REVISED -
	PLOT SCALE = 48.0000' / in.	CHECKED -	REVISED -
	PLOT DATE = 12/10/2012	DATE -	REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

STAGE CONSTRUCTION DETAILS /ENTRANCE DETAILS

SCALE: N/A SHEET NO. 1 OF 1 SHEETS STA. TO STA.

F.A.P RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
817	421BR-1	ST. CLAIR	43	9
CONTRACT NO. 76F75			ILLINOIS FED. AID PROJECT	
