
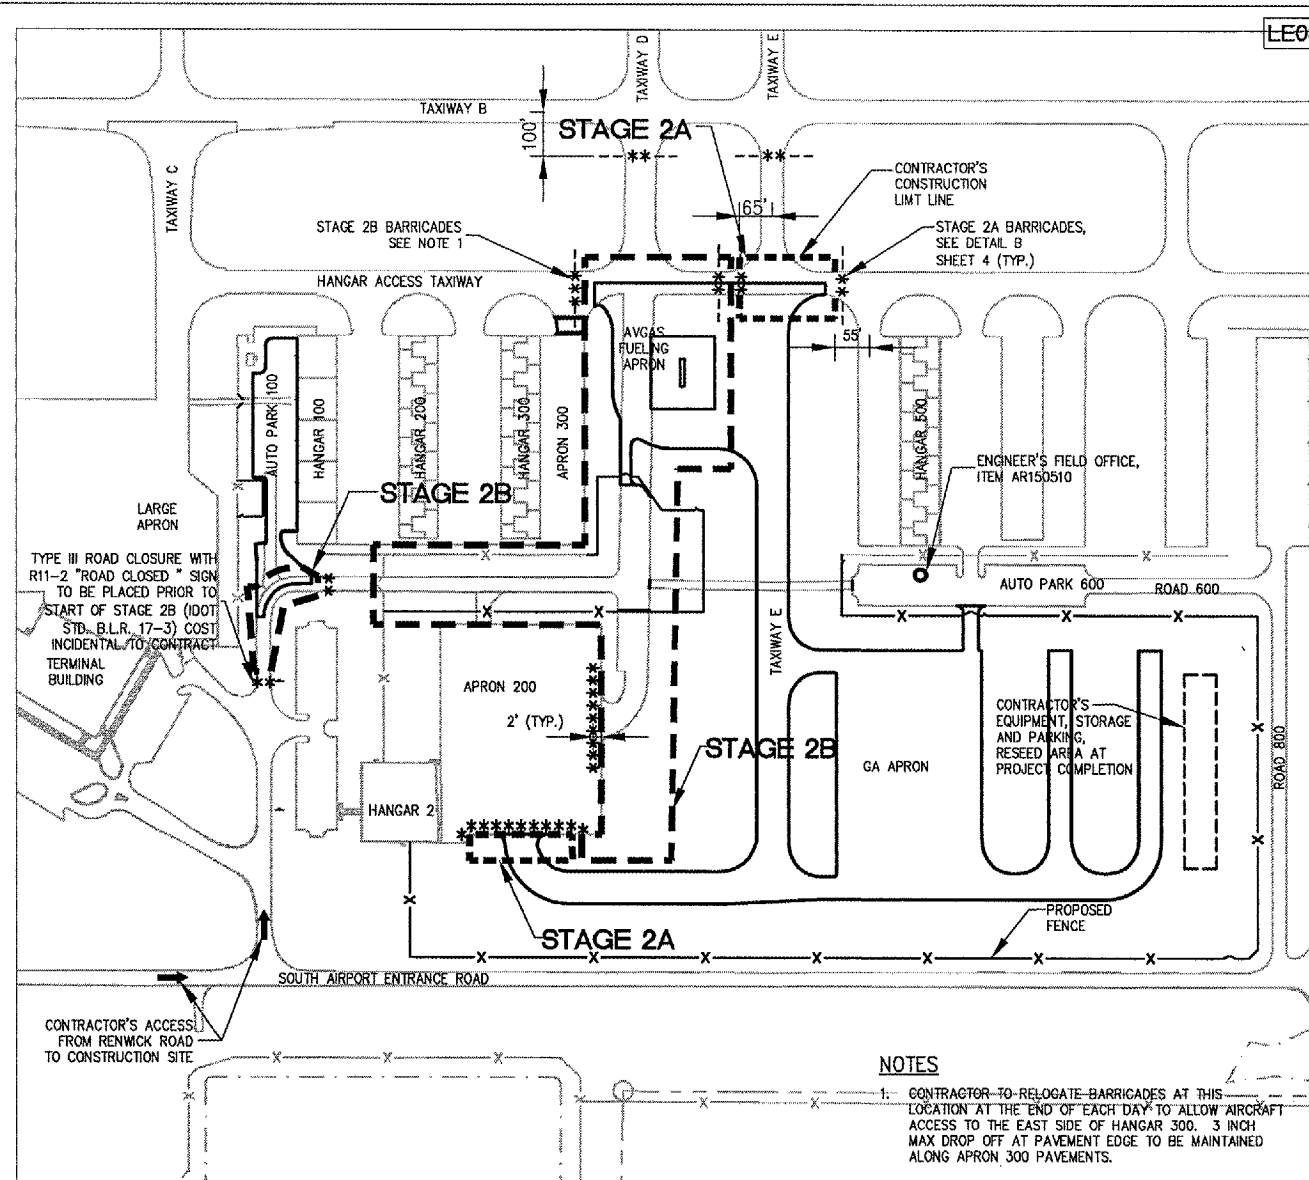


STAGE 1

- NOTES:**
- ALL CONTRACTOR'S ACTIVITIES SHALL BE LIMITED TO AREA WITHIN THE STAGE 1 LIMITS AS SHOWN.
 - ALL CONSTRUCTION EQUIPMENT WILL BE LIMITED TO A HEIGHT OF 30 FEET UNLESS PRIOR APPROVAL GIVEN BY THE ENGINEER.
 - SEE CONSTRUCTION AND SAFETY NOTES, SHEET 4.
- THE FOLLOWING ITEMS ARE TO BE COMPLETED IN STAGE 1:**
- PROVIDE TEMPORARY BARRICADES AS SHOWN.
 - PROVIDE LATHING AND WARNING TAPE AS SHOWN.
 - PROVIDE ENGINEER'S FIELD OFFICE AND CONTRACTOR'S EQUIPMENT, STORAGE AND PARKING AREA.
 - INSTALL TEMPORARY SOIL EROSION CONTROL MEASURES AS REQUIRED.
 - COMPLETE EARTHWORK AND INSTALL STORM SEWER PIPE, DRAINAGE STRUCTURES AND CONCRETE ENCASED DUCT WITHIN STAGE 1 LIMITS.
 - PREPARE SUBGRADE WITHIN STAGE 1 LIMITS.
 - PLACE CRUSHED AGGREGATE BASE WITHIN STAGE 1 LIMITS.
 - INSTALL UNDERDRAINS WITHIN STAGE 1 LIMITS.
 - PLACE P.C.C. PAVEMENT, TIE DOWNS, GROUND RODS.
 - CONSTRUCT BITUMINOUS PAVEMENT WITHIN STAGE 1 LIMITS.
 - PLACE PROPOSED PAVEMENT MARKINGS WITHIN STAGE 1 LIMITS.
 - INSTALL HIGH-MAST LIGHTING POLES AND ASSOCIATED ELECTRICAL WITHIN STAGE 1 LIMITS.
 - INSTALL FENCING AND ELECTRIC GATES WITHIN STAGE 1 LIMITS - ADDITIVE NO. 1.
 - REGRADE SHOULDERS AND SWALES WHERE NECESSARY WITHIN STAGE 1 LIMITS.
 - TOPSOIL AND SEED WITHIN STAGE 1 LIMITS.
 - REMOVE LATHING AND WARNING TAPE, BARRICADES AND TEMPORARY EROSION CONTROL MEASURES AS NECESSARY WITHIN STAGE 1 LIMITS.



STAGE 2A

- NOTES (STAGE 2A & 2B):**
- NEITHER STAGE 2A OR 2B MAY BEGIN BEFORE JULY 1, 2005.**
- STAGE 2A MUST BE COMPLETED WITHIN 3 CALENDAR DAYS.
- ALL CONTRACTOR'S ACTIVITIES SHALL BE LIMITED TO AREA WITHIN THE STAGE 2A LIMITS AS SHOWN.**
- ALL CONSTRUCTION EQUIPMENT WILL BE LIMITED TO A HEIGHT OF 30 FEET UNLESS PRIOR APPROVAL GIVEN BY THE ENGINEER.
 - SEE CONSTRUCTION AND SAFETY NOTES, SHEET 4.
- THE FOLLOWING ITEMS ARE TO BE COMPLETED IN STAGE 2A:**
- PROVIDE TEMPORARY BARRICADES AS SHOWN.
 - PROVIDE LATHING AND WARNING TAPE AS SHOWN.
 - INSTALL TEMPORARY SOIL EROSION CONTROL MEASURES AS REQUIRED.
 - COMPLETE EARTHWORK WITHIN STAGE 2A LIMITS.
 - PREPARE SUBGRADE WITHIN STAGE 2A LIMITS.
 - PLACE CRUSHED AGGREGATE BASE WITHIN STAGE 2A LIMITS.
 - INSTALL UNDERDRAINS WITHIN STAGE 2A LIMITS.
 - CONSTRUCT BITUMINOUS PAVEMENT WITHIN STAGE 2A LIMITS.
 - REGRADE SHOULDERS AND SWALES WHERE NECESSARY WITHIN STAGE 2A LIMITS.
 - PLACE TOPSOIL WITHIN STAGE 2A LIMITS.

STAGE 2B

- THE FOLLOWING ITEMS ARE TO BE COMPLETED IN STAGE 2B:**
- PROVIDE TEMPORARY BARRICADES AS SHOWN.
 - PROVIDE LATHING AND WARNING TAPE AS SHOWN.
 - INSTALL TEMPORARY SOIL EROSION CONTROL MEASURES AS REQUIRED.
 - COMPLETE EARTHWORK AND INSTALL STORM SEWER PIPE, DRAINAGE STRUCTURES AND CONCRETE ENCASED DUCT WITHIN STAGE 2B LIMITS.
 - PREPARE SUBGRADE WITHIN STAGE 2B LIMITS.
 - PLACE CRUSHED AGGREGATE BASE WITHIN STAGE 2B LIMITS.
 - INSTALL UNDERDRAINS WITHIN STAGE 2B LIMITS.
 - PLACE P.C.C. PAVEMENT, TIE DOWNS, GROUND RODS.
 - CONSTRUCT BITUMINOUS PAVEMENT WITHIN STAGE 2B LIMITS.
 - INSTALL HIGH-MAST LIGHTING POLES AND ASSOCIATED ELECTRICAL WITHIN STAGE 2B LIMITS.
 - INSTALL FENCING WITHIN STAGE 2B LIMITS.
 - REGRADE SHOULDERS AND SWALES WHERE NECESSARY WITHIN STAGE 2B LIMITS.
 - PLACE TOPSOIL WITHIN STAGE 2B LIMITS.
 - ALL SEEDING WITHIN STAGE 2A AND 2B LIMITS
 - PLACE PAVEMENT MARKINGS WITHIN STAGE 2A AND 2B LIMITS.
 - CLEAN UP ANY REMAINING MATERIALS AND DEBRIS AND SWEEP PAVEMENT PRIOR TO REOPENING.
 - REMOVE LATHING AND WARNING TAPE AND TEMPORARY BARRICADES.
 - REMOVE TEMPORARY SOIL EROSION CONTROL MEASURES ONCE A STAND OF GRASS HAS DEVELOPED.

NOTES

1. CONTRACTOR TO RELOCATE BARRICADES AT THIS LOCATION AT THE END OF EACH DAY TO ALLOW AIRCRAFT ACCESS TO THE EAST SIDE OF HANGAR 300. 3 INCH MAX DROP OFF AT PAVEMENT EDGE TO BE MAINTAINED ALONG APRON 300 PAVEMENTS.

LE035



HANSON PROFESSIONAL SERVICES INC.
 815 Commerce Drive, Suite 200
 Oak Brook, Illinois 60523
 Telephone: 630.990.3800
 Fax: 630.990.3801



JOLIET REGIONAL PORT DISTRICT
 1 Hangar Road
 Romeoville, Illinois 60446
 Telephone: 815.838.9497
 Fax: 815.838.9524

EXTEND TAXIWAY E: CONSTRUCT GA APRON, AVGAS FUELING APRON AND AUTO PARK 100

**AIP PROJECT NO. 3-17-0140-B38
 IDA PROJECT NO. LOT-3441**

No.	Drawing Issue Description	Date	By

Date
 MARCH 25, 2005
 Sheet Title

CONSTRUCTION STAGING PLAN

840-04D8041
 Project Number
 LDH 03/11/05
 Layout By Date
 LDH/TMM 03/11/05
 Designed By Date
 RMH 03/15/05
 Reviewed By Date
 LDH TMM ---
 Drawn By Sheet No.

I:\04\085\00040\0408041\DRAWINGS\SHEETS\05-STAGING PLAN\DWG MAR 28, 2005 12:11PM TMM
