


INTENDED SEQUENCE

1. PLACEMENT OF PERIMETER EROSION BARRIER PRIOR TO COMMENCEMENT OF ANY WORK. SEE STANDARD 280001.
2. PLACEMENT OF INLET AND PIPE PROTECTION ON EXISTING CULVERTS PRIOR TO COMMENCEMENT OF WORK. PLACEMENT OF INLET AND PIPE PROTECTION AFTER CONSTRUCTION OF PROPOSED STRUCTURES. SEE STANDARD 280001.
3. PLACEMENT OF TEMPORARY SEEDING ON GRADED SURFACES NOT HAVING PERMANENT SEEDING APPLIED.
4. PLACEMENT OF TEMPORARY DITCH CHECKS AFTER DITCH GRADING IS COMPLETE. SEE STANDARD 280001.
5. PLACEMENT OF EROSION CONTROL BLANKET AFTER FINAL GRADING AROUND CULVERTS.
6. ONGOING MAINTENANCE OF EROSION CONTROL ELEMENTS PER THE SWPPP.
7. REMOVE TEMPORARY EROSION CONTROL ELEMENTS AFTER FINAL GRADING AND PERMANENT SEEDING ESTABLISHED AS PER THE SWPPP AND APPROVED BY THE ENGINEER.

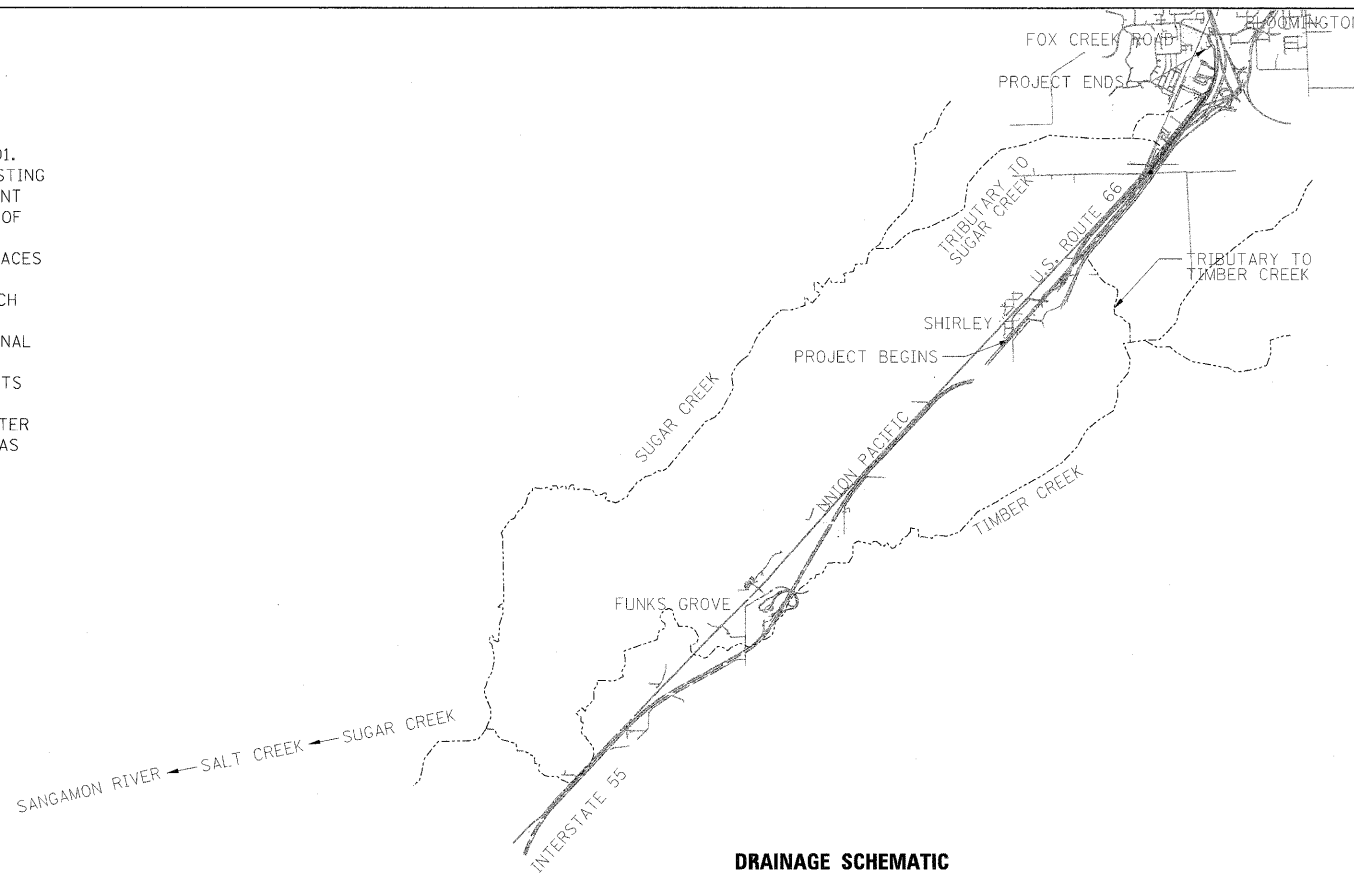

DRAINAGE SCHEMATIC

- NOTES**
1. MAJOR GRADING SLOPES ALONG THE PROPOSED BIKEWAY ARE 3:1 MAX
 2. SOILS DISTURBANCE SHALL ONLY OCCUR WITHIN THE AREAS SHOWN
 3. RECEIVING WATER FOR DRAINAGE FROM PROJECT IS SUGAR CREEK. SUGAR CREEK IS A TRIBUTARY OF SALT CREEK, WHICH FLOWS TO THE SANGAMON RIVER.
 4. NO WETLANDS HAVE BEEN IDENTIFIED IN THE PROJECT AREA

FILE NAME = I:\01jobs\0152024\CAOD\Road\Sheet\0-718.Eros.dgn	USER NAME = Pop00275	DESIGNED - heyen	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	TEMPORARY EROSION CONTROL PLAN	F.A. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.	
		DRAWN - pop00275	REVISED -				01-00001-01-BT	MCLEAN	50	30	
		CHECKED - heyen	REVISED -			SCALE: SEE SHEET	SHEET NO. 4 OF 4 SHEETS	STA. 731+00.00 TO STA. 751+85.16	CONTRACT NO. 91429		
		DATE - 11/03/2009	REVISED -			ILLINOIS FED. AID PROJECT					
