


CONTRACT 62695

ID	Task Name	Duration	Start	Finish	Qtr 3, 2005			Qtr 4, 2005			Qtr 1, 2006			Qtr 2, 2006			Qtr 3, 2006	
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
89	PUBLIC NOTIFICATION (2 weeks)	0 days	Mon 4/17/06	Mon 4/17/06														
90	CLOSE RAMP @ 95th Ex.	0 days	Mon 5/1/06	Mon 5/1/06														
91	rem. / relocate temp conc barrier (2 crews)	2 days	Mon 5/1/06	Tue 5/2/06														
92	temp. pavement markings	1 day	Wed 5/3/06	Wed 5/3/06														
93	c & g removal (2 crews)	2 days	Thu 5/4/06	Fri 5/5/06														
94	pavement removal (2 crews)	2 days	Thu 5/4/06	Fri 5/5/06														
95	paved shoulder removal	1 day	Thu 5/4/06	Thu 5/4/06														
96	drill & set piles (partial wall 34, 35) (2 crews)	8 days	Mon 5/8/06	Wed 5/17/06														
97	timber lagging	7 days	Fri 5/12/06	Mon 5/22/06														
98	structure excavation	2 days	Fri 5/12/06	Mon 5/15/06														
99	reinf. bars epoxy coated (2 crews)	4 days	Thu 5/18/06	Tue 5/23/06														
100	concrete structures (2 crews)	3 days	Mon 5/22/06	Wed 5/24/06														
101	earth excavation	6 days	Thu 5/25/06	Thu 6/1/06														
102	storm sewer 36" to 48"	3 days	Fri 5/26/06	Tue 5/30/06														
103	storm sewer 12" to 30" (3 crews)	6 days	Fri 5/26/06	Fri 6/2/06														
104	manholes	4 days	Fri 5/26/06	Wed 5/31/06														
105	catch basins (2 crews)	5 days	Fri 5/26/06	Thu 6/1/06														
106	CTA NOTIFICATION FOR SINGLE TRACKING (42 days)	42 days	Thu 4/6/06	Fri 6/2/06														
107	ovrhd./cant. sign foundations	5 days	Mon 6/5/06	Fri 6/9/06														
108	ovrhd./cant. sign structure (2 crews)	5 days	Mon 6/12/06	Fri 6/16/06														
109	sign panels	2 days	Mon 6/19/06	Tue 6/20/06														
110	subbase gran. mat. 24"	3 days	Mon 6/5/06	Wed 6/7/06														
111	stabilized subbase 4"	1 day	Thu 6/8/06	Thu 6/8/06														
112	pcc pvmt. 11" (jointed)	4 days	Fri 6/9/06	Wed 6/14/06														
113	pcc shoulders 11"	4 days	Thu 6/15/06	Tue 6/20/06														
114	temporary pavement	2 days	Thu 6/15/06	Fri 6/16/06														
115	conc. curb & gutter	3 days	Wed 6/21/06	Fri 6/23/06														
116	pavement markings	1 day	Mon 6/26/06	Mon 6/26/06														
117	topsoil furnish & place	1 day	Tue 6/27/06	Tue 6/27/06														
118	seeding class 2A	1 day	Wed 6/28/06	Wed 6/28/06														
119	erosion control blanket (2 crews)	2 days	Thu 6/29/06	Fri 6/30/06														
120	OPEN RAMP @ 95th Ex.	0 days	Fri 6/30/06	Fri 6/30/06														
121																		
122	PUBLIC NOTIFICATION (2 weeks)	0 days	Sat 6/17/06	Sat 6/17/06														
123	CLOSE RAMP @ Halsted Ex.	0 days	Sat 7/1/06	Sat 7/1/06														
124	rem. / relocate temp conc barrier (2 crews)	1 day	Mon 7/3/06	Mon 7/3/06														
125	temp. pavement markings	1 day	Tue 7/4/06	Tue 7/4/06														
126	curb & gutter removal	2 days	Wed 7/5/06	Thu 7/6/06														
127	pavement removal	2 days	Wed 7/5/06	Thu 7/6/06														
128	paved shoulder removal	1 day	Wed 7/5/06	Wed 7/5/06														
129	earth excavation	1 day	Fri 7/7/06	Fri 7/7/06														
130	storm sewer 12" to 30" (2 crews)	3 days	Mon 7/10/06	Wed 7/12/06														
131	manholes	1 day	Mon 7/10/06	Mon 7/10/06														
132	catch basins (2 crews)	2 days	Mon 7/10/06	Tue 7/11/06														

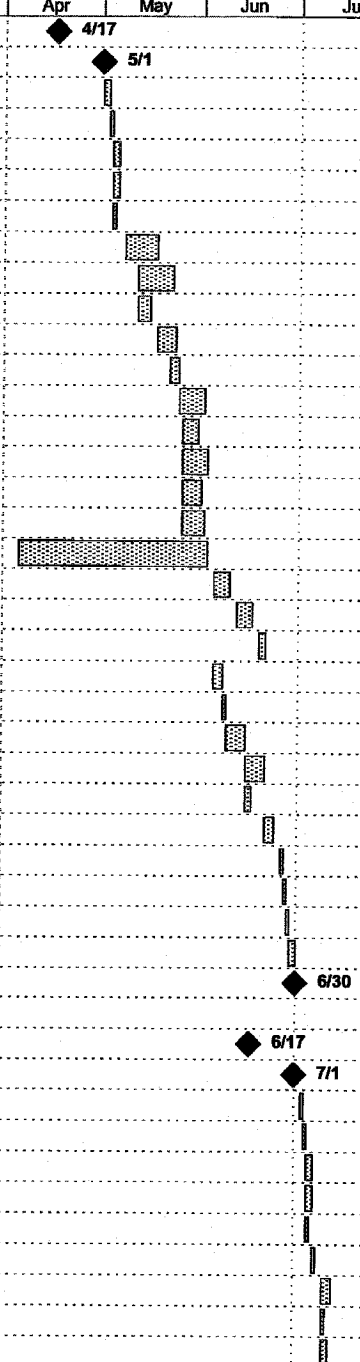

Project: 17B Construction Schedule
Date: Tue 3/29/05

Task: [Pattern] Progress
 Split: [Pattern] Milestone
 Summary: [Pattern] Summary
 External Tasks: [Pattern] External Tasks
 Project Summary: [Pattern] Project Summary
 External Milestone: [Pattern] External Milestone
 Deadline: [Pattern] Deadline

FOR INFORMATION ONLY

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 94 (DAN RYAN EXPRESSWAY)

SUGGESTED CONSTRUCTION SEQUENCE
CONTRACT #62695 (17B)
SHEET 3 OF 4

SCALE: NONE DRAWN BY: JPA
DATE: APRIL 15, 2005 CHECKED BY: MAG

P:\02373\road\17B\17B33.dgn 4/14/2005 7:52:26 AM
