

ROAD CLOSED SIGNING LOCATIONS - ASH GROVE DRIVE


SUGGESTED CONSTRUCTION SEQUENCE

WORK DONE UNDER ROAD CLOSURE (ASH GROVE DRIVE)

- 1.) THE CONTRACTOR SHALL PLACE ROAD CLOSED SIGNS IN ACCORDANCE WITH THIS SHEET AND STANDARD BLR 21.
 2.) REMOVE EXISTING PAVEMENT FROM STA. 17+25 TO STA. 17+63.
 3.) REMOVE EXISTING CURB AND GUTTER AND SIDEWALK STA. 17+25 TO STA. 18+05 LT. & RT. & STA. 17+95 LT. & RT..
 4.) INSTALL PRECAST CONCRETE BOX CULVERT AND EMBANKMENT STA. 17+43.86
- 4.) INSTALL PRECAST CONCRETE BOX CULVERT AND EMBANKMENT STA. 17+43.86.
 5.) INSTALL CLASS D PATCH 10" & GRANULAR CULVERT BACKFILL STA. 17+25 TO STA 17+63.
 6.) INSTALL COMBINATION CURB AND GUTTER STA. 17+25 TO STA. 18+05.
 7) THE CONTRACTOR SHALL OPEN THE ROAD TO TRAFFIC AND COMPLETE REMAINING WORK UNDER FLAGGERS.

WORK DONE UNDER FLAGGERS (ASH GROVE DRIVE)

- 1.) FINISH INSTALLING ANY REMAINING PRECAST CONCRETE BOX CULVERT.
 2.) CONSTRUCT CAST IN PLACE CONCRETE END SECTIONS AND PIPE HANDRAIL
- 3.) INSTALL NEW P.C.C. DRIVEWAY PAVEMENT 8" STA. 17+83 LT. AND NEW P.C.C. SIDEWALK STA. 17+25 TO STA. 18+05 LT. & RT.
 3.) SHAPE AND GRADE EARTH FOR SHOULDERS AND ENTRANCES STA. 17+25 TO
- 4.) FINAL STRIPING, SEEDING AND MISCELLANEOUS CLEANUP.

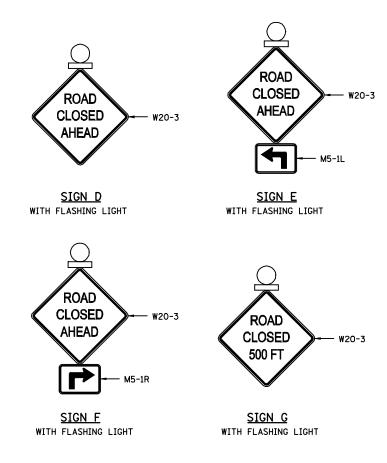

| FILE NAME = | USER NAME = laughlinrl | DESIGNED - | REVISED - |
|---|------------------------------------|------------|-----------|
| c:\pw_work\PWIDOT\LAUGHLINRL\dØ1435Ø7\D | 672AØ2-SHT-TCP.dgn | DRAWN - | REVISED - |
| | PLOT SCALE = 2.00000 '/ IN. | CHECKED - | REVISED - |
| | PLOT DATE = May-18-2009 03:19:28PM | DATE - | REVISED - |
| | | | |



| Allen | Henderson | & | Associates, Inc. | | | |
|---|----------------|------|--------------------|--|--|--|
| Civil and Structural Engineers Springfield, IL. | | | | | | |
| 62703 | Phone: (217)54 | 4-80 | 33 IL. Design Firm | | | |
| No. 184-001907 | | | | | | |

| TRAFFIC CONTROL PLAN | | | F.A.U. RTE. | F.A.U. SECTION | | COUNTY | TOTAL SHEETS | SHEET NO. | | |
|----------------------|--------|----------------------------|----------------|----------------|---------|---|-----------------|--------------|-------|-------|
| | | | 8012 | 21(I-3) | | SANGAMON | 147 | 56 | | |
| L | | | | | | | | CONTRACT | NO. 7 | '2A02 |
| L | SCALE: | SHEET NO. 147 OF 56 SHEETS | STA. | TO STA. | FED. RO | FED. ROAD DIST. NO. ILLINOIS FED. AID PROJECT | | | | |
