


NOTES

1. USE EXISTING EXIT 101 SIGNS WHILE THE EASTBOUND I-74 LANES ARE RECONSTRUCTED.
2. USE CHANGEABLE MESSAGE SIGN ① IN PLACE OF EXIT 101 SIGNS WHILE THE WESTBOUND I-74 LANES ARE RECONSTRUCTED.
3. WESTBOUND I-74 TRAFFIC WILL BE USING THE 4-LANE TEMPORARY RUNAROUND OR EASTBOUND I-74 LANES DURING SOME CONSTRUCTION STAGES.
4. THE LOCATIONS OF TEMPORARY INFORMATION SIGNING WILL VARY ACCORDING TO CONSTRUCTION STAGE. SEE TEMPORARY SIGNING PLANS FOR EACH STAGE.
5. RAMP G CLOSURE SHALL BE CONCURRENT WITH RAMP H CLOSURE THROUGHOUT STAGES 5-12.
6. RAMP G SHALL NOT BE CLOSED UNTIL THE FOLLOWING WORK IS COMPLETED.
 - a) COMPLETION OF EB AND WB I-74 FROM JEFFERSON STREET TO MORTON AVENUE INTERCHANGE AND FROM I-474 TO I-155
 - b) COMPLETION OF I-155 RAMP E TO EB I-74
 - c) COMPLETION OF RAMP F EXIT TO MORTON AVENUE
 - d) TEMPORARY WIDENING OF MORTON AVENUE RAMP E ENTRANCE TO WB I-74 TO 2 LANES
 - e) TEMPORARY RECONFIGURATION OF MORTON AVENUE TO ISOLATE RAMP H DETOUR TRAFFIC AND PROVIDE DUAL LEFT TURNS FROM NB MORTON AVENUE TO RAMP E ENTRANCE TO WB I-74
 - f) COMPLETION OF MORTON AVENUE RAMP B APPROACH WIDENING
 - g) CONSTRUCTION OF TEMPORARY EASTBOUND I-74 PAVEMENT

**DETOUR ROUTE FOR RAMP G CLOSURE
STAGE 5 THROUGH 12
DETOUR LENGTH = 7.0 MILES**

LEGEND

- LOCAL ROAD
- DETOUR ROUTE
- ▨ ROADWAY CLOSURE
- TCP• SIGN INCLUDED IN TRAFFIC CONTROL & PROTECTION (SEE SIGN SCHEDULE)
- XX-X SIGN REFERENCE NUMBER (SEE SIGN SCHEDULE)

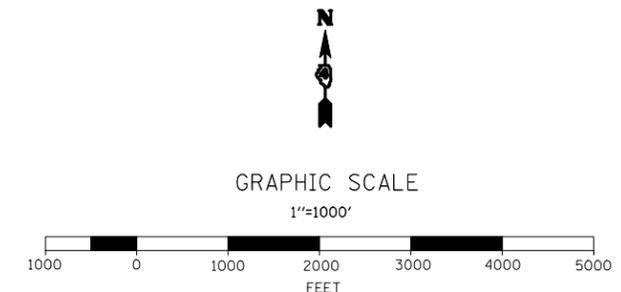

FILE NAME = D468620-Detour_RampG-dtl.dgn	DESIGNED - DA	REVISED -		STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	MAINTENANCE OF TRAFFIC RAMP G DETOUR PLAN	F.A.I. RTE. = 90-[14R(14HB-4,14,14HB)/BR]	SECTION = TAZEWELL	COUNTY =	TOTAL SHEETS = 2433	SHEET NO. = 838
USER NAME = TERRA	CHECKED - HTL/LVA	REVISED -				SCALE: SHEET NO. 26 OF 27 SHEETS STA. TO STA.	CONTRACT NO. 68620			
PLOT DATE = 7/16/2012	DATE = 7/20/2012	REVISED -				ILLINOIS FED. AID PROJECT				
