


NOTE:

1. THE MAINTENANCE OF TRAFFIC EROSION AND SEDIMENT CONTROL PLANS INCLUDE INLET AND PIPE PROTECTION, PERIMETER EROSION BARRIER, TEMPORARY DITCH CHECKS, EROSION CONTROL BLANKET, AND TEMPORARY EROSION CONTROL SEEDING TO BE IMPLEMENTED AS STABILIZATION PRACTICES TO PROVIDE PROTECTION FROM EROSION AND CONTROL OF SEDIMENT IN AREAS OF DISTURBANCE DUE TO CONSTRUCTION OF TEMPORARY RAMP F WHICH IS BEING CONSTRUCTED IN STAGE 2A OF THE MAINTENANCE OF TRAFFIC PLANS. SEE MAINTENANCE OF TRAFFIC - STAGE 2A FOR ADDITIONAL INFORMATION.
2. TEMPORARY EROSION CONTROL SEEDING HAS BEEN CALCULATED BY ESTIMATING THREE APPLICATIONS OVER THE ENTIRE PROJECT LIMITS. SEE SEEDING SCHEDULE FOR TEMPORARY EROSION CONTROL SEEDING QUANTITY AND BDE 2342, THE STORM WATER POLLUTION PREVENTION PLAN IN THE PROJECT SPECIFICATIONS, FOR STABILIZATION PRACTICES.

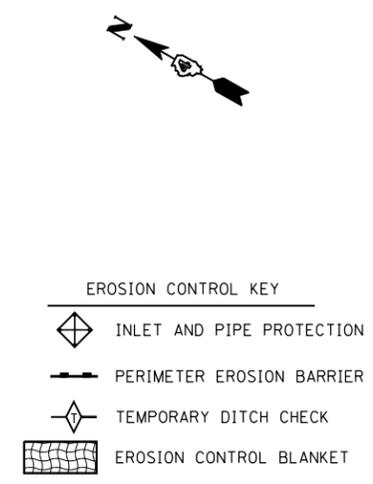

TEMP. DITCH CHECK SPACING		
SLOPE %	HEIGHT AT CENTER OF DITCH CHECK (OVERFLOW PT) (INCHES)	SPACING OF DITCH CHECK (FEET)
8.0	12"	13
	18"	20
	24"	26
7.0	12"	14
	18"	21
	24"	28
6.0	12"	17
	18"	26
	24"	34
5.0	12"	20
	18"	30
	24"	40
4.0	12"	25
	18"	38
	24"	50
3.0	12"	33
	18"	50
	24"	66
2.0	12"	50
	18"	75
	24"	100
1.0 & UNDER	12"	100
	18"	150
	24"	200
