

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
336	99-00232-00-WR	KANE	97	20
STA.	TO STA.			
FED. ROAD DIST. NO.	ILLINOIS FED. AID PROJECT		CONTRACT NO.: 83738	

PROJECT CONSTRUCTION STAGE II

TRAFFIC MAINTENANCE:

ORCHARD ROAD - TRAFFIC SHALL BE MAINTAINED ON THE EXISTING ORCHARD ROAD PAVEMENT WITH ONE LANE OF TRAFFIC IN EACH DIRECTION. SOUTHBOUND LEFT TURN LANES SHALL BE PROVIDED AT JERICO ROAD. TRAFFIC CONTROL SHALL BE INSTALLED AS DETAILED IN THESE PLANS.

JERICO ROAD - TEMPORARY PAVEMENT WILL BE CONSTRUCTED ALONG THE NORTH SIDE OF JERICO ROAD TO MAINTAIN ONE LANE OF TRAFFIC IN EACH DIRECTION. TRAFFIC CONTROL SHALL BE INSTALLED AS DETAILED IN THESE PLANS.

CORNELL AVENUE - TRAFFIC SHALL BE MAINTAINED ON THE EXISTING SIDE STREET PAVEMENT.


THE FOLLOWING WORK ITEMS ARE TO BE COMPLETED DURING STAGE II:

- TRAFFIC CONTROL ITEMS, TEMPORARY PAVEMENT MARKING AND OTHER TRAFFIC CONTROL DEVICES SHALL BE INSTALLED THROUGHOUT THE CONSTRUCTION AREA PRIOR TO WORK COMMENCING.
- GRADING AND EMBANKMENT CONSTRUCTION SHALL BE COMPLETED FOR THE ORCHARD ROAD, SOUTHBOUND LANES.
- CONSTRUCT STORM SEWER LATERALS AND TRUNK LINE SEWER FOR ORCHARD ROAD, SOUTHBOUND LANES.
- CONSTRUCT ORCHARD ROAD SOUTHBOUND PAVEMENT LANES AND OUTSIDE CURB AND GUTTER.
- CONSTRUCT PATH ALONG WEST SIDE OF ORCHARD ROAD, SOUTHBOUND LANES SOUTH OF JERICO ROAD.
- CONSTRUCT SOUTHWEST PORTION OF THE INTERSECTION OF ORCHARD ROAD AND JERICO ROAD
- INSTALL PERMANENT TRAFFIC SIGNALS AND STREET LIGHTING FOUNDATIONS ALONG SOUTHBOUND PAVEMENTS
- COMPLETE FINAL RESTORATION OF WEST EMBANKMENT SLOPES
- CONSTRUCT TEMPORARY PAVEMENT FOR ORCHARD ROAD TRANSITION STA 162+66.85 TO STA 171+62.62


ALL TEMPORARY PAVEMENT MARKING, ON FINAL PAVEMENT SURFACES, SHALL BE PAVEMENT MARKING TAPE, TYPE III UNLESS NOTED OTHERWISE

SEE SHEET 33 FOR ADDITIONAL MAINTENANCE OF TRAFFIC NOTES


SEE SHEET 44 FOR STAGE CONSTRUCTION JOINTS

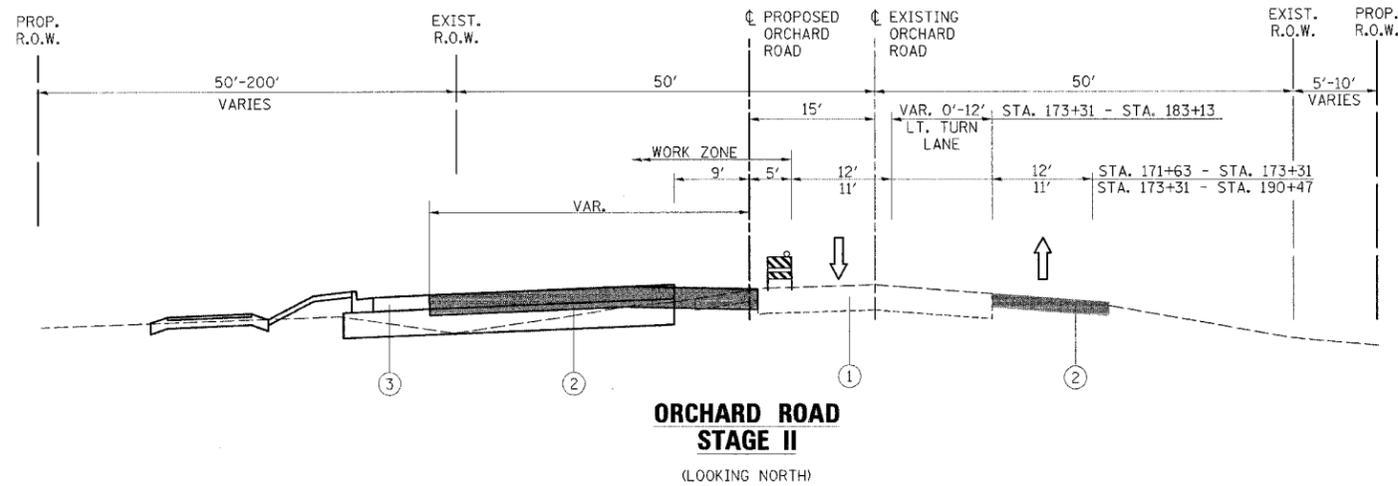

**ORCHARD ROAD
STAGE II**
(LOOKING NORTH)

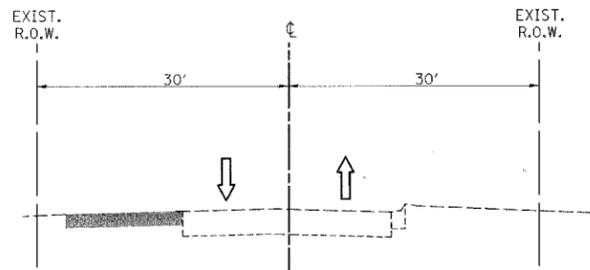

**CORNELL AVENUE
STAGE II**
(LOOKING EAST)

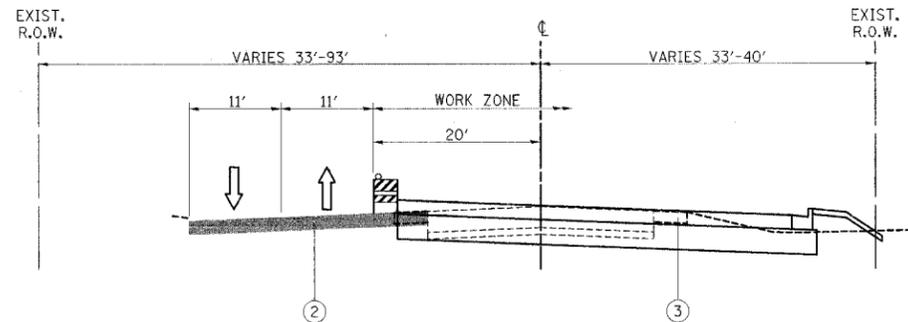

**JERICO ROAD
STAGE II**
(LOOKING EAST)
STA. 305+08 TO STA. 311+30

LEGEND

- ① EXISTING PAVEMENT
- ② TEMPORARY PAVEMENT, 10"
- ③ PROPOSED PAVEMENT
- ④ TEMPORARY PAVEMENT MARKING
- ⑤ TEMPORARY PAVEMENT RAMP

rjngroup
Excellence through Ownership
200 West Front Street
Wheaton, IL 60187

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
KANE COUNTY DIVISION OF TRANSPORTATION
ORCHARD ROAD RECONSTRUCTION
**MAINTENANCE OF TRAFFIC
TYPICAL SECTIONS AND NOTES
STAGE II**

SCALE: VERT.
HORIZ.
DATE: 11/04/05

DRAWN BY: RJN
CHECKED BY: SPF
