

PRE-STAGE

- 1. NORTHBOUND TRAFFIC SHALL BE REDUCED TO ONE LANE AND TEMPORARY CONCRETE BARRIER SHALL BE INSTALLED AS SHOWN.
- 2. REMOVE EXISTING PAVEMENT, CURB AND GUTTER, AND SIDEWALK BETWEEN STATION 120+50 AND 135+97.
- 3. CONSTRUCT STORM SEWER ON SKOKIE BLVD FROM STATION 120+60 TO STATION 138+80 AND PATCH THE PAVEMENT AS SHOWN IN ROADWAY PLAN BETWEEN STATION 120+50 AND 135+97. CONSTRUCT PROPOSED CURB AND GUTTER BETWEEN STATION 120+50 AND 138+80.

- I. REMOVE MEDIANS AND ISLANDS AND CONSTRUCT TEMPORARY PAVEMENT. USE TRAFFIC CONTROL STANDARDS 701427, 701502, 701601, 701602, 701701, 701801 AND 701901 TO PERFORM THIS WORK
- 2. INSTALL TEMPORARY TRAFFIC SIGNAL AT MIDDLE ENTRANCE, NORTH ENTRANCE AND OLD ORCHARD ROAD AND REMOVE TRAFFIC SIGNAL POST FROM THE MEDIAN AT NORTH ENTRANCE.
- 3. CONSTRUCT STORM SEWER AND TWO OUTSIDE NORTHBOUND LANES OF SKOKIE BLVD.


EAST EX ROW WEST EX ROW B SKOKIE BOULEVARD CONSTRUCTION WORK ZONE -DRUM OR BARRICADE TEMPORARY PAVEMENT MARKING (TYP)

STAGE 2A

- 1. SETUP TRAFFIC CONTROL STRIPING, SIGNS AND BARRICADES FOR SKOKIE BOULEVARD WITH FIVE LANES OF TRAFFIC (TWO THRU LANES IN EACH DIRECTION AND ONE TURN LANE). ONE NORTHBOUND LANE TO BE SHIFTED ON NEWLY CONSTRUCTED PAVEMENT.
- 2. TEMPORARY CONCRETE BARRIER TO BE REMOVED FROM SITE.
- 3. CONSTRUCT THIRD NORTHBOUND LANE ON SKOKIE BOULEVARD.


SKOKIE BLVD STAGE 2A TYPICAL SECTION

SKOKIE BLVD STAGE 1A TYPICAL SECTION

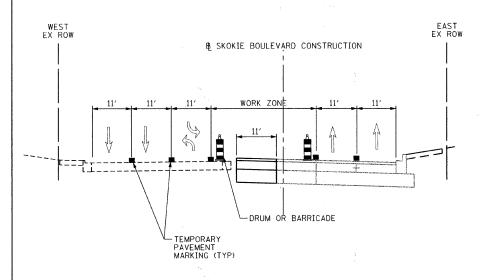

STAGE 2B

- 1. SETUP TRAFFIC CONTROL STRIPING, SIGNS AND BARRICADES FOR SKOKIE BOULEVARD WITH FIVE LANES OF TRAFFIC (TWO THRU LANES IN EACH DIRECTION AND ONE TURN LANE). TWO NORTHBOUND LANES TO BE SHIFTED ON NEWLY CONSTRUCTED PAVEMENT.
- 2. CONSTRUCT TURN LANES ON SKOKIE BOULEVARD.

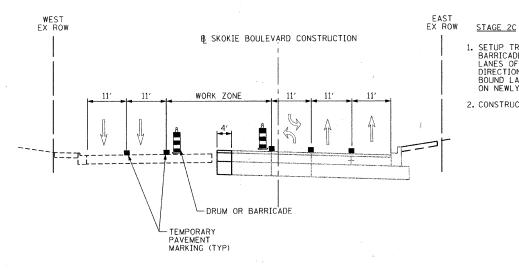

SKOKIE BLVD STAGE 2C TYPICAL SECTION

- 1. SETUP TRAFFIC CONTROL STRIPING, SIGNS AND BARRICADES FOR SKOKIE BOULEVARD WITH FIVE LANES OF TRAFFIC (TWO THRU LANES IN EACH DIRECTION AND ONE TURN LANE). TWO NORTH-BOUND LANES AND TURN LANE TO BE SHIFTED ON NEWLY CONSTRUCTED PAVEMENT.
- 2. CONSTRUCT TURN LANES ON SKOKIE BOULEVARD.

SKOKIE BLVD STAGE 2B TYPICAL SECTION

FILE NAME =	USER NAME = CEComin	DESIGNED FA	REVISED -
g:\ch#8\##45\roed\sheets\#45-MT-3#1-TYP.sht		DRAWN FA	REVISED -
	PLOT SCALE = 50.000 '/ IN.	CHECKED DWB	REVISED ~
	PLOT DATE = 10/26/2011	DATE 10/26/2011	REVISED -

STATE OF ILLINOIS **DEPARTMENT OF TRANSPORTATION**

U.S. ROUTE 41 (SKOKIE BOULEVARD) SUGGESTED TRAFFIC CONTROL PLANS - TYPICAL SECTIONS SHEET NO. 1 OF 21 SHEETS STA.

SECTION COUNTY 350 00-00243-00-CH COOK 142 22 CONTRACT NO. 63566 FED. ROAD DIST. NO. 7 | ILLINOIS | FED. AID PROJECT

Trem Systems
