


STAGE IV



CONSTRUCTION ACTIVITIES

STAGE IV

1. COMPLETE PYOTT ROAD, AIRPORT ROAD, AND DRIVEWAY CONSTRUCTION (SURFACE COURSE), REMOVE OLD PYOTT ROAD TO LIMITS DESCRIBED IN PLANS, COMPLETE FINAL GRADING AND SEEDING, AND REMOVE TEMPORARY WIDENING (SOME MAY BE USED AS PART OF FINAL SHOULDER).

NOTES


1. AFTER PLACEMENT OF SURFACE COURSE AND BEFORE PLACEMENT OF FINAL STRIPING, TEMPORARY MARKING FOR STRIPING UTILIZING TAPE WILL BE USED TO DELINEATE TRAFFIC LANES. THE TAPE WILL BE REMOVED BEFORE FINAL STRIPING.
2. ALL CONSTRUCTION STAGING IS SUGGESTED AND CAN BE REVISED ON WRITTEN APPROVAL OF THE ENGINEER TWO WEEKS PRIOR TO THE START OF WORK. THERE WILL BE NO ADJUSTMENT IN THE "TRAFFIC CONTROL AND PROTECTION" UNIT PRICE DUE TO THE CONTRACTOR CHANGING THE PLAN CONSTRUCTION SEQUENCE. ANY CHANGES WILL BE IN ACCORDANCE WITH THESE NOTES AND THE SPECIAL PROVISION FOR "TRAFFIC CONTROL AND PROTECTION".
3. TEMPORARY WIDENING REMOVAL IS INCIDENTAL TO "TRAFFIC CONTROL AND PROTECTION".

SUMMARY OF TRAFFIC CONTROL

1. UTILIZE LANE CLOSURES AND MOVING LANE CLOSURES TO COMPLETE SURFACE COURSE AND STRIPING

APPLICABLE IDOT TRAFFIC CONTROL STANDARDS

701001-01	OFF-RD OPERATIONS, 2L, 2W, MORE THAN 15' AWAY
701006-02	OFF-RD OPERATIONS, 2L, 2W, 15' TO 2' FROM PAVEMENT EDGE
701901	TRAFFIC CONTROL DEVICES
D-1 STANDARD (TC22)	ARTERIAL ROAD INFORMATIONAL SIGN
701311-2	LANE CLOSURE 2L, 2W MOVING OPERATIONS-DAY ONLY
701301-02	LANE CLOSURE, 2L, 2W, SHORT TIME OPERATIONS
701306-01	LANE CLOSURE, 2L, 2W, SLOW MOVING OPERATIONS DAY ONLY, FOR SPEED >= 45 MPH
D-1 STANDARD (TC10)	TRAFFIC CONTROL AND PROTECTION FOR SIDE ROADS, INTERSECTIONS, AND DRIVEWAYS

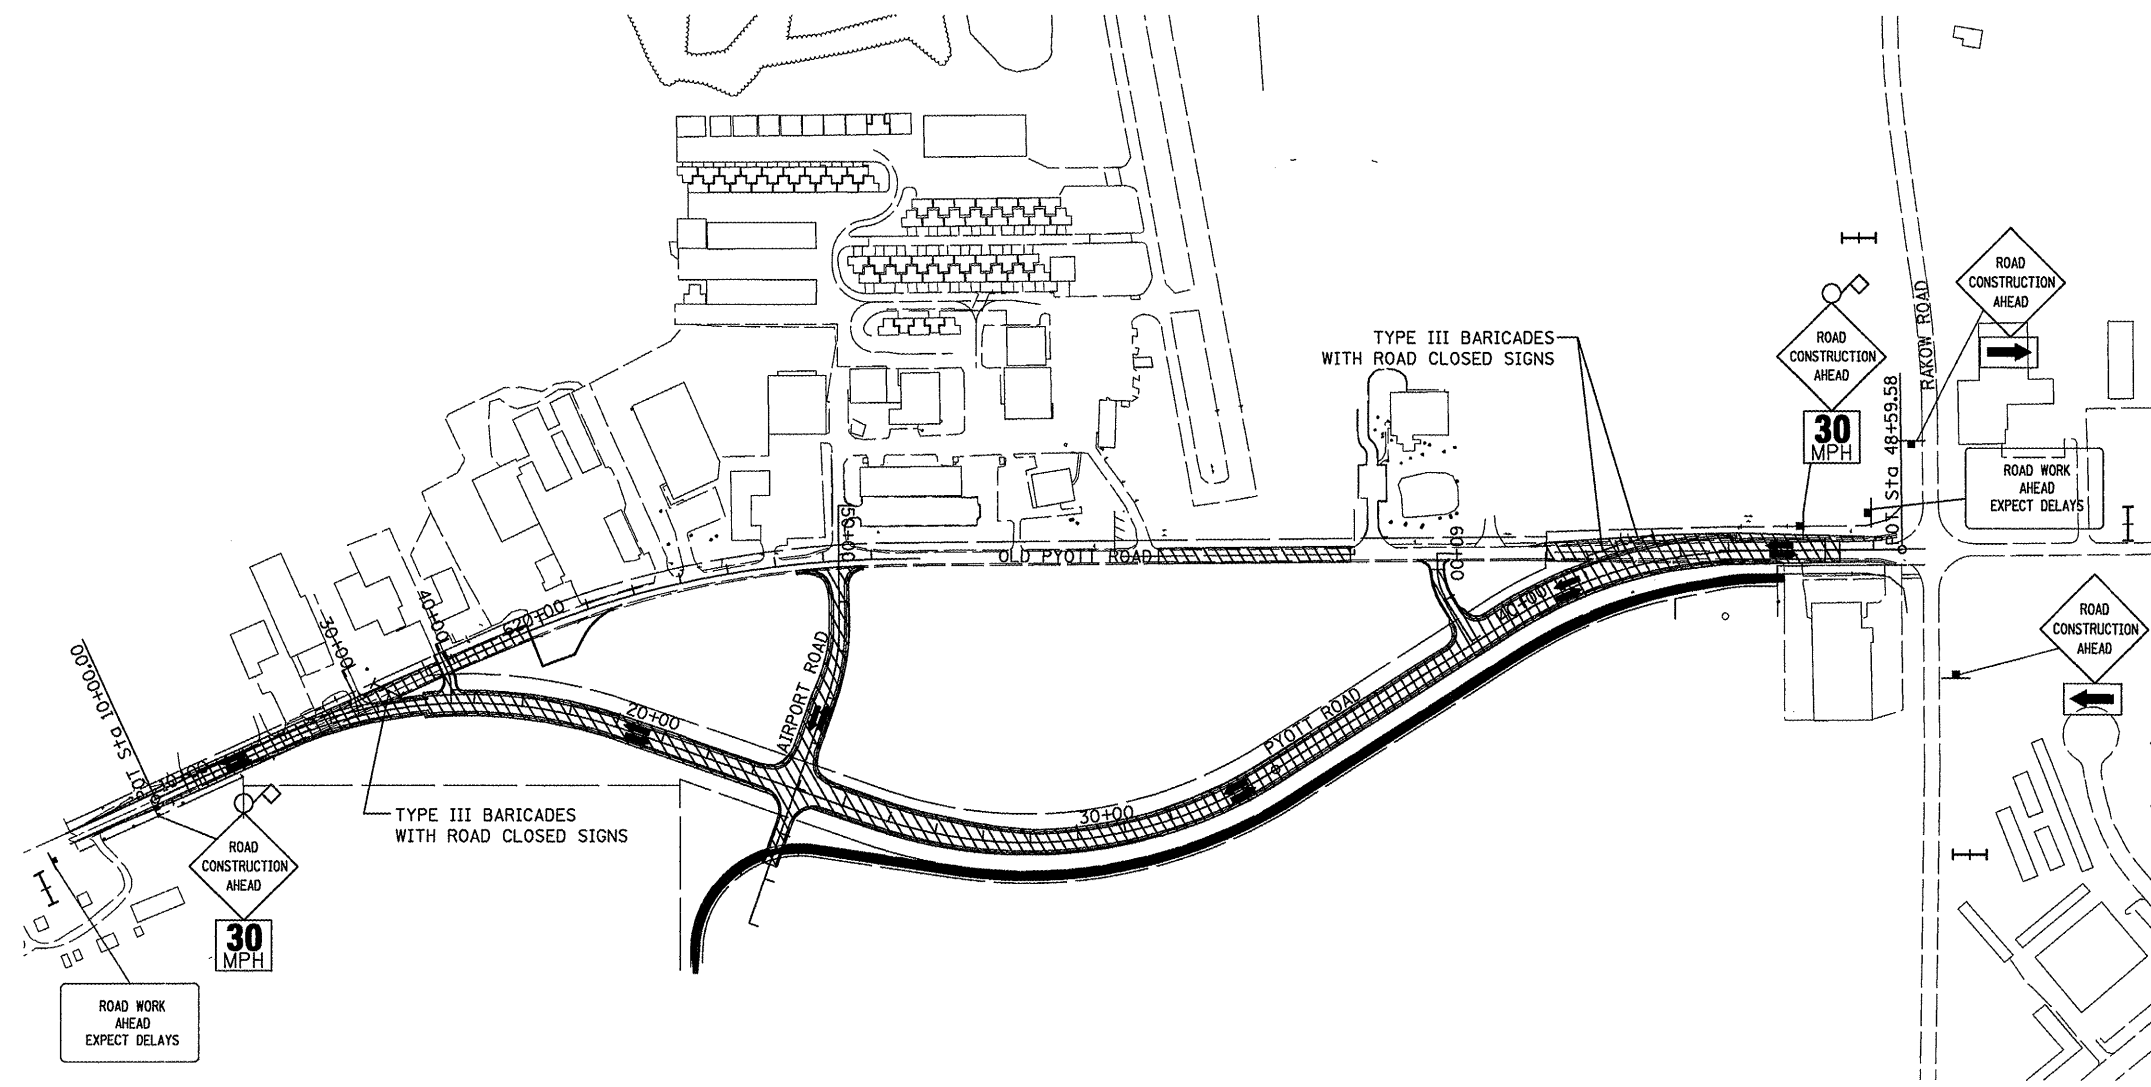

LEGEND

- WORK AREA
- COMPLETED ROADWAY SURFACE
- INTERIM ROADWAY SURFACE
- SIGN LOCATION
- TYPE II BARRICADE WITH STEADY BURNING LIGHTS
- DIRECTION OF TRAFFIC
- FLASHING LIGHT, SIGN MOUNTED
- 18" X 18" (MIN.) ORANGE WARNING FLAG
- TYPE III BARRICADE
- ROW LINE
- DRUM OR BARRICADE
- CHANGEABLE MESSAGE SIGN, TO REMAIN THROUGH ALL STAGES FOR MORE INFORMATION SEE SHEET 8

Hanson Professional Services Inc.
 Suite 200, 845 Commercial Drive
 Oak Brook, Illinois 60523
 © Copyright Hanson Professional Services Inc. 2009



FILE NAME =	USER NAME = B1e1n01219	DESIGNED - DRM	REVISED -	VILLAGE OF LAKE IN THE HILLS, ILLINOIS	CONSTRUCTION PHASING - STAGE IV	COUNTY	TOTAL SHEETS	SHEET NO.
1:\05\jobs\00841\05b8021\civil part b\sheet\c-1mt-mt401.dwg	DRAWN - CBP	REVISED -	MCHENRY			143	16	
PLOT SCALE = 399.9992' / IN.	CHECKED - AAH	REVISED -	AIP NO. 3-17-0112-B10 ILLINOIS IDA NO. 3CK-3807					
PLOT DATE = 02/25/2009, 11:39 AM	DATE - 05/21/08	REVISED -						
