
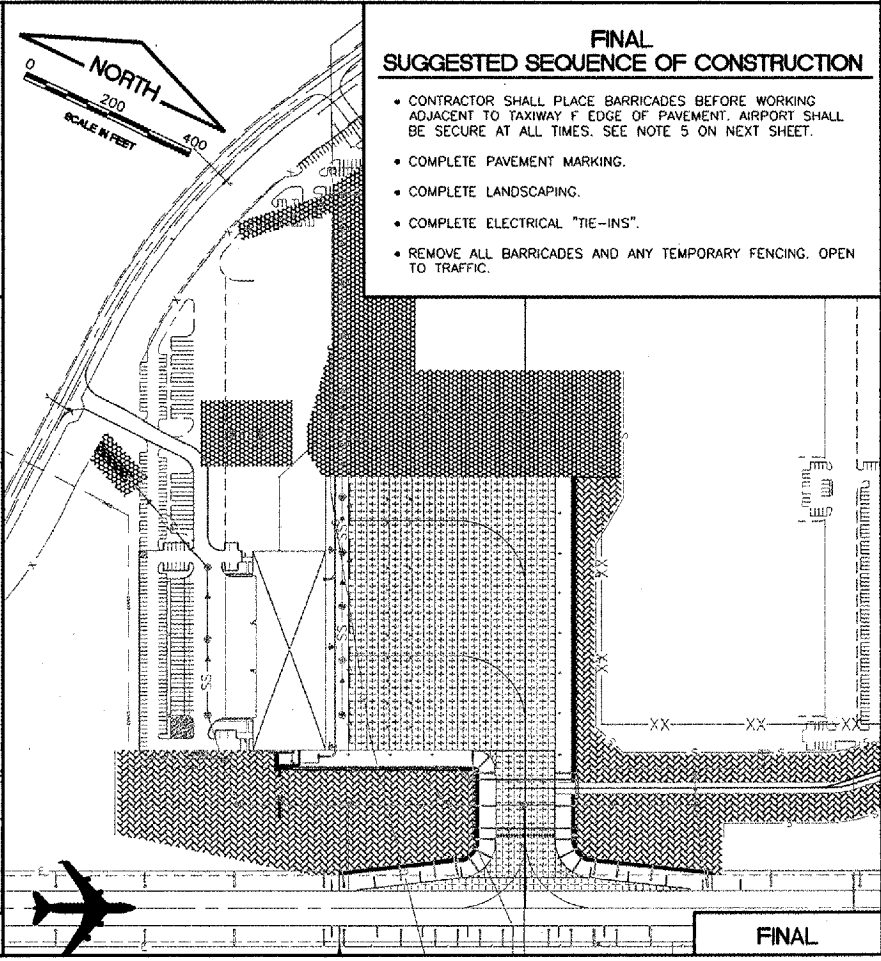
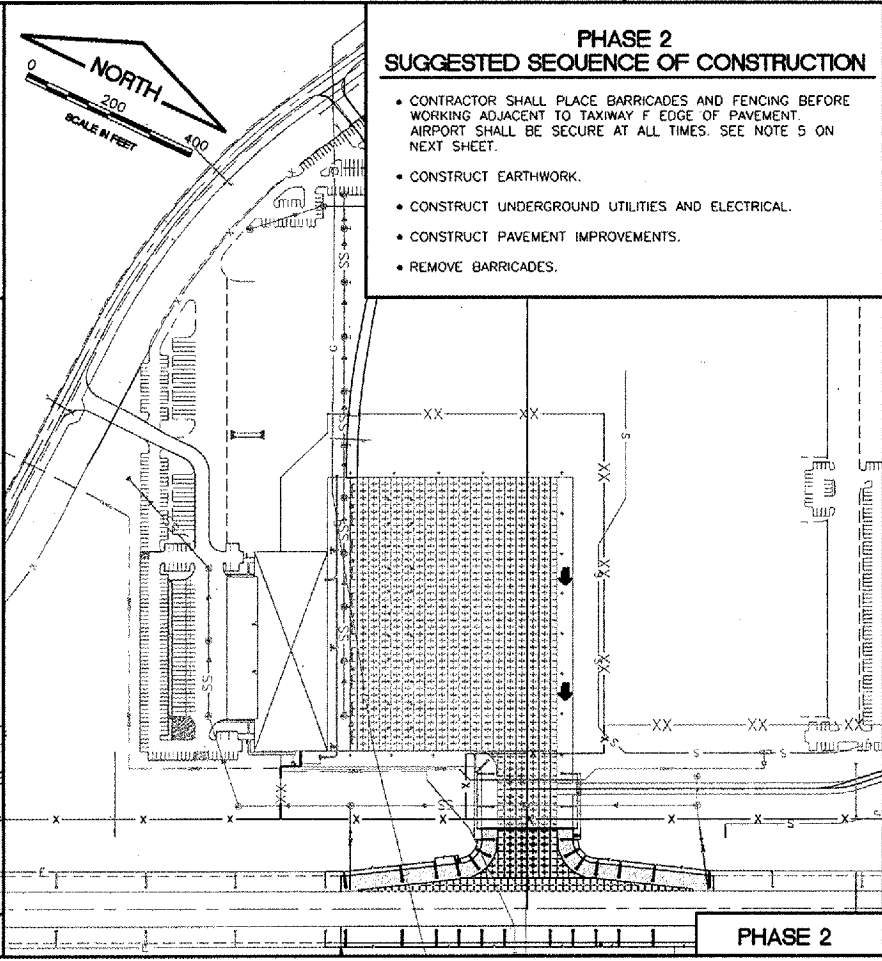
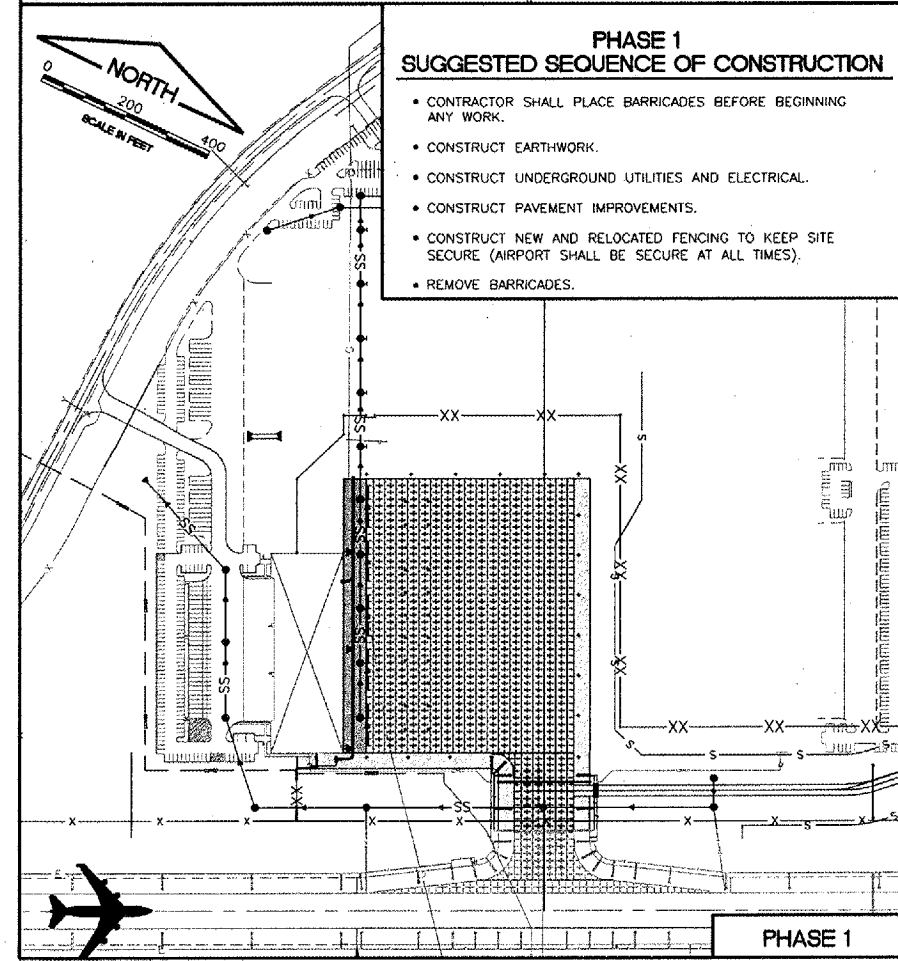


| PHASE | WORK AREA | ALLOWABLE WORK PERIODS | AIRCRAFT OPERATIONAL RESTRICTIONS | APPROXIMATE SCHEDULE |
|-------|--|--|---|---|
| 1 | AREAS OUTSIDE OF TAXIWAY F A.O.A. AND TSA SECURITY FENCING | 7:00 A.M. - 7:00 P.M. | NO RESTRICTIONS | JUNE 6-SEPTEMBER 9, 2008 (96 CALENDAR DAYS) |
| 2 | AREAS WITHIN TAXIWAY F A.O.A. AND TSA SECURITY FENCING | DAILY CLOSURES OF TAXIWAY F WILL BE PERMITTED 7:00 A.M. - 7:00 P.M. | WORK WITHIN THE TAXIWAY F A.O.A. WILL REQUIRE THE TEMPORARY CLOSURE OF TAXIWAY F AS SHOWN. WORK REQUIRING THE CLOSURE OF TAXIWAY F SHALL BE EXPEDITED AND PRIORITIZED TO MINIMIZE CLOSURE TIME. | SEPTEMBER 10-OCTOBER 31, 2008 (52 CALENDAR DAYS) |
| FINAL | AREAS OUTSIDE AND WITHIN TAXIWAY F A.O.A. AND TSA SECURITY FENCING FOR FINAL LANDSCAPING AND MARKING | DAILY CLOSURES OF TAXIWAY F WILL BE PERMITTED 7:00 A.M. - 7:00 P.M. | WORK WITHIN THE TAXIWAY F A.O.A. WILL REQUIRE THE TEMPORARY CLOSURE OF TAXIWAY F AS SHOWN. WORK REQUIRING THE CLOSURE OF TAXIWAY F SHALL BE EXPEDITED AND PRIORITIZED TO MINIMIZE CLOSURE TIME. | NOVEMBER 1-NOVEMBER 25, 2008 (26 CALENDAR DAYS) |
| | | | | 174 CAL DAYS TOTAL |

REVISIONS

| NUMBER | BY | DATE |
|--------|----|------|
| | | |
| | | |
| | | |



**CHICAGO ROCKFORD INTERNATIONAL AIRPORT
 ROCKFORD, ILLINOIS**
**SEQUENCE OF CONSTRUCTION
 PLAN - SHEET 1**

© Copyright CMT, Inc.

CMT
 CRANKFORD, MURPHY & TILLY, INC.
 CONSULTING ENGINEERS
 License No. 184-000618

Chicago Rockford International Airport

DESIGN BY: JRL
 DRAWN BY: JRO
 CHECKED BY: RFD
 APPROVED BY:
 DATE: 02/29/08
 JOB No: 07258-06
 ILLINOIS PROJECT: RFD-3787
 A.I.P. PROJECT: 3-17-0088-XX
FINAL SUBMITTAL
 SHEET 4 OF 83 SHEETS
