

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
74	(90-11R-2; 90(13,14,14-1)R-1	TAZEWELL	1366	124
STA.		TO STA.		
FED. ROAD DIST. NO. 4		ILLINOIS FED. AID PROJECT		

PRE-STAGE 3 (THESE ITEMS ARE TO BEGIN DURING PRE-STAGE 3, DURATION FROM SEPT. 2005 - NOV 2005;
CONSTRUCTION: REMAINING ITEMS TO BEGIN AFTER WINTER SHUTDOWN IF THEY IMPACT TRAFFIC OPERATIONS

- ⑥ REMOVE EXISTING SHOULDERS AND PLACE TEMPORARY PAVEMENT
- ⑦ COMPLETE TEMPORARY TRAFFIC SIGNALS AT NORTH MAIN STREET AND BLACKJACK BOULEVARD AND PROPOSED ISLAND, PROPOSED SIGNALS TO BE CONSTRUCTED
- ⑧ REMOVE AND REPLACE SHOULDERS FROM STATION 4+157 TO 4+264 PRIOR TO MEDIAN CONSTRUCTION
- ⑨ RECONSTRUCT NORTH MAIN STREET MEDIAN FROM STATION 4+013 TO 4+157
- ⑩ CONSTRUCT STORM SEWER CROSSINGS AT STATION 3+655 AND 3+925


GENERAL NOTES:

SEE SIGNING PLAN FOR STAGED REMOVAL OF EXISTING SIGNS AND STAGED PLACEMENT OF PROPOSED INFORMATION AND GUIDE SIGNS.

THE STAGED CONSTRUCTION SHOWN HERE IS A GENERAL SEQUENCING SUGGESTION.

TRAFFIC:

- 1. MAINTAIN TWO LANES OF TRAFFIC IN EACH DIRECTION ON NORTH MAIN STREET DURING PEAK HOURS AND AT LEAST ONE LANE OF TRAFFIC IN EACH DIRECTION DURING OFF PEAK HOURS. LANE CLOSURES SHALL BE IN ACCORDANCE WITH STANDARD 701602.
- 2. TRAFFIC SHALL BE MAINTAINED ON BLACKJACK BOULEVARD AND CATERPILLAR TRAIL.

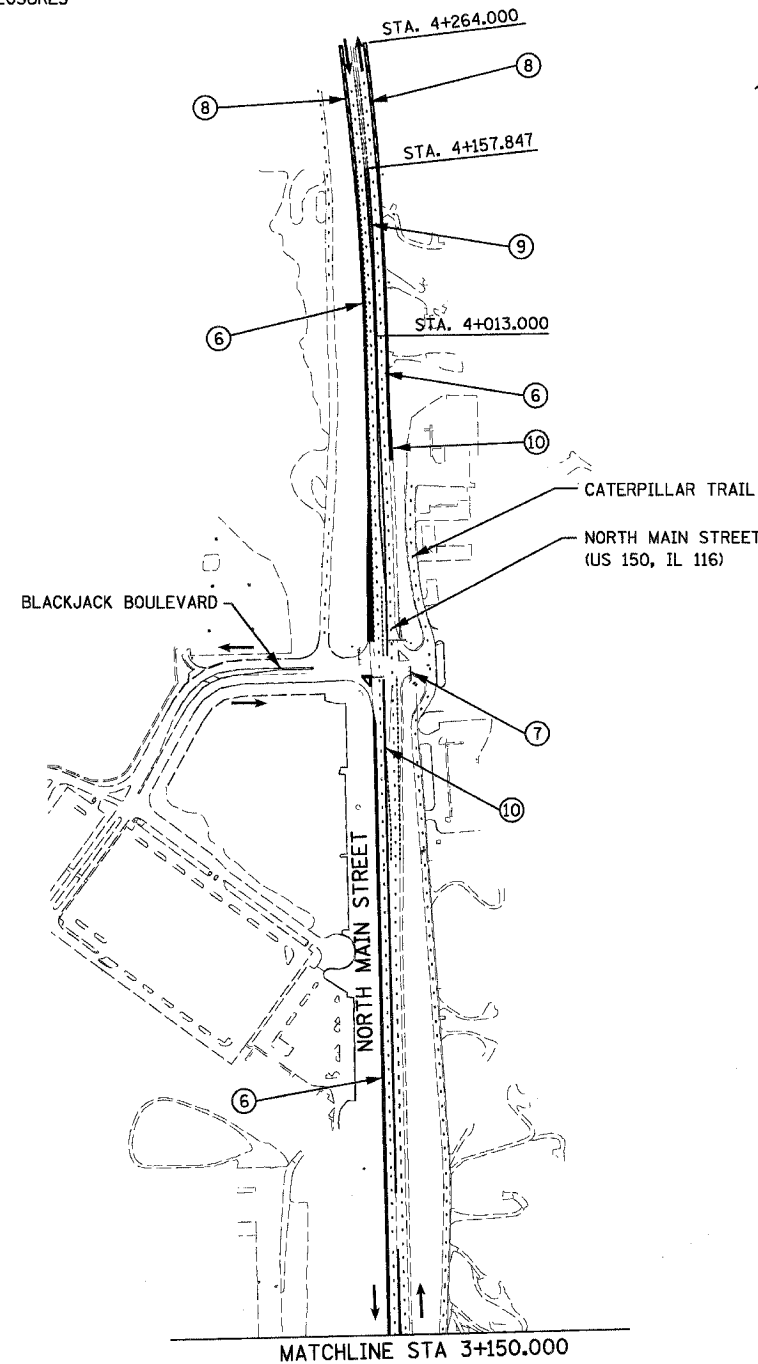

LEGEND

- WORK AREA
- DIRECTION OF TRAFFIC FLOW

SHEET 2 OF 2

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
 F.A.I. ROUTE 74 (I-74)
 CONSTRUCTION SEQUENCING
 STAGE 3A-1 (PRE-STAGE 3)

URS
 URS CORPORATION
 CHICAGO, ILLINOIS

DRAWN BY KMO
 CHECKED BY RTG
 DATE 12/20/2004
