




PLAN	DATE
REVISED	BY
NOTED	BY
ALIGNED	BY
CHECKED	BY
DESIGNED	BY
DRAWN	BY
NO.	

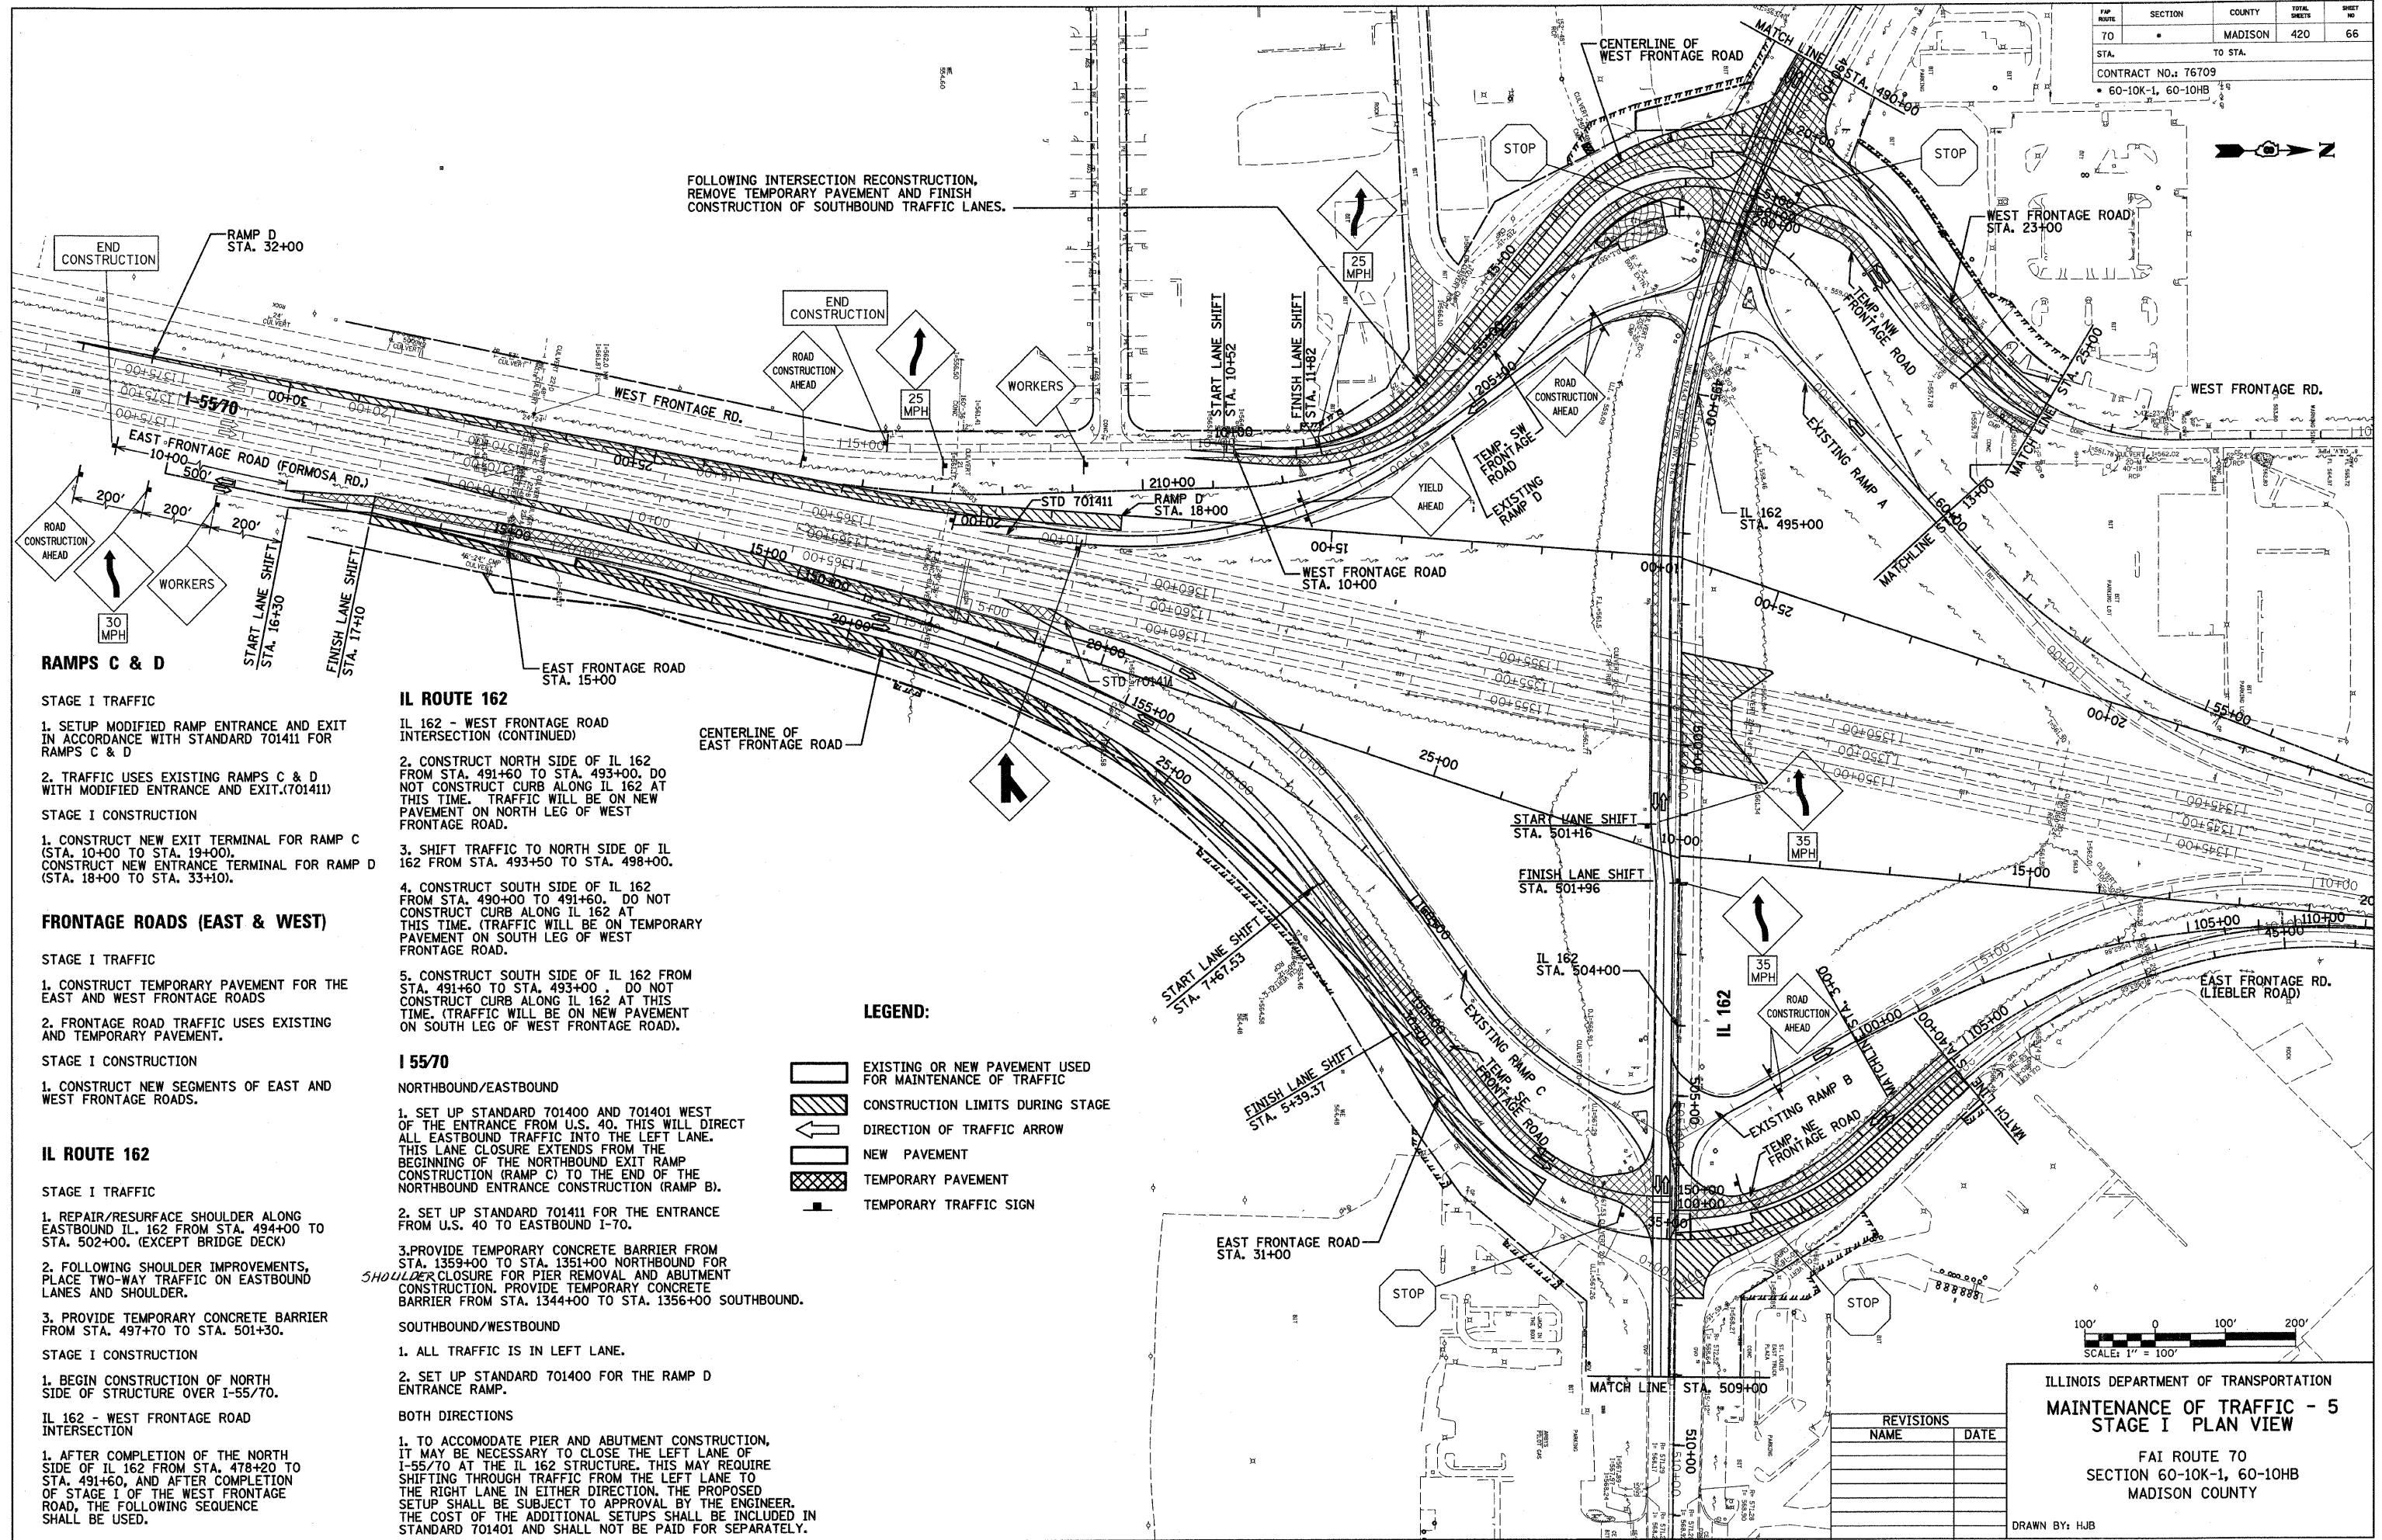

END CONSTRUCTION
 RAMP D STA. 32+00

FOLLOWING INTERSECTION RECONSTRUCTION,
 REMOVE TEMPORARY PAVEMENT AND FINISH
 CONSTRUCTION OF SOUTHBOUND TRAFFIC LANES.

RAMPS C & D

STAGE I TRAFFIC

1. SETUP MODIFIED RAMP ENTRANCE AND EXIT IN ACCORDANCE WITH STANDARD 701411 FOR RAMPS C & D
2. TRAFFIC USES EXISTING RAMPS C & D WITH MODIFIED ENTRANCE AND EXIT.(701411)

STAGE I CONSTRUCTION

1. CONSTRUCT NEW EXIT TERMINAL FOR RAMP C (STA. 10+00 TO STA. 19+00), CONSTRUCT NEW ENTRANCE TERMINAL FOR RAMP D (STA. 18+00 TO STA. 33+10).

FRONTAGE ROADS (EAST & WEST)

STAGE I TRAFFIC

1. CONSTRUCT TEMPORARY PAVEMENT FOR THE EAST AND WEST FRONTAGE ROADS
2. FRONTAGE ROAD TRAFFIC USES EXISTING AND TEMPORARY PAVEMENT.

STAGE I CONSTRUCTION

1. CONSTRUCT NEW SEGMENTS OF EAST AND WEST FRONTAGE ROADS.

IL ROUTE 162

STAGE I TRAFFIC

1. REPAIR/RESURFACE SHOULDER ALONG EASTBOUND IL 162 FROM STA. 494+00 TO STA. 502+00. (EXCEPT BRIDGE DECK)
2. FOLLOWING SHOULDER IMPROVEMENTS, PLACE TWO-WAY TRAFFIC ON EASTBOUND LANES AND SHOULDER.
3. PROVIDE TEMPORARY CONCRETE BARRIER FROM STA. 497+70 TO STA. 501+30.

STAGE I CONSTRUCTION

1. BEGIN CONSTRUCTION OF NORTH SIDE OF STRUCTURE OVER I-55/70.

IL 162 - WEST FRONTAGE ROAD INTERSECTION

1. AFTER COMPLETION OF THE NORTH SIDE OF IL 162 FROM STA. 478+20 TO STA. 491+60, AND AFTER COMPLETION OF STAGE I OF THE WEST FRONTAGE ROAD, THE FOLLOWING SEQUENCE SHALL BE USED.

IL ROUTE 162

IL 162 - WEST FRONTAGE ROAD INTERSECTION (CONTINUED)

2. CONSTRUCT NORTH SIDE OF IL 162 FROM STA. 491+60 TO STA. 493+00. DO NOT CONSTRUCT CURB ALONG IL 162 AT THIS TIME. TRAFFIC WILL BE ON NEW PAVEMENT ON NORTH LEG OF WEST FRONTAGE ROAD.

3. SHIFT TRAFFIC TO NORTH SIDE OF IL 162 FROM STA. 493+50 TO STA. 498+00.

4. CONSTRUCT SOUTH SIDE OF IL 162 FROM STA. 490+00 TO STA. 491+60. DO NOT CONSTRUCT CURB ALONG IL 162 AT THIS TIME. (TRAFFIC WILL BE ON TEMPORARY PAVEMENT ON SOUTH LEG OF WEST FRONTAGE ROAD).

5. CONSTRUCT SOUTH SIDE OF IL 162 FROM STA. 491+60 TO STA. 493+00. DO NOT CONSTRUCT CURB ALONG IL 162 AT THIS TIME. (TRAFFIC WILL BE ON NEW PAVEMENT ON SOUTH LEG OF WEST FRONTAGE ROAD).

I 55/70

NORTHBOUND/EASTBOUND

1. SET UP STANDARD 701400 AND 701401 WEST OF THE ENTRANCE FROM U.S. 40. THIS WILL DIRECT ALL EASTBOUND TRAFFIC INTO THE LEFT LANE. THIS LANE CLOSURE EXTENDS FROM THE BEGINNING OF THE NORTHBOUND EXIT RAMP CONSTRUCTION (RAMP C) TO THE END OF THE NORTHBOUND ENTRANCE CONSTRUCTION (RAMP B).

2. SET UP STANDARD 701411 FOR THE ENTRANCE FROM U.S. 40 TO EASTBOUND I-70.

3. PROVIDE TEMPORARY CONCRETE BARRIER FROM STA. 1359+00 TO STA. 1351+00 NORTHBOUND FOR SHOULDER CLOSURE FOR PIER REMOVAL AND ABUTMENT CONSTRUCTION. PROVIDE TEMPORARY CONCRETE BARRIER FROM STA. 1344+00 TO STA. 1356+00 SOUTHBOUND.

SOUTHBOUND/WESTBOUND

1. ALL TRAFFIC IS IN LEFT LANE.


2. SET UP STANDARD 701400 FOR THE RAMP D ENTRANCE RAMP.

BOTH DIRECTIONS

1. TO ACCOMMODATE PIER AND ABUTMENT CONSTRUCTION, IT MAY BE NECESSARY TO CLOSE THE LEFT LANE OF I-55/70 AT THE IL 162 STRUCTURE. THIS MAY REQUIRE SHIFTING THROUGH TRAFFIC FROM THE LEFT LANE TO THE RIGHT LANE IN EITHER DIRECTION. THE PROPOSED SETUP SHALL BE SUBJECT TO APPROVAL BY THE ENGINEER. THE COST OF THE ADDITIONAL SETUPS SHALL BE INCLUDED IN STANDARD 701401 AND SHALL NOT BE PAID FOR SEPARATELY.

LEGEND:

- EXISTING OR NEW PAVEMENT USED FOR MAINTENANCE OF TRAFFIC
- CONSTRUCTION LIMITS DURING STAGE
- DIRECTION OF TRAFFIC ARROW
- NEW PAVEMENT
- TEMPORARY PAVEMENT
- TEMPORARY TRAFFIC SIGN



ILLINOIS DEPARTMENT OF TRANSPORTATION
MAINTENANCE OF TRAFFIC - 5
STAGE I PLAN VIEW

FAI ROUTE 70
 SECTION 60-10K-1, 60-10HB
 MADISON COUNTY

DRAWN BY: HJB

PLOT DATE: *DATE-TIME*

REVISIONS	
NAME	DATE
