

RT. STA. 310+82 TO STA. 313+10

RT. STA. 312+80 TO STA. 313+57

TEMPORARY DETOUR ROAD

STORM SEWER INSTALLATION

DRIVEWAY TEMPORARY ACCESS

LT. STA. 326+00±

RT. STA. 323+95 TO STA. 324+60

## STAGE 3

## CONSTRUCTION

- CONSTRUCT TEMPORARY ACCESS AS DETAILED.
- REMOVE EXISTING PAVEMENT AND OTHER ITEMS INDICATED.
- CONSTRUCT CROSSROAD AND LATERAL STORM SEWER.
- PERFORM EARTHWORK.
- FINAL UTILITY ADJUSTMENTS SHALL BE PERFORMED.
- CONSTRUCT CURB AND GUTTER AND PAVEMENT
- DRIVEWAY APRONS AT STA. 308+38.5, 309+72, 310+39.9, 311+31.4, 311+78 AND 312+07.2 SHALL NOT BE CONSTRUCTED UNTIL STAGE 3 IS OPEN TO TRAFFIC AND TEMPORARY AGGREGATE BETWEEN DRIVEWAYS IS REMOVED.
- ALL OTHER DRIVEWAY APRONS, SIDEWALK, AND OTHER ITEMS WITHIN THE LIMITS OF STAGE 3 CAN BE COMPLETED NOW OR IN LATER
- 9. REMOVE TEMPORARY ACCESS ITEMS AFTER OPENING WARD STREET BACK UP TO TRAFFIC.

## TRAFFIC


- CONSTRUCT IMPROVEMENTS FROM STA. 308+40 TO STA. 313+00 WHILE CLOSING THIS PORTION OF SOUTH WARD STREET TO ALL TRAFFIC. WARD STREET SHALL BE CLOSED TO THRU TRAFFIC FROM STA. 300+50 TO STA. 308+40 AND STA. 313+00 TO STA. 315+00. TWO-LANE, 2-WAY TRAFFIC SHALL BE MAINTAINED OUTSIDE OF THESE LIMITS.
- TEMPORARY GRAVEL ACCESS SHALL BE CONSTRUCTED PRIOR TO CLOSING THIS PORTION OF WARD STREET. GRAVEL SHALL BE PLACED BETWEEN DRIVES AT STA. 308+38.5, STA. 309+72, AND STA. 310+39.9, ALLOWING ACCESS FOR THESE RESIDENCES TO THE SOUTH OF THE CONSTRUCTION LIMITS. GRAVEL SHALL ALSO BE PLACED BETWEEN DRIVES AT STA. 311+04, STA. 311+31.4, STA. 311+78, AND STA. 312+07.2, OUTLETTING VEHICLES FROM THESE RESIDENCES JUST TO THE NORTH OF THE CONSTRUCTION LIMITS FOR THIS PHASE.
- IMPROVEMENTS FOR THE CHASE STREET ENTRANCE TO THE CHURCH OF CHRIST SHALL BE CONSTRUCTED SIMULTANEOUSLY WITH STAGE 3 WORK. ACCESS TO THE CHURCH OFF OF WARD STREET SHALL REMAIN OPEN UNTIL THESE IMPROVEMENTS ARE COMPLETED AND THIS ENTRANCE IS AVAILABLE TO TRAFFIC.
- D. IMPLEMENT SPECIAL SIGN TABLE IN SPECIAL PROVISIONS.

STAGE 3 STA 308+40: TO STA 313+00:

SHEET NO.

29

IMPROVEMENTS
STAGING PLAN
MACOMB STREET I WARD

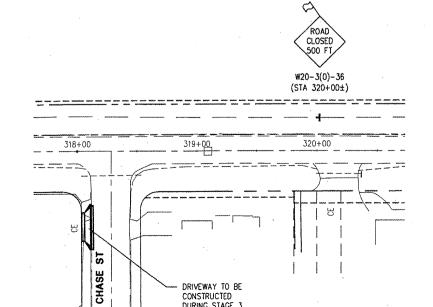

CONSTRUCTED

DURING STAGE 3

ROAD

WORK


AHEAD,

W21-4(0)-36

INSTALLATION

EAST AND WEST

OF WARD ST

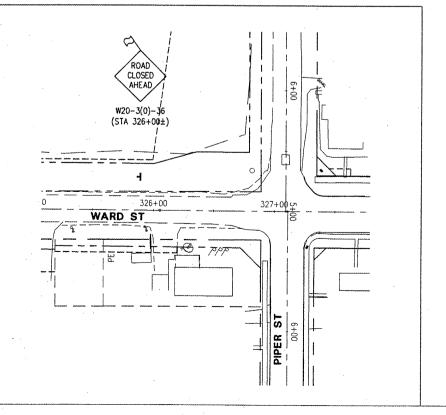

78

28

493

183

176

1124

SCALE IN FEET
