



F.A.S. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
1373	00-00058-00-RS	COOK	113	25
STA.	TO STA.			
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		
CONTRACT No: 83861				

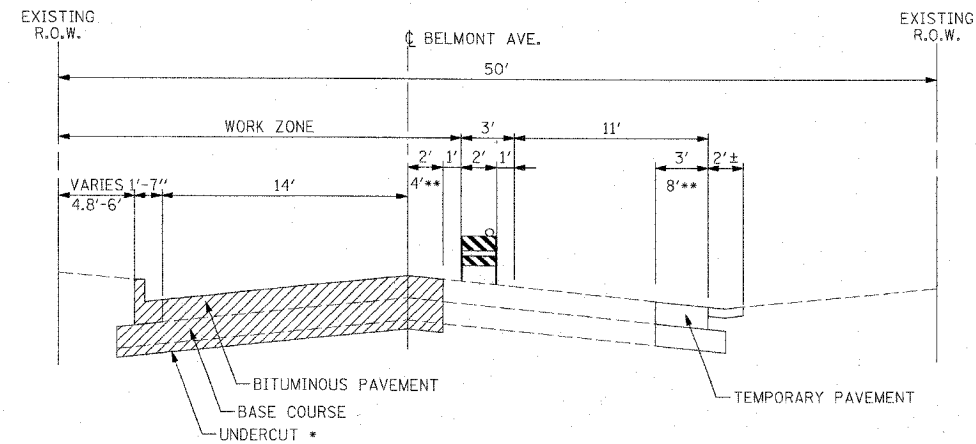


MAINTENANCE OF TRAFFIC TYPICAL SECTION
STAGE II
BELMONT AVENUE
STA. 110+60 TO STA. 112+50**
STA. 112+50 TO STA. 128+50

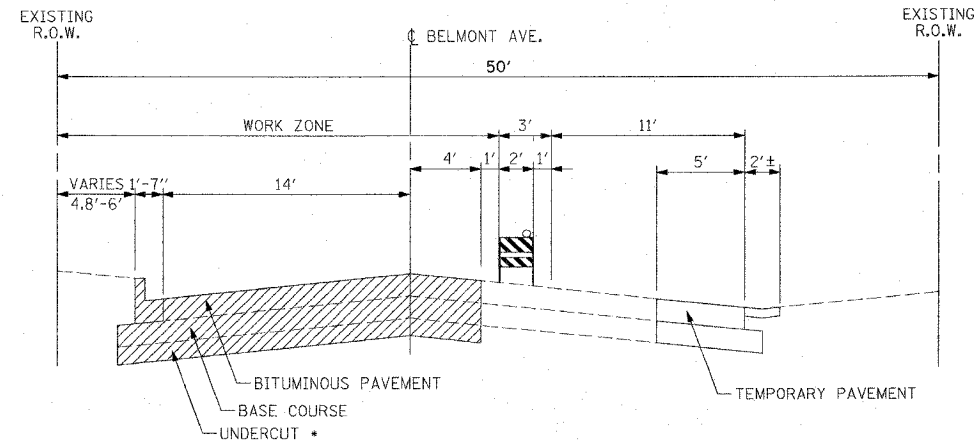

MAINTENANCE OF TRAFFIC TYPICAL SECTION
STAGE II
BELMONT AVENUE
STA. 129+50 TO STA 145+50.94

- STA. 110+60 TO STA. 112+50, 6" OF UNDERCUT IS REQUIRED
- STA. 112+50 TO STA. 129+50, NO UNDERCUT IS REQUIRED
- STA. 129+50 TO STA. 136+50, 12" OF UNDERCUT IS REQUIRED
- STA. 136+50 TO STA. 142+00, NO UNDERCUT IS REQUIRED
- STA. 142+00 TO STA. 145+50.94, 6" OF UNDERCUT IS REQUIRED

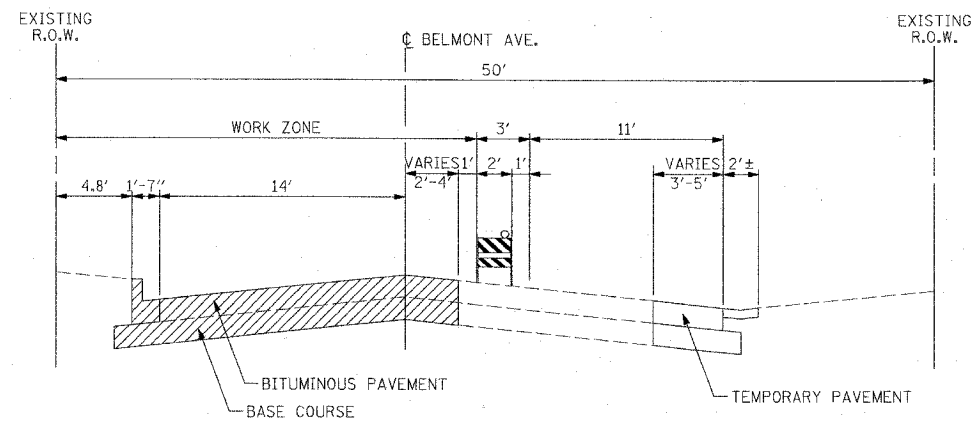

MAINTENANCE OF TRAFFIC TYPICAL SECTION
STAGE II
BELMONT AVENUE
STA. 128+50 TO STA. 129+50

STAGE II:

WORK AREA:

- THE WORK AREA IS LOCATED ON THE NORTH SIDE OF BELMONT AVENUE IN THE WESTBOUND LANES STARTING AT STA 115+00.

WORK COMPONENTS:

- INSTALL TYPE II BARRICADES @ 50' C-C TANGENTS, 25' C-C TAPERS, 10' C-C RADII
- REMOVE EXISTING PAVEMENT IN THE RIGHT-OF-WAY.
- CONSTRUCT NEW STORM SEWER.
- CONSTRUCT NEW PAVEMENT AND DRIVEWAYS ON THE NORTH SIDE OF BELMONT AVENUE

MAINTENANCE OF TRAFFIC:

- MAINTAIN DETOUR ROUTE ESTABLISHED IN STAGE 1B.
- EASTBOUND TRAFFIC WILL BE MAINTAINED ON THE EXISTING EASTBOUND LANES AND ON THE TEMPORARY PAVEMENT CONSTRUCTED DURING STAGE 1
- ALL SIDE STREETS AND DRIVEWAYS WILL REMAIN OPENED TO TRAFFIC UNLESS OTHERWISE NOTED.

GENERAL NOTES:

- IT IS THE RESPONSIBILITY OF THE CONTRACTOR TO PROVIDE ADEQUATE DRAINAGE AND EROSION CONTROL DURING CONSTRUCTION.
- ALL EXISTING PAVEMENT MARKINGS IN CONFLICT WITH TEMPORARY TRAFFIC CONFIGURATIONS SHALL BE REMOVED.

REVISIONS		ILLINOIS DEPARTMENT OF TRANSPORTATION
NAME	DATE	
		MAINTENANCE OF TRAFFIC STAGE II TYPICAL SECTIONS

SCALE: VERT. N.T.S.
HORIZ. N.T.S.
DATE 4/6/06

DRAWN BY MJK
CHECKED BY BDC
