


STAGE I QUANTITIES

70300220	TEMPORARY PAVEMENT MARKING - LINE 4"		
	LOCATION	COLOR	FOOT
	LT. STA. 18+04 - LT. STA. 34+56	WHITE	1653
	RT. STA. 18+28 - RT. STA. 23+96	WHITE	568
	RT. STA. 25+88 - RT. STA. 33+76	WHITE	788
	LT. STA. 4+02 - LT. STA. 8+87	WHITE	556
	LT. STA. 1+94 - RT. STA. 8+85	WHITE	750
			TOTAL 4315 FOOT
70300280	TEMPORARY PAVEMENT MARKING - LINE 24"		
	LOCATION	COLOR	FOOT
	RT. STA. 17+44	WHITE	12
	LT. STA. 34+66	WHITE	12
			TOTAL 24 FOOT

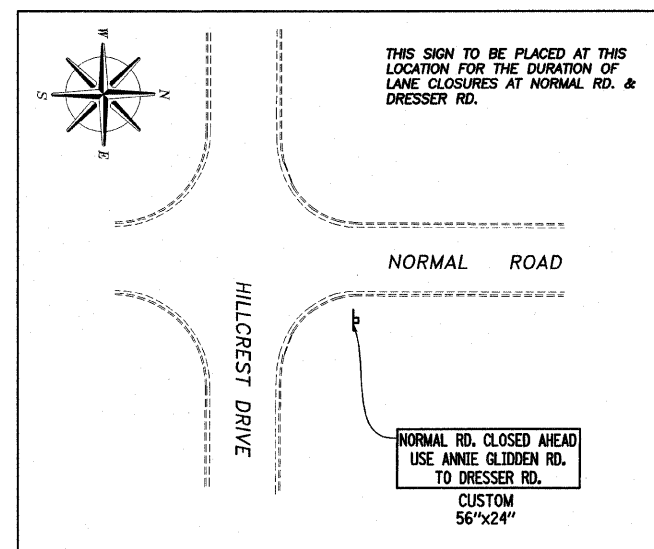

- WORK AREA
- SIGN
- TRAFFIC SIGNAL
- BARREL

**TRAFFIC CONTROL PLAN
NORMAL ROAD - STAGE I**

**DRESSER & NORMAL ROADS
SECTION 09-00175-00-SP
CITY OF DEKALB**
