

ROUTE NO.	SECTION NO.	TOTAL SHEETS
F.A.U. 6578 F.A.U. 6679	03-00019-1 1-PP	98
FED. ROAD DIST. NO.	COUNTY	PROJECT
	PEORIA	M-5093
ILLINOIS		
CONTRACT NO. 89389		

CONSTRUCTION STAGING (SUGGESTED)


THE CONTRACTOR WILL PERFORM ALL PHASE WORK BY CLOSING ONE LANE OF TRAFFIC WHEN NECESSARY IN ACCORDANCE WITH ILLINOIS DEPARTMENT OF TRANSPORTATION STANDARDS. DURING NON-WORKING HOURS BOTH LANES OF TRAFFIC WILL REMAIN OPEN. ACCESS WILL BE MAINTAINED TO ALL BUSINESSES AND SCHOOLS EXCEPT AS DIRECTED BY THE ENGINEER. DRAINAGE AND UTILITIES WILL BE MAINTAINED AT ALL TIMES EXCEPT TO MAKE NEW CONNECTIONS

PHASE 2 (HATCHED AREA)
 PFEIFFER ROAD EAST OF AIRPORT WILL BE OPENED.
 NORTHBOUND TRAFFIC ON AIRPORT ROAD WILL BE SHIFTED TO NEW PAVEMENT.
 TEMPORARY CULVERTS ON THE SOUTH SIDE OF WEST LEG OF PFEIFFER WILL BE INSTALLED (60 METER - SEE BELOW).
 INSTALL TEMPORARY AGGREGATE (150 MM THICK, FOR USE AS BASE COURSE) FOR TEMPORARY PAVEMENT.
 TEMPORARY BITUMINOUS PAVEMENT WILL BE BUILT ON SOUTH SIDE OF WEST LEG OF PFEIFFER (SEE TEMPORARY PAVEMENT QUANTITIES LISTED BELOW).
 FROM APPROXIMATE STA. 10+410 RT. TO STA. 10+160 RT. (853 SQ. METER).
 COST OF TEMPORARY ITEMS INCLUDES MATERIALS, PLACEMENT AND REMOVAL.

APPROXIMATE LOCATIONS OF TEMPORARY CULVERTS:
 STA. 10+201.460 RT. - 6 METER
 STA. 10+262.000 RT. - 8 METER
 STA. 10+296.270 RT. - 8 METER
 STA. 10+314.000 RT. - 10 METER
 STA. 10+322.370 RT. - 8 METER
 STA. 10+343.190 RT. - 13 METER
 STA. 10+388.285 RT. - 7 METER

PFEIFFER ROAD TEMPORARY PAVEMENT QUANTITIES (APPROXIMATELY 853 SQUARE METERS):
 PRIME COAT : 870 LITERS (3 APPLICATIONS)
 TEMPORARY BITUMINOUS : 427 METRIC TONS (200 MM THICKNESS)
 TEMPORARY AGGREGATE BASE COURSE : 320 METRIC TONS (150 MM THICKNESS)

TEMPORARY PAVEMENT MARKING QUANTITY THIS PHASE - 316 METER
 COST TO REMOVE ANY EXISTING OR TEMPORARY PAVEMENT MARKINGS WILL BE CONSIDERED INCLUDED IN THE CONTRACT.
 UNIT COST FOR TEMPORARY PAVEMENT MARKINGS

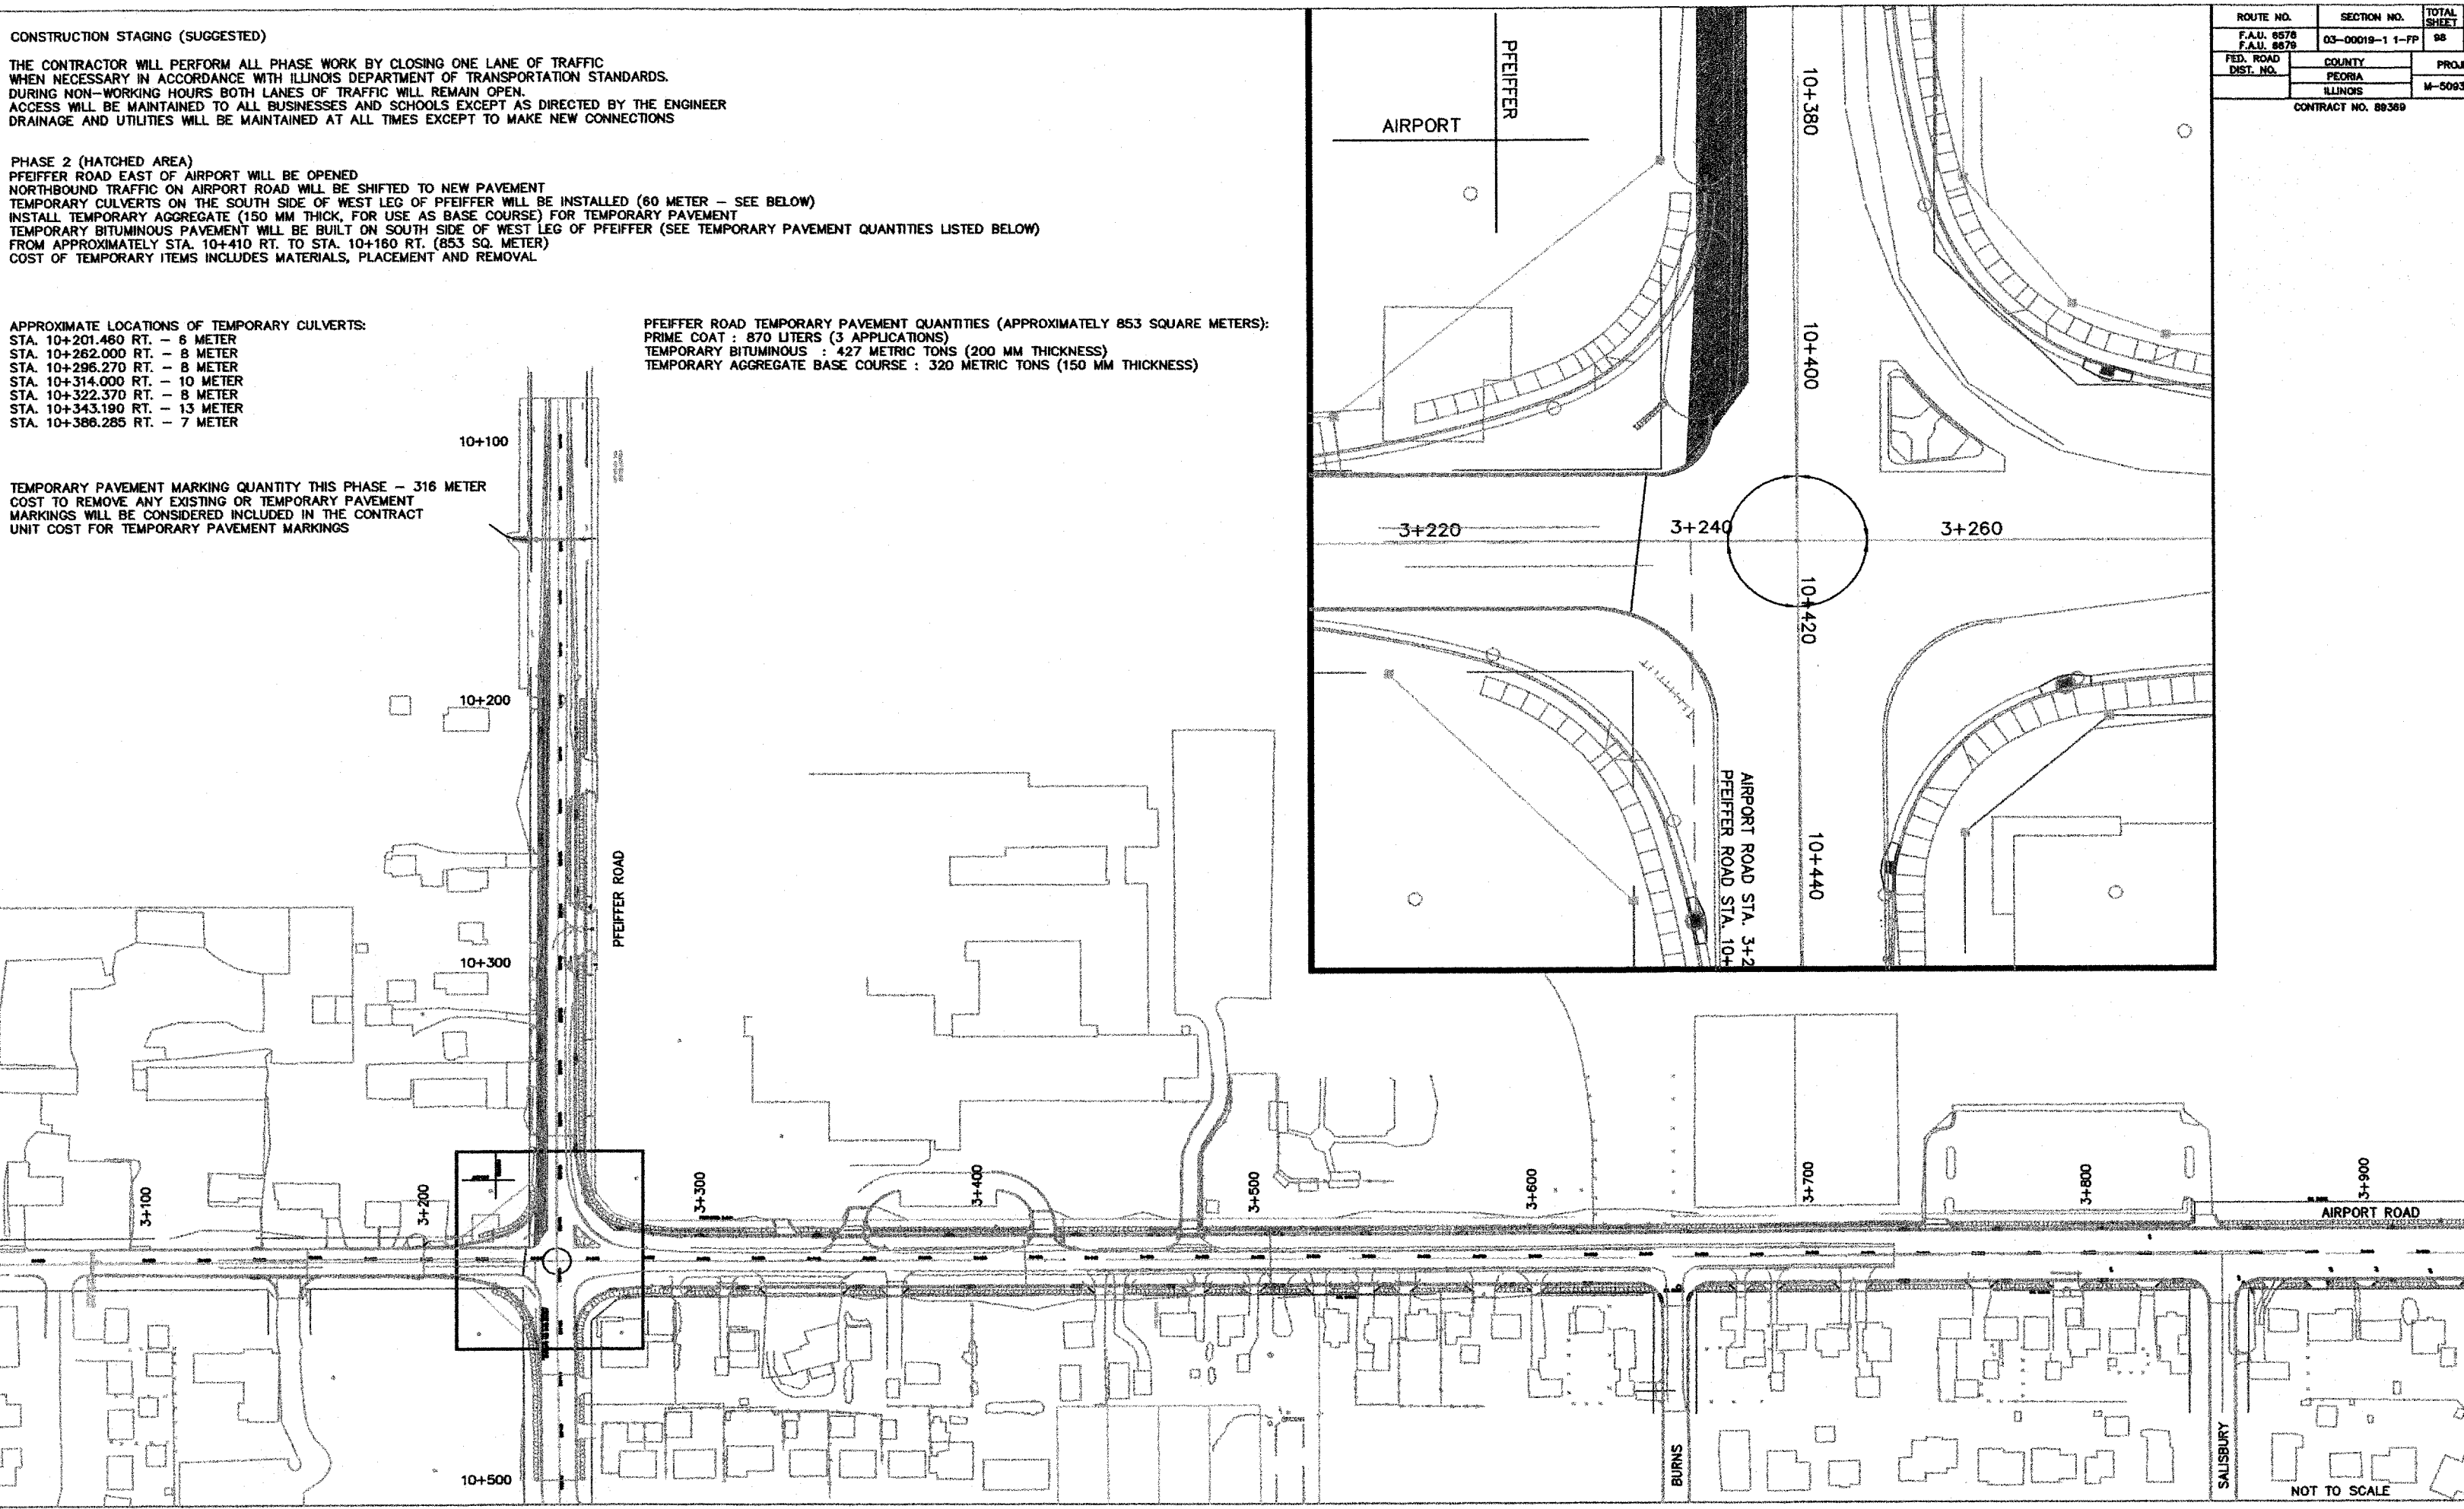

NOT TO SCALE
