
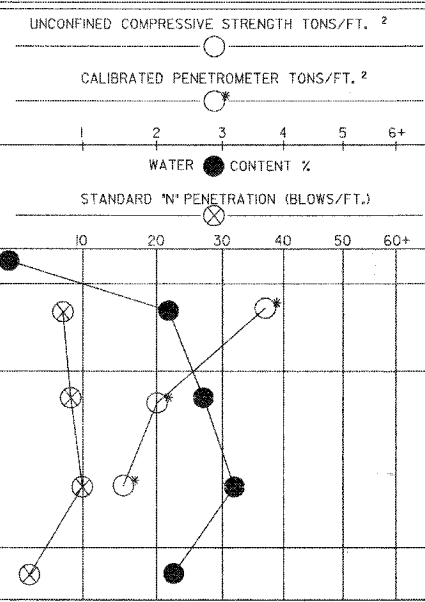



F.A.U. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
2552	00-00114-00-PV	DuPAGE	563	563
STA.		TO STA.		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		
CONTRACT NO. 63024				

LOG OF BORING NO. B-25				
CLIENT T.Y. Lin International/Bascor			STATION AND OFFSET-WASHINGTON STREET Station: 433+34 Offset: 11' Left	
PROJECT LOCATION 75th Street and Washington Street Naperville, Illinois			PROJECT DESCRIPTION Subsurface Investigation for the 75th Street and Washington Street Intersection Improvements	
DEPTH (ft.) BELOW GROUND SURFACE	SAMPLE NUMBER	SAMPLE TYPE	SAMPLE DISTANCE SAMPLE RECOVERY	DESCRIPTION OF MATERIAL
				GROUND SURFACE ELEVATION 665.2
	1	QS		12.0' ASPHALT
	2	SS		SILTY LOAM-dark brown to black-loose (A-4) Possible Fill
5.0	3	SS		SILTY CLAY to SILTY CLAY LOAM-brown and gray-stiff (A-4/A-6) Wet
	4	SS		
10.0	5	SS		SILTY LOAM to SILT-brown-loose (A-4) 665.2
END OF BORING				
WATER LEVEL OBSERVATIONS			 <b>O'BRIEN &amp; ASSOCIATES, INC.</b> CONSULTING ENGINEERS <small>235 E. DAVIS ST., ARLINGTON HTS., IL 60005          (847) 398-1441 • FAX (847) 398-2376</small>	
W.L.	Dry WD		BORING STARTED July 1, 2002	
W.L.	Dry AB		BORING COMPLETED July 1, 2002	
W.L.			RIG CME-75	FOREMAN RH
W.L.			DRAWN RWC	APPROVED DOB
			JOB No. 01252	SHEET 1 OF 1



<table border="1" style="width: 100%;"> <thead> <tr> <th colspan="2">REVISIONS</th> </tr> <tr> <th>NAME</th> <th>DATE</th> </tr> </thead> <tbody> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> </tbody> </table>	REVISIONS		NAME	DATE																					INTERSECTION IMPROVEMENT WASHINGTON STREET - 75th STREET  <b>BORING LOG</b> <b>B-25</b>	City of  <b>Naperville</b>
REVISIONS																										
NAME	DATE																									
CONSULTANT <b>TYLIN INTERNATIONAL</b>		SHEET NO. DRAWN: CHECKED: APPROVED: DATE: APRIL 11, 2008 SCALE: JOB NO.: P-91-494-00 PROJECT NO.: M-CMM-7003 (985)																								

P:\60241\1\60241\borings\B-25.dwg 10:46:03 AM 4/11/2008
