
NOTES: PRESTAGE WORK SHALL INCLUDE CONSTRUCTION THE TEMPORARY WIDENING AND GUARDRAIL ON THE EAST SIDE OF IL 78 AS SHOWN ON THE STAGING TYPICAL SECTION AND STAGING PLANS. THIS WORK SHALL BE DONE USING TRAFFIC CONTROL AND PROTECTION STANDARD 701326. THE THICKNESS AND COMPSITION OF THE TRMPORARY PAVEMENT IS AS SHOWN IN THE SPECIAL PROVISIONS. DURING STAGE 1 AND 2 USE STANDARD 701321 FOR TRAFFIC CONTROL AND PROTECTION LAY HMA SURFACE COURSE AFTER STAGE 2 USING 701201 FOR TRAFFIC CONTROL AND PROTECTION TEMPORARY PAINT PAVEMENT MARKING LINE 4" IMPACT ATTENUATORS, TEMPORARY (NON - REDIRECTIVE), TEST LEVEL 3

STA 914+04 12' RT

\STA 914+04

STA 913+76.58 15.63' RT

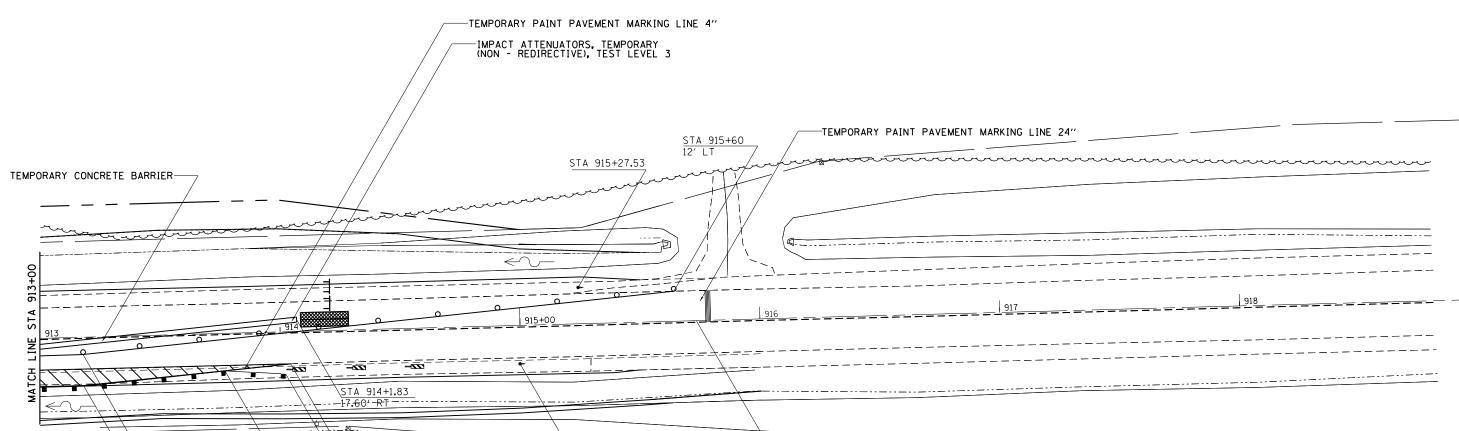

STA 915+73.46 0.00' LT

STA 915+02.58

= TEMPORARY PAVEMENT

= TEMPORARY GUARD RAIL

STA 913+17.59 \ 19.22' RT

= PATCH, CLASS C

= IMPACT ATTENUATOR

O = DRUM WITH STEADY BURNING BI-DIRECTIONAL LIGHT

<u>STA 913+17.59</u>

= TYPE III BARRICADE WITH FLASHING LIGHTS

●── = TRAFFIC SIGNAL

Ī	FILE NAME =	USER NAME = rundbladerr	DESIGNED -	REVISED -		DATS			STAGING PLANS			SECTION	COUNTY CHEETS	SHEET
	c:\pw_work\pwidot\rundbladerrr\d0232736	.D201310-sht-staging.dgn	DRAWN -	REVISED -	STATE OF ILLINOIS	11 70					650	104T-3	JO DAVIESS 97	38
		PLOT SCALE = 40.0000 '/ in.	CHECKED -	REVISED -	DEPARTMENT OF TRANSPORTATION	SCALE: SHEET OF SHEETS STA. TO STA.						CONTRACT NO. 64	4F 74	
	Default	PLOT DATE = Thu Oct 10 13:44:19 2013	DATE -	REVISED -							ILLINOIS FED. A	FED. AID PROJECT		
