



LOCAL RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
M.S. 1040	05-00010-00-PV	HENRY	136	32
STA. 81+00		TO STA. 85+98.54		
FED. ROAD DIST. NO. -		ILLINOIS	FED. AID PROJECT	



SHIVE HATTERY
 Cedar Rapids, IA · Iowa City, IA · Des Moines, IA
 Moline, IL · Bloomington, IL · Chicago, IL
 SHIVE-HATTERY, INC. 1701 RIVER DRIVE, SUITE 200 MOLINE, IL 61265
 PHONE (309) 764-7650 FAX (309) 764-8616
 http://www.shive-hattery.com
 ILLINOIS FIRM NUMBER: 184-000214

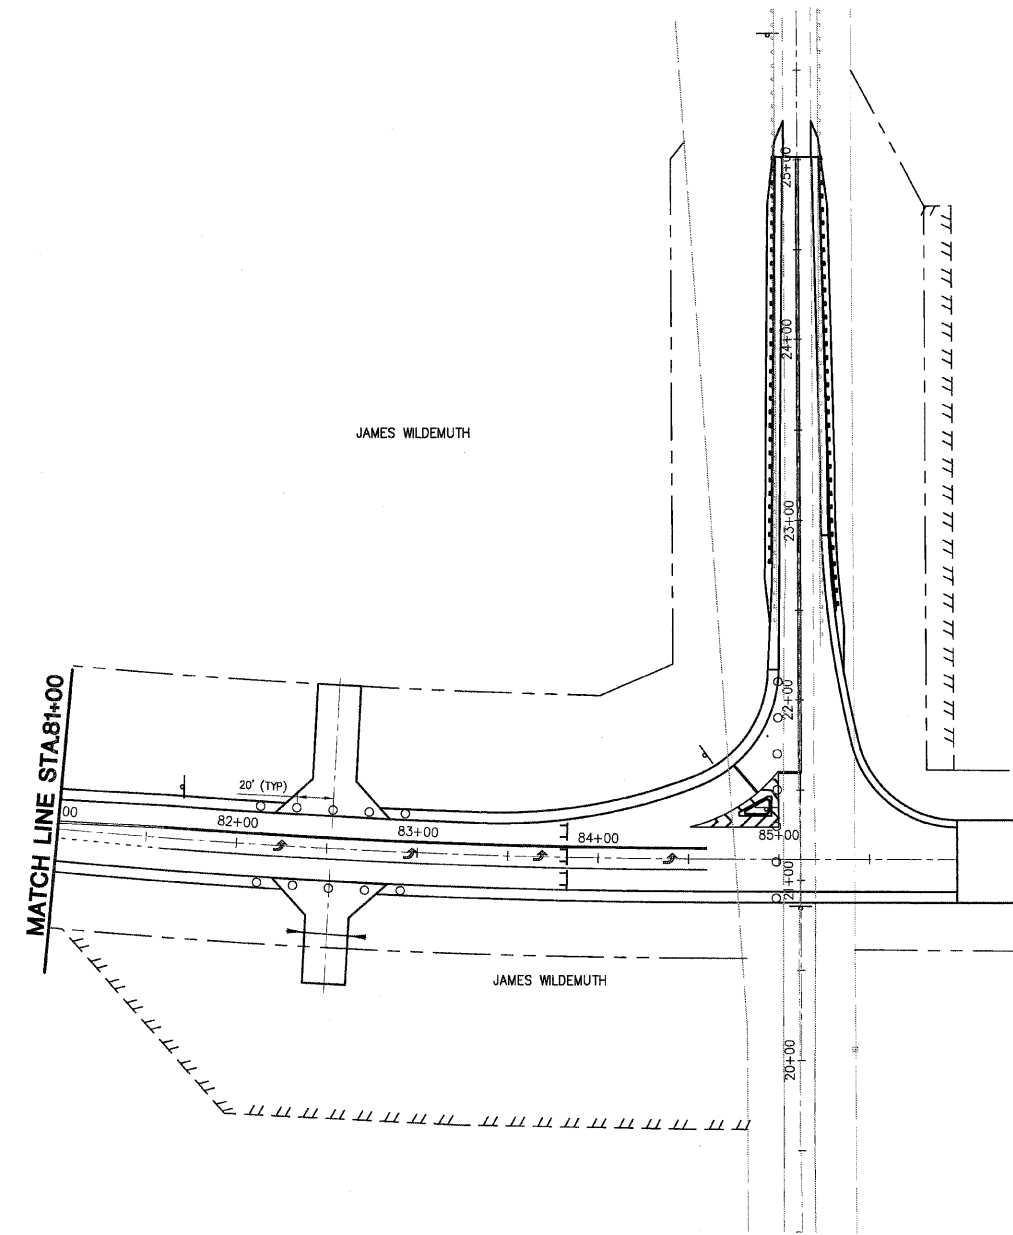

LEGEND

- DRUM OR BARRICADE
- ⌊ TYPE III BARRICADE

NOTES

- CONSTRUCT 2900E ROADWAY EMBANKMENT ONE SIDE AT A TIME WHILE MAINTAINING NORMAL TRAFFIC FLOW ON 2900E AND PARTIOT WAY.
- CLOSE 2900E USING BLR 21--8. CONSTRUCT PCC INTERSECTION FROM STATION 20+93.56 TO STATION 22+91.93. LIMIT ROAD CLOSURE TO TWO WEEKS MAXIMUM. COORDINATE WITH THE VILLAGE OF ANNAPAN PRIOR TO CLOSURE.
- CONSTRUCT PAVEMENT WIDENING AND HOT MIX ASPHALT OVERLAY FROM STATION 20+93.56 TO STATION 25+01.56 USING STANDARD 701326-03 AND STANDARD 701201-03.

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL

SCALE: VERT. _____
 HORIZ. _____
 DATE: 03-11-09

DRAWN BY MAC
 CHECKED BY PMH

SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL

PLOT DATE = #DATE#
 PLOT SCALE = #SCALE#
 USER NAME = #USER#
