


DATE	BY
SURVEYED	PLOTTED
NOTED	AREAS CHECKED
NO.	


DATE	BY
SURVEYED	PLOTTED
NOTED	AREAS CHECKED
NO.	

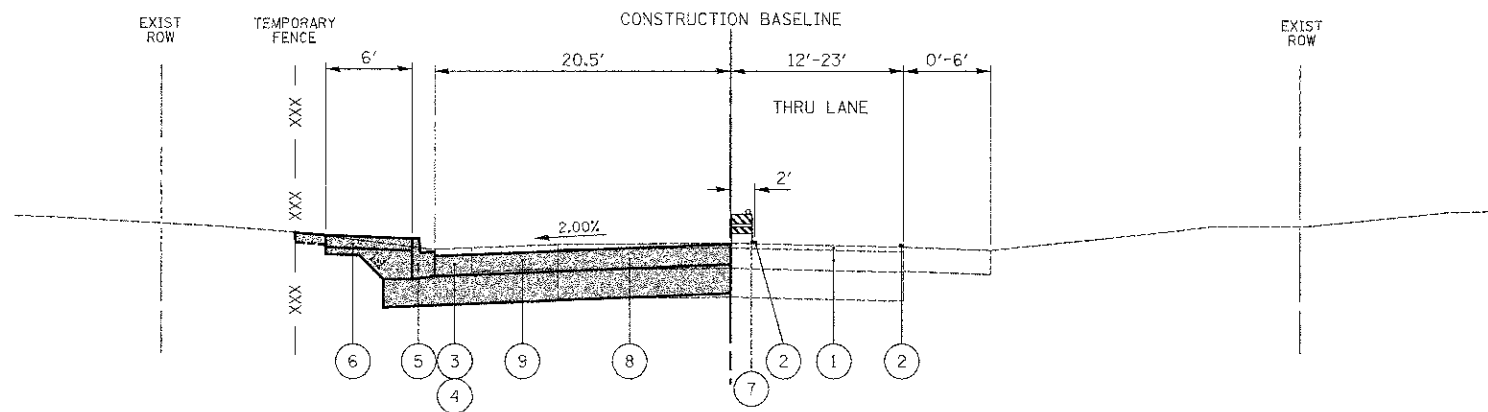

TYPICAL SECTION WASHINGTON STREET - STAGE I
STA 200+00.00 TO STA 52+90.00

- PROPOSED LEGEND**
- 1 EXISTING BITUMINOUS PAVEMENT
 - 2 PROPOSED TEMPORARY PAVEMENT MARKING (4" WHITE LINE)
 - 3 PROPOSED HOT-MIX ASPHALT BINDER COURSE, IL-19.0, N70
 - 4 PROPOSED AGGREGATE SUBGRADE, 12"
 - 5 PROPOSED COMBINATION CONCRETE CURB AND GUTTER, TYPE B-6.12
 - 6 PROPOSED SIDEWALK
 - 7 TYPE II BARRICADE (NON-METALLIC) W/ STEADY-BURN LIGHT
 - 8 PAVEMENT REMOVAL
 - 9 GRAVEL SHOULDER REMOVAL - PAID FOR AS "EARTH EXCAVATION"

PERMANENT CONSTRUCTION DURING STAGE
(SEE STAGES OF CONSTRUCTION PLAN SHEETS)

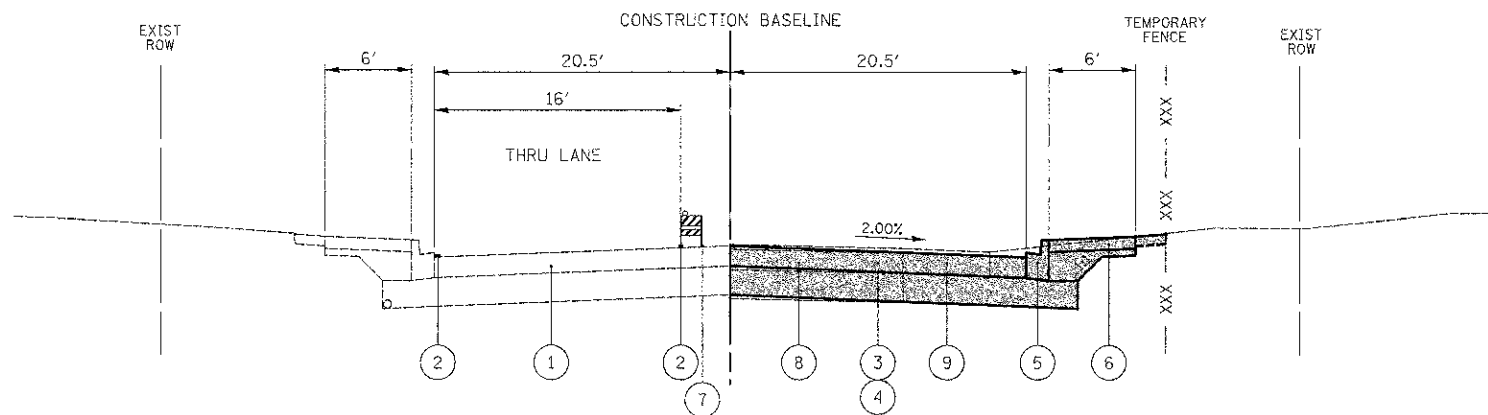

TYPICAL SECTION WASHINGTON STREET - STAGE II
STA 200+00.00 TO STA 52+90.00

THE CONTRACTOR SHALL CONTACT THE DISTRICT ONE TRAFFIC CONTROL SUPERVISOR AT (847) 705-4470 A MINIMUM OF 72 HOURS IN ADVANCE OF BEGINNING WORK.

PRE-STAGE I (NOT ILLUSTRATED)	STAGE I	STAGE 2	STAGE 3 (NOT ILLUSTRATED)
<ol style="list-style-type: none">ERECT ALL ADVANCED CONSTRUCTION SIGNING.IMPLEMENT SOIL & SEDIMENT EROSION CONTROL PLAN AND PROVIDE TEMPORARY FENCE WHERE PERIMETER EROSION CONTROL BARRIER IS NOT SHOWN.TURN OFF AND COVER TRAFFIC SIGNALS AT THE CEDAR LAKE ROAD AND WASHINGTON STREET, AND INSTALL TEMPORARY TRAFFIC SIGNALS AND LIGHTING.REMOVE TREES AND RELOCATE TRAFFIC SIGNS WHERE NECESSARY.CONSTRUCT UTILITIES ON THE SOUTH SIDE OF WASHINGTON STREET THAT ARE CROSSING THE ONE-WAY TRAFFIC LANE AS SHOWN IN SOC STAGE I UTILIZING IDOT STANDARD 701301.MILL PAVEMENT ON CEDAR LAKE ROAD, MAINTAINING TRAFFIC PER STANDARD 701306, AND PROVIDE TEMPORARY RAMPS.REMOVE CONFLICTING PAVEMENT MARKINGS AND PLACE TEMPORARY MARKINGS, ERECT BARRICADES AND TEMPORARY TRAFFIC SIGNS AND SHIFT TRAFFIC.	<ol style="list-style-type: none">REMOVE EXISTING PAVEMENT AND CURB AND GUTTER ON THE NORTH SIDE OF WASHINGTON STREET.INSTALL DRAINAGE STRUCTURES, MAIN STORM SEWER, & STORM SEWER LATERALS ON NORTH SIDE OF WASHINGTON STREET AND ACROSS CEDAR LAKE ROAD.CONSTRUCT BASE COURSE, BINDER COURSE, CURB AND GUTTER, DRIVEWAYS, AND SIDEWALKS ON NORTH SIDE OF WASHINGTON STREET AND THE WEST SIDE OF CEDAR LAKE ROAD.CONSTRUCT BASE COURSE AND BINDER COURSE IN THE TRIANGULAR AREA NORTH OF PROPOSED MEDIAN ISLAND AT THE INTERSECTION OF WASHINGTON STREET AND CEDAR LAKE ROAD.PLACE PERMANENT LANDSCAPING ON NORTH SIDE OF WASHINGTON STREET.REMOVE CONFLICTING PAVEMENT MARKINGS AND PLACE TEMPORARY MARKINGS, RELOCATE BARRICADES, ADJUST TEMPORARY SIGNING, TEMPORARY TRAFFIC SIGNALS, AND SHIFT TRAFFIC ON WASHINGTON STREET AND CEDAR LAKE ROAD FOR STAGE II CONSTRUCTION.BEGIN INSTALLATION OF PERMANENT TRAFFIC SIGNALS.	<ol style="list-style-type: none">REMOVE EXISTING PAVEMENT AND CURB AND GUTTER ON THE SOUTH SIDE OF WASHINGTON STREET.CONSTRUCT ALL REMAINING STORM SEWERS ON THE SOUTH SIDE OF WASHINGTON STREET.CONSTRUCT BASE COURSE, BINDER COURSE, CURB AND GUTTER, DRIVEWAYS, SIDEWALKS, AND BIKEPATH ON SOUTH SIDE OF WASHINGTON STREET AND EAST SIDE OF CEDAR LAKE ROAD.PLACE PERMANENT LANDSCAPING ON SOUTH SIDE OF WASHINGTON STREET.REMOVE CONFLICTING PAVEMENT MARKINGS AND PLACE SHORT-TERM PAVEMENT MARKINGS, REMOVE BARRICADES, ADJUST TEMPORARY TRAFFIC SIGNALS, AND SHIFT TRAFFIC ON WASHINGTON STREET AND CEDAR LAKE ROAD FOR STAGE III CONSTRUCTION.	<ol style="list-style-type: none">PLACE SURFACE COURSE TO FINISHED GRADE ON WASHINGTON STREET AND CEDAR LAKE ROAD, MAINTAINING TRAFFIC PER STANDARD 701501, AND PLACE SHORT-TERM PAVEMENT MARKINGS AS REQUIRED.COMPLETE AND ACTIVATE ALL PERMANENT TRAFFIC SIGNAL INSTALLATIONS AND REMOVE TEMPORARY SIGNALS.REMOVE ALL CONFLICTING PAVEMENT MARKINGS, PLACE PERMANENT PAVEMENT MARKINGS AND PERMANENT SIGNING, AND REMOVE ALL TEMPORARY TRAFFIC SIGNS.COMPLETE ALL REMAINING LANDSCAPING AND CLEAN-UP WORK.



450 E Devon Ave, Suite 300
Itasca, Illinois 60143
Tel: 630.773.3900 Fax: 630.773.3975
www.civiltechinc.com

DESIGNED - PK	REVISED -
DRAWN - JRR	REVISED -
CHECKED - RTM	REVISED -
DATE - 1/7/2013	REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

NO SCALE

STAGES OF CONSTRUCTION TYPICAL SECTIONS

SHEET NO. 1 OF 1 SHEETS

F.A.U. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
0187	05-00121-07-WR	LAKE	223	84
CONTRACT NO. 63765				
FED. ROAD DIST. NO. 1 ILLINOIS FED. AID PROJECT				
