

ROUTE NO.	SECTION NO.	TOTAL SHEET
F.A.U. 8578	03-00019-1 1-PP	98
F.A.U. 8679		
FED. ROAD DIST. NO.	COUNTY	PROJ. NO.
	PEORIA	M-5063
	ILLINOIS	
CONTRACT NO. 89369		



**CONSTRUCTION STAGING (SUGGESTED)**

THE CONTRACTOR WILL PERFORM ALL PHASE WORK BY CLOSING ONE LANE OF TRAFFIC WHEN NECESSARY IN ACCORDANCE WITH ILLINOIS DEPARTMENT OF TRANSPORTATION STANDARDS. DURING NON-WORKING HOURS BOTH LANES OF TRAFFIC WILL REMAIN OPEN. ACCESS WILL BE MAINTAINED TO ALL BUSINESSES AND SCHOOLS EXCEPT AS DIRECTED BY THE ENGINEER. DRAINAGE AND UTILITIES WILL BE MAINTAINED AT ALL TIMES EXCEPT TO MAKE NEW CONNECTIONS

**PHASE 1A (HATCHED AREA)**  
INSTALL TEMPORARY BITUMINOUS RAMPS (SEE TEMPORARY PAVEMENT QUANTITIES LISTED BELOW)

TEMPORARY BITUMINOUS RAMPS AT VARIOUS LOCATIONS (APPROXIMATELY 1429 SQUARE METERS TOTAL):  
PRIME COAT : 1944 LITERS (4 APPLICATIONS)  
TEMPORARY BITUMINOUS : 1071 METRIC TONS (300 MM THICKNESS)

PLEASE NOTE THAT THE ABOVE QUANTITY INCLUDES LOCATIONS SHOWN IN PHASE 1A, PHASE 4A, PHASE 5A, PHASE 6A, AND PHASE 7A

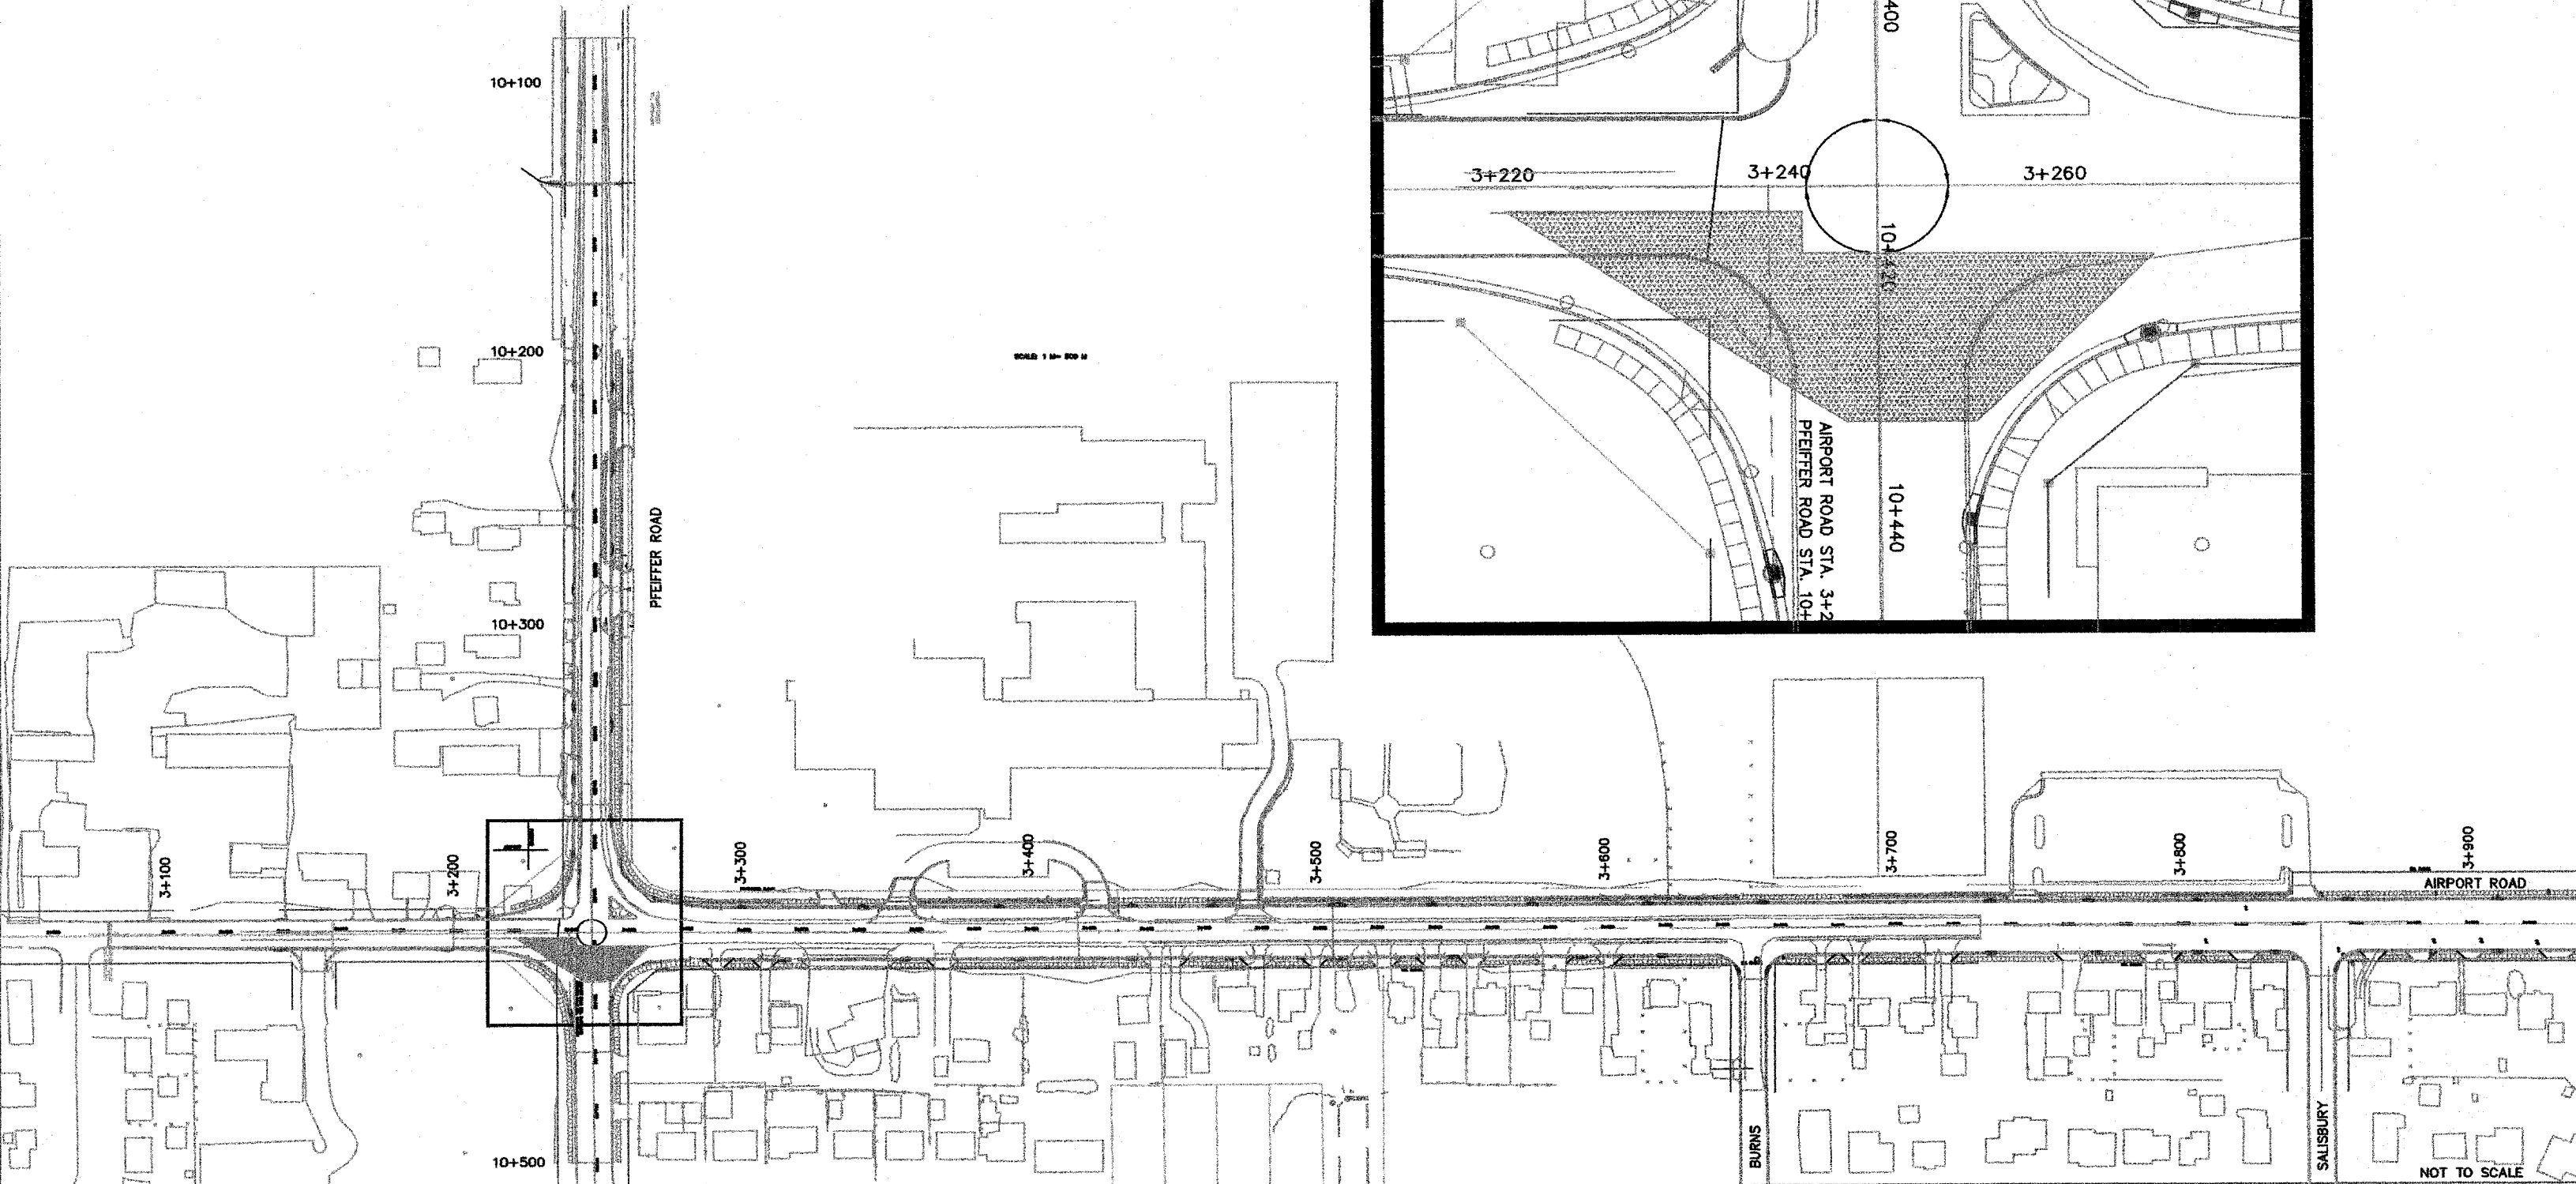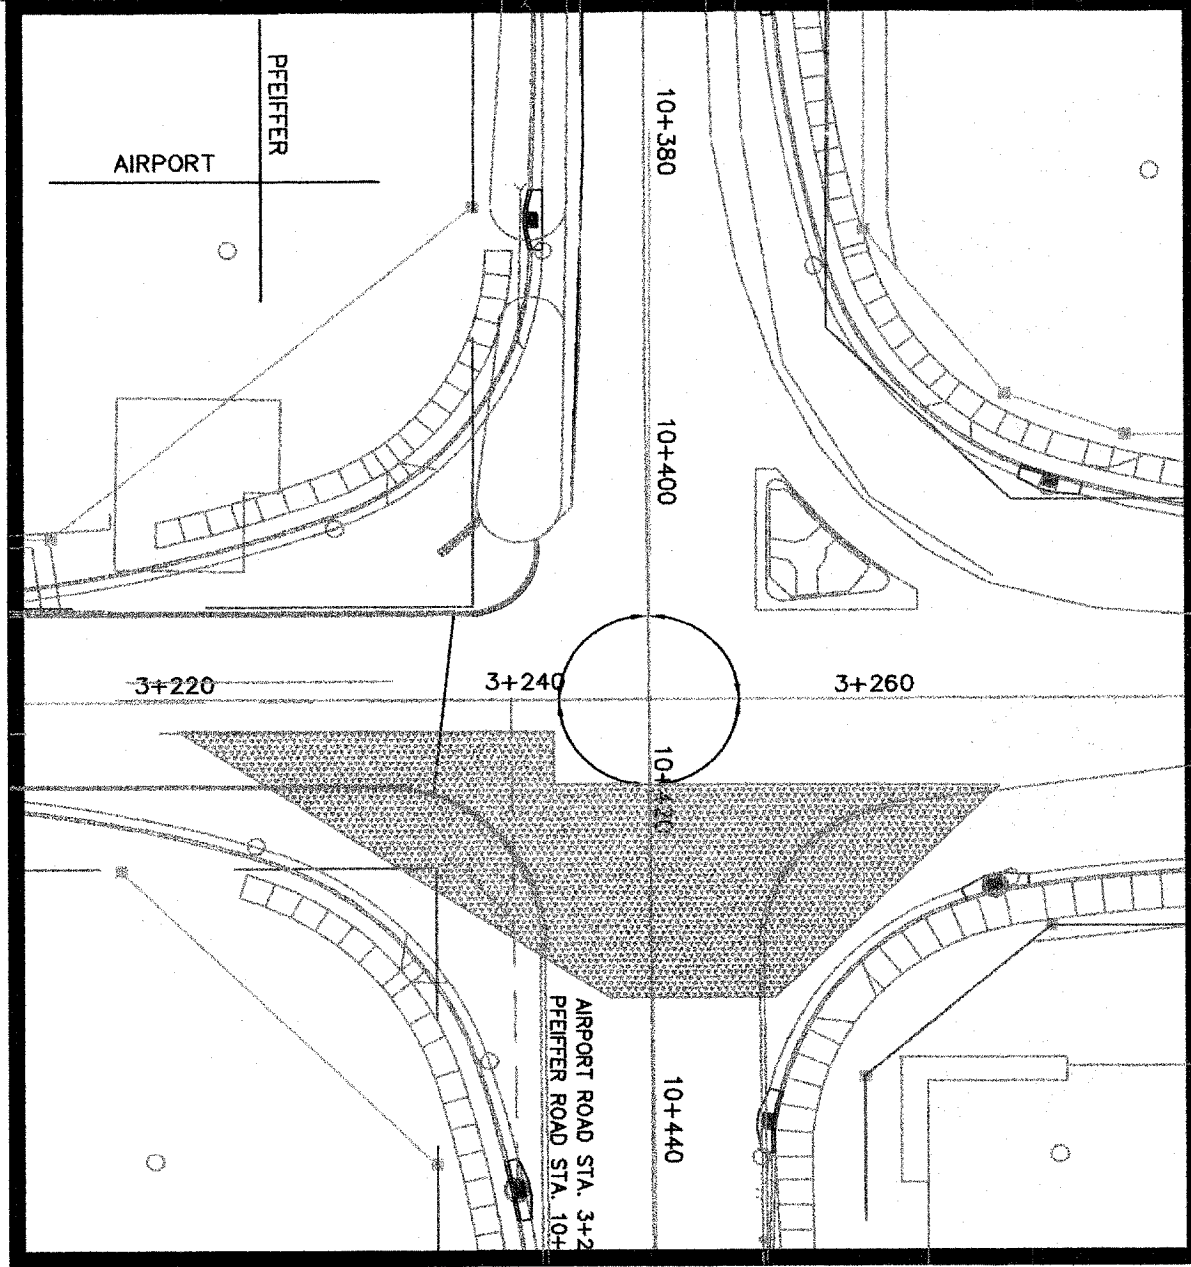

NOT TO SCALE
