


TYPE II BARRICADE, DRUM OR VERTICAL BARRICADE WITH STEADY BURN MONO-DIRECTIONAL LIGHT

TYPE III BARRICADE WITH FLASHING LIGHT

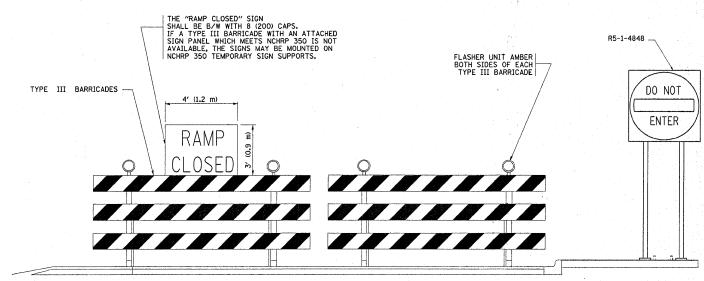

DETAIL FOR REQUIRED BARRICADES & SIGNS

RAMP CLOSURE ADVANCE WARNING SIGN




BLACK LEGEND ON ORANGE REFLECTORIZED BACKGROUND

1 (25) BORDER

THESE SIGNS ARE REQUIRED ON ALL THE EXIT GUIDE SIGNS FOR THE CLOSED EXIT RAMPS.

RAMP CLOSURE ADVANCE INFORMATION SIGN



THESE SIGNS ARE REQUIRED ON BOTH SIDES OF THE RAMP, MINIMUM OF 1 WEEK IN ADVANCE OF THE CLOSURE,

GENERAL NOTES:

- (1) CONES MAY BE SUBSTITUTED FOR DRUMS OR TYPE II
 BARRICADES DURING DAY OPERATIONS. CONES SHALL BE
- ② STEADY BURN LIGHTS WILL NOT BE REQUIRED FOR DAY OPERATIONS.
- $\ensuremath{\mathfrak{J}}$ a flagger shall be positioned at each closed ramp that is open to construction vehicles.
- 4 ALL ROUTE MARKERS AND TRAILBLAZER ASSEMBLIES WHICH DIRECT MOTORISTS TO A CLOSED ENTRANCE RAMP SHALL BE COVERED.
- (5) THE SIGNING AND BARRICADING WHICH IS REQUIRED BY THIS DETAIL SHALL BE INCLUDED IN THE COST OF TRAFFIC CONTROL AND PROTECTION (EXPRESSWAYS).

- 6 AUTHORIZATION FROM THE DISTRICT'S BUREAU OF TRAFFIC IS REQUIRED FOR ALL RAMP CLOSURES.
- (T) THE RAMP CLOSURE ADVANCE INFORMATION SIGNS SHALL BE ERECTED IF THE CLOSURE TIME EXCEEDS TWENTY- FOUR 24 HOURS. ADDITIONAL ADVANCE WARNING SIGNS ON EXIT GUIDE SIGNING WILL BE REQUIRED FOR EXIT RAMP CLOSURES THAT EXCEED TWENTY FOUR 24 HOURS IN LENGTH.
- (8) ROAD CONSTRUCTION AHEAD SIGNS MAY BE OMITTED WHEN THIS DETAIL IS USED IN CONJUNCTION WITH OTHER TRAFFIC CONTROL THAT ALREADY INCLUDES A ROAD CONSTRUCTION AHEAD SIGN.
- ARTERIAL ROAD CONSTRUCTION AHEAD SIGNS MAY BE OMITTED ON CLOSURES LESS THAN 24 HOURS IN DURATION.

ALL DIMENSIONS ARE IN INCHES (MILLIMETERS)
UNLESS OTHERWISE SHOWN.

FILE NAME =	USER NAME = rosienejm	DESIGNED - DWS	REVISED - DWS/JAF 12-0		STATE OF ILLINOIS	FREEWAY ENTRANCE AND EXIST RAMP CLOSURE DETAILS		F.A. I. RTE.	SECTION	COUNTY TO	OTAL SHEET HEETS NO.	
c:\pw_work\PWIDOT\ROSIEREJM\d0184552\D1	stStd.dgn	DRAWN -	REVISED - JAF 02-06					55	99-1-TWS-I-5	WILL :	13 13	
	PLOT SCALE = 50.0000 '/ IN.	CHECKED -	REVISED - SPB 01-07		DEPARTMENT OF TRANSPORTATION				_	TC-08	CONTRACT NO	io. 60K43
	PLOT DATE = 3/20/2010	DATE - 02-83	REVISED - SPB 12-09			SCALE: NONE	SHEET NO. 1 OF 1 SHEETS STA.	TO STA.	FED. ROAD (DIST. NO. 1 ILLINOIS FED. A	AID PROJECT	
