


3

2

WORK ZONE PUBLIC INFORMATION SIGN

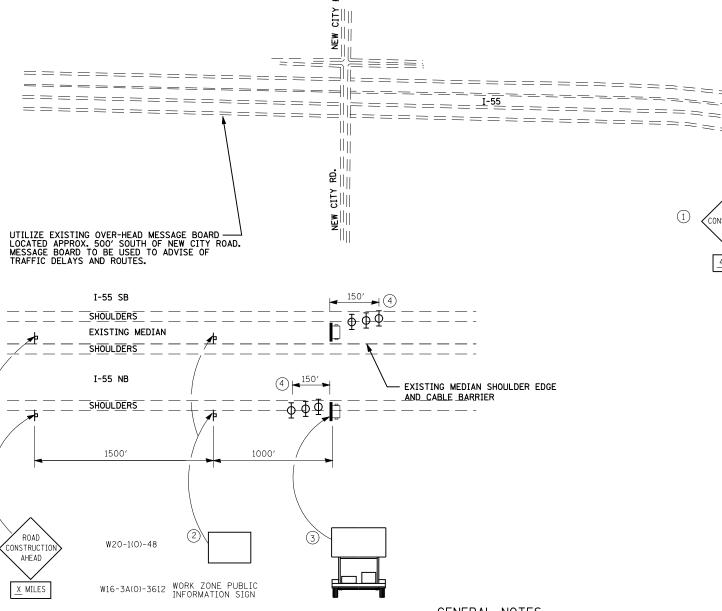

GENERAL NOTES

STANDARD 701400-03 IS USED WHERE AT ANY TIME A LANE IS CLOSED ON A FREEWAY/EXPRESSWAY. WHEN THE LEFT LANE IS CLOSED, LEFT LANE CLOSED SIGNS SHALL BE SUBSTITUTED FOR THE RIGHT LANE CLOSED SIGN.

SYMBOLS

ARROW BOARD

PORTABLE CHANGEABLE MESSAGE SIGN

TYPE II BARRICADE, DRUM, OR VERTICAL BARRICADE WITH MONODIRECTIONAL FLASING LIGHT

SEE STANDARD 701400-03 FOR COMPLETE SIGN DETAILS

- ① THE ROAD CONSTRUCTION AHEAD SIGN SHALL BE LOCATED 3 TO 5 MILES IN ADVANCE OF THE PROJECT LIMITS.
- THE MESSAGE AND SIZE OF THE WORK ZONE PUBLIC INFORMATION SIGN SHALL BE AS SPECIFIED BY THE DEPARTMENT.
- 3 SEE SPECIAL PROVISIONS FOR TRAFFIC WARNING MESSAGES
- (4) THREE, TYPE II BARRICADES, DRUMS, OR VERTICAL BARRICADES AT 50° CENTERS.

FILE NAME =	USER NAME = laughlinrl	DESIGNED -	LLQ	REVISED -						F.A.I RTF.	SECTION	COUNTY TOTAL SHEET NO.
:\pw_work\PWIDOT\LAUGHLINRL\dØ131883\D672A64_24-28_MOT.dgn		DRAWN - JJS		REVISED -	STATE OF ILLINOIS	I-55 ADVANCED WARNING & MAINTENANCE OF TRAFFIC			55	(84-3HB-6)BR	SANGAMON 90 24	
	PLOT SCALE = 400.0000 '/ IN.	CHECKED -	MTM	REVISED -	DEPARTMENT OF TRANSPORTATION					S	.N. 084-0028	CONTRACT NO. 72A64
	PLOT DATE = May-09-2009 11:31:50AM	DATE -	MARCH 5,2009	REVISED -	SC		SHEET NO. 1 OF 5 SHEETS	STA.	TO STA.		DIST. NO. 6 ILLINOIS FED. AI	

1

CONSTRUCTION

AHEAD

4 MILES

W20-1(0)-48

W16-3A(0)-3612
