


CALENDAR OF CONSTRUCTION WORK

PHASE	YEAR	WORK DATES		CONSTRUCTION WORK
		FROM	TO	
PHASE I	2009	APRIL 1	AUG. 15	INSTALLATION OF UTILITY SERVICE DROP DOWNS FOR THE SE QUADRANT AT THE CORNER GARDEN. EXCAVATION AND PLACEMENT OF POROUS GRANULAR MATERIAL, PLANTING MIX, AND GEOTECHNICAL FABRIC, (ALL CORNER GARDENS). INSTALLATION OF WATER SERVICE, IRRIGATION SYSTEMS AND ALL ASSOCIATED HARDSCAPE ITEMS FOR THE GATEWAYS AND CORNER GARDENS.
		MAY 1	SEPT. 15	INSTALLATION OF ALL WOODY PLANTS. WOODY PLANTS MUST BE CONTAINER OR DUG WHILE DORMANT AND MAINTAINED PROPERLY UNTIL PLANTED. ALL WOODY PLANTS MUST BE INSTALLED PRIOR TO PERENNIALS.
		AUG. 15	SEPT. 15	INSTALL PERENNIAL PLANTS AND MULCH AFTER ALL WOODY PLANTS HAVE BEEN INSTALLED.
		OCT. 1	OCT. 31	INSTALL BULBS.
PHASE I	2009	OCT. 31		CERTIFICATION TO THE BUREAU OF MAINTENANCE THAT ALL PLANTS HAVE BEEN INSTALLED AND ARE IN A LIVE HEALTHLY CONDITION AND ELIGIBLE FOR A APRIL 16 - APRIL 23, 2010 PERIOD OF ESTABLISHMENT INSPECTION.
PHASE	YEAR	WORK DATES		CONSTRUCTION WORK
		FROM	TO	
PHASE II	2010	MARCH 2	APRIL 16	PERIOD OF ESTABLISHMENT PLANT CARE REQUIRED FOR ALL PLANTS. (WEEDING, WATERING, OR OTHER WORK WHICH IS NECESSARY TO MAINTAIN HEALTH AND SATISFACTORY APPEARANCE OF THE PLANTING IS INCLUDED IN THE COST OF THE CONTRACT).
		APRIL 16	APRIL 23	PERIOD OF ESTABLISHMENT INSPECTION.
		APRIL 23	MAY 1	INSTALLATION OF ALL REQUIRED REPLACEMENT PLANTS, AND ALL REQUIRED CLEAN UP OF ALL PLANT BEDS SHALL BE COMPLETED BY THIS DATE.
PHASE II	2010	MAY 1		COMPLETION DATE
	2010	MAY 17		FINAL INSPECTION DATE

QUADRANT NOMENCLATURE

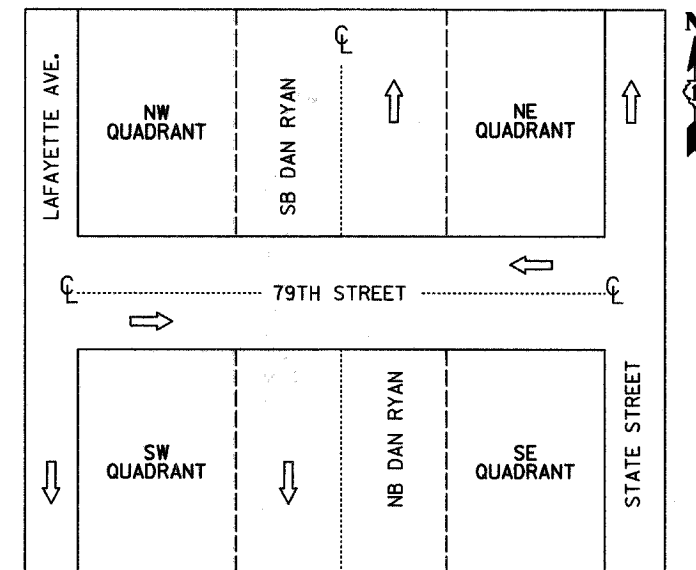

IDOT HOT-MIX ASPHALT MIXTURE REQUIREMENTS

ITEM	AC TYPE	AIR VOIDS
PAVEMENT REMOVAL AND REPLACEMENT		
HOT-MIX ASPHALT SURFACE COURSE, MIX "D", N TO 1 1/2"	PG 64-22	4%@70Gyr
LEVELING BINDER (MACHINE METHOD), N TO, 1 1/2"	PG 64-22/58-22	4%@70Gyr

THE UNIT WEIGHT USED TO CALCULATE ALL HMA SURFACE MIXTURE QUANTITIES IS 112/SQ YD/IN. USE 135 LB/SQ YD/IN. IF USING A SMA MIX.

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 94 (DAN RYAN EXPRESSWAY)
CALENDAR OF CONSTRUCTION, QUADRANT
NOMENCLATURE, AND HOT-MIX ASPHALT
MIXTURE REQUIREMENTS

SCALE: NONE
DATE: MAY 1, 2008

DRAWN BY: AMB
CHECKED BY: TGB
