

**MAINTENANCE OF TRAFFIC STAGE 1B (THIS SHEET)**

**SEQUENCE OF CONSTRUCTION**

1. EXISTING EDGE OF PAVEMENT SHALL BE MILLED ALONG WIDENING AS REQUIRED BY THE ENGINEER TO MEET THE DROP-OFF REQUIREMENTS.
2. REMOVE EXISTING STRIPING.
3. PLACE TEMPORARY STRIPING TO MAINTAIN SHIFTED TRAFFIC.
4. WIDEN EXISTING U.S. 45 TO THE SOUTH (BASE AND BINDER COURSE ONLY - SURFACE COURSE TO BE CONSTRUCTED IN STAGE 3). CONSTRUCT CURB & GUTTER AND ENTRANCES.
5. FOURTH STREET CLOSED FOR RECONSTRUCTION OF FOURTH STREET BRIDGE.
6. CONSTRUCT CHOISSEY STREET AND FOURTH STREET ONE LANE AT A TIME UNDER TRAFFIC. USE FLAGMEN FOR LANE CLOSURE AND BUILD PARTS OF ROAD UNDER TRAFFIC IN LIFTS.
7. REMOVE MUNDY STREET ACCESS TO FOURTH STREET.

**TRAFFIC PLACEMENT**


1. MAINTAIN TRAFFIC ON EXISTING U.S. 45 AND PAVEMENT CONSTRUCTED IN STAGE 1A
2. FOURTH STREET SHALL BE CLOSED TO TRAFFIC FOR BRIDGE REPLACEMENT
3. ALL SIDEROADS SHALL REMAIN OPEN AND SHALL BE CONSTRUCTED UNDER TRAFFIC
4. ALL ENTRANCES SHALL REMAIN OPEN AND SHALL BE CONSTRUCTED UNDER TRAFFIC

**TRAFFIC CONTROL STANDARDS**

701006, 701201, 701326

**TRAFFIC CONTROL PAYMENT**


TRAFFIC CONTROL AND PROTECTION, LUMP SUM AS PER TRAFFIC CONTROL STANDARD USED

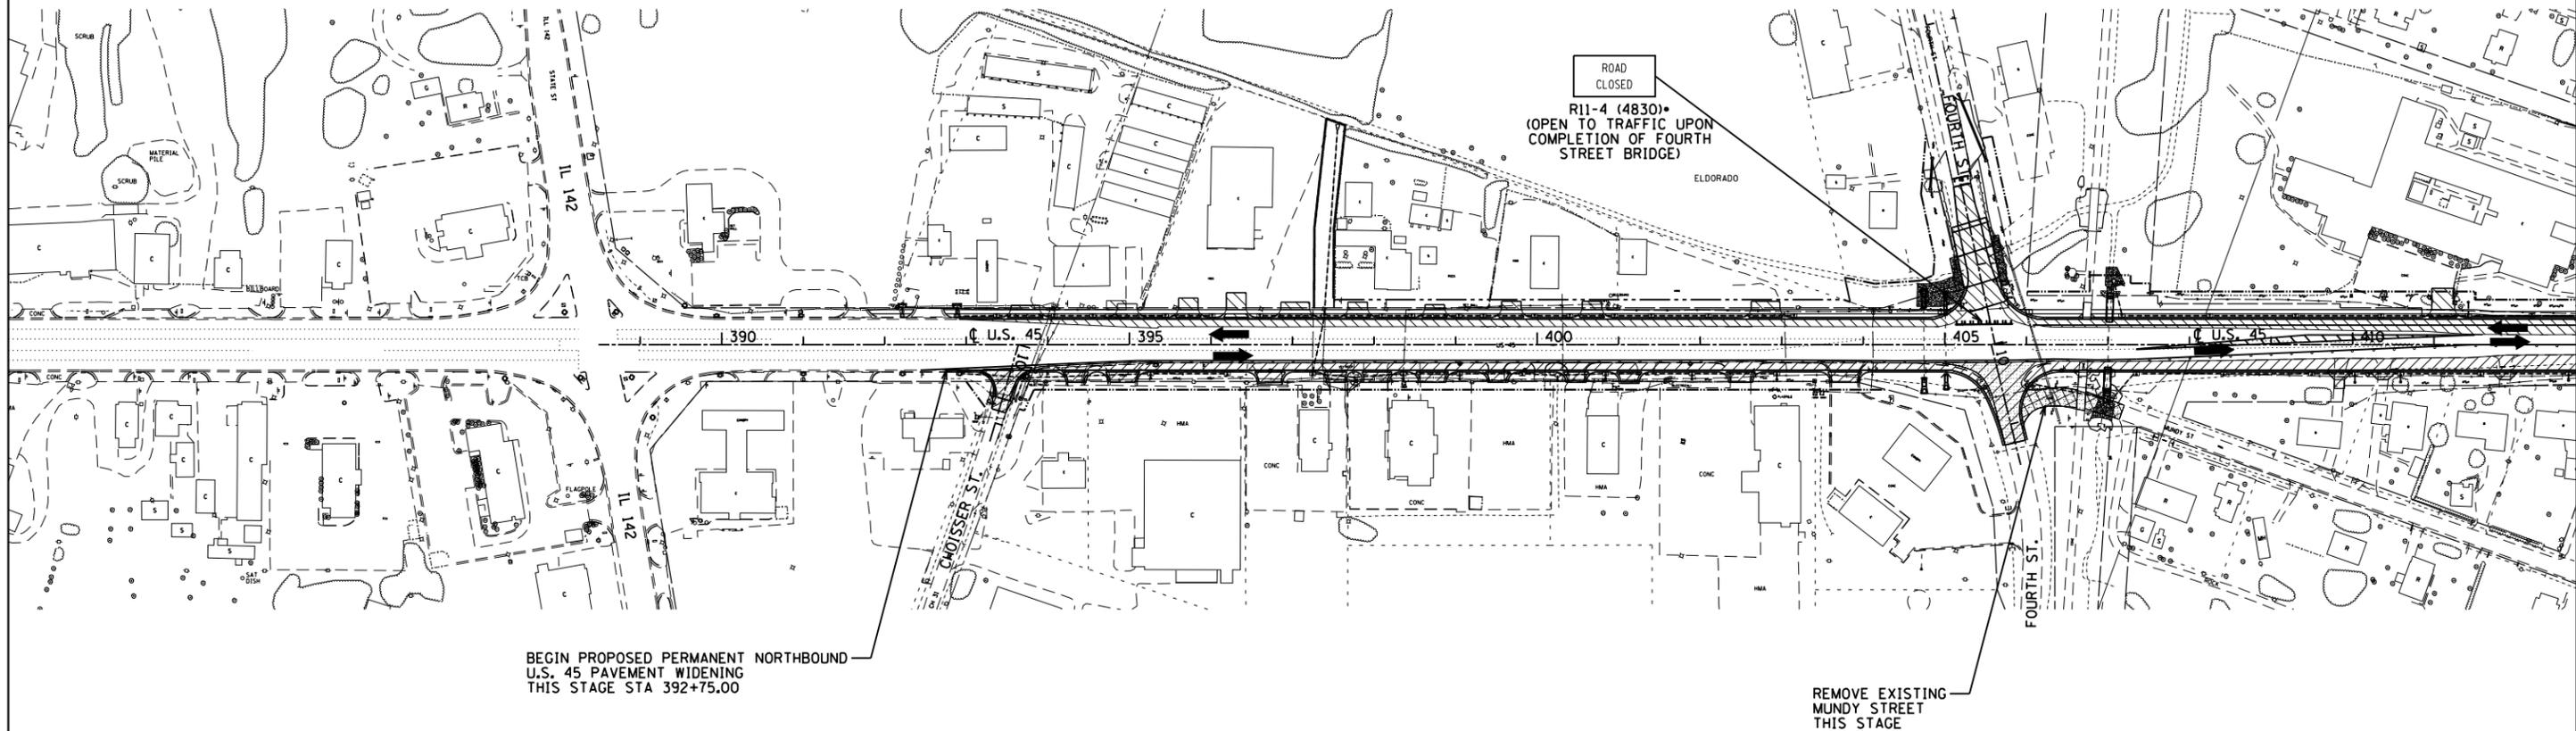

**LEGEND**

	TEMPORARY PAVEMENT CONSTRUCTED AS NOTED		DIRECTION OF TRAFFIC FLOW
	PERMANENT PAVEMENT CONSTRUCTED THIS STAGE		CONSTRUCTION SIGN
	PERMANENT PAVEMENT CONSTRUCTED IN PREVIOUS STAGE		TYPE III BARRICADE
	PAVEMENT REMOVAL THIS STAGE		DRUMS WITH STEADY BURNING MONODIRECTIONAL LIGHTS 25' CENTERS
			SIGN PANEL/BARRICADE ASSEMBLY (INCLUDED IN THE COST FOR TRAFFIC CONTROL AND PROTECTION, LUMP SUM)

**NOTES:**  
ALL SIDEROADS / ENTRANCES ARE TO REMAIN OPEN AND BE CONSTRUCTED WITH MINIMAL TEMPORARY SHUTDOWNS AT THE DIRECTION OF THE ENGINEER.



FILE NAME =	USER NAME = bemory	DESIGNED -	REVISED -	<b>STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION</b>	<b>CONSTRUCTION STAGING PLAN STAGE 1B</b>	F.A.P. RTE. 332	SECTION (29,30)R-1	COUNTY SALINE	TOTAL SHEETS 745	SHEET NO. 245
Default	P:\Projects\2011 Projects\11297 - IDOT US 45 Ph2\CV\CADD Sheets\0978077-sht-Stage1B.dwg	DRAWN -	REVISED -			CONTRACT NO. 78077		ILLINOIS FED. AID PROJECT		
	PLOT SCALE = 200.0000' / in.	CHECKED -	REVISED -		SCALE: 1" = 100'	SHEET	OF	SHEETS	STA. 388+50.00	TO STA. 412+00.00
	PLOT DATE = 4/30/2014	DATE -	REVISED -							
