

MAINTENANCE OF TRAFFIC STAGE 1B (THIS SHEET)

SEQUENCE OF CONSTRUCTION

1. REMOVE EXISTING STRIPING.
2. PLACE TEMPORARY STRIPING TO MAINTAIN SHIFTED TRAFFIC.
3. WIDEN EXISTING U.S. 45 TO THE SOUTH (RIGHT) (BASE AND BINDER COURSE ONLY - SURFACE COURSE TO BE CONSTRUCTED IN STAGE 3). CONSTRUCT CURB & GUTTER, SHOULDER, AND ENTRANCES.
4. CONSTRUCT JEFFERSON STREET, POPLAR STREET, ADAMS STREET, AND DEWEY STREET ONE LANE AT A TIME UNDER TRAFFIC. USE FLAGMEN FOR LANE CLOSURE AND BUILD PARTS OF ROAD UNDER TRAFFIC IN LIFTS.

TRAFFIC PLACEMENT

1. MAINTAIN TRAFFIC ON EXISTING U.S. 45 AND PAVEMENT CONSTRUCTED IN STAGE 1A
2. ALL SIDEROADS SHALL REMAIN OPEN AND SHALL BE CONSTRUCTED UNDER TRAFFIC
3. ALL ENTRANCES SHALL REMAIN OPEN AND SHALL BE CONSTRUCTED UNDER TRAFFIC

TRAFFIC CONTROL STANDARDS

701006, 701201, 701326

TRAFFIC CONTROL PAYMENT



TRAFFIC CONTROL AND PROTECTION, LUMP SUM AS PER TRAFFIC CONTROL STANDARD USED

LEGEND

	TEMPORARY PAVEMENT CONSTRUCTED AS NOTED		DIRECTION OF TRAFFIC FLOW
	PERMANENT PAVEMENT CONSTRUCTED THIS STAGE		CONSTRUCTION SIGN
	PERMANENT PAVEMENT CONSTRUCTED IN PREVIOUS STAGE		TYPE III BARRICADE
	PAVEMENT REMOVAL THIS STAGE		DRUMS WITH STEADY BURNING MONODIRECTIONAL LIGHTS @ 25' CENTERS
			SIGN PANEL/BARRICADE ASSEMBLY (INCLUDED IN THE COST FOR TRAFFIC CONTROL AND PROTECTION, LUMP SUM)

NOTES:

ALL SIDEROADS / ENTRANCES ARE TO REMAIN OPEN AND BE CONSTRUCTED WITH MINIMAL TEMPORARY SHUTDOWNS AT THE DIRECTION OF THE ENGINEER.

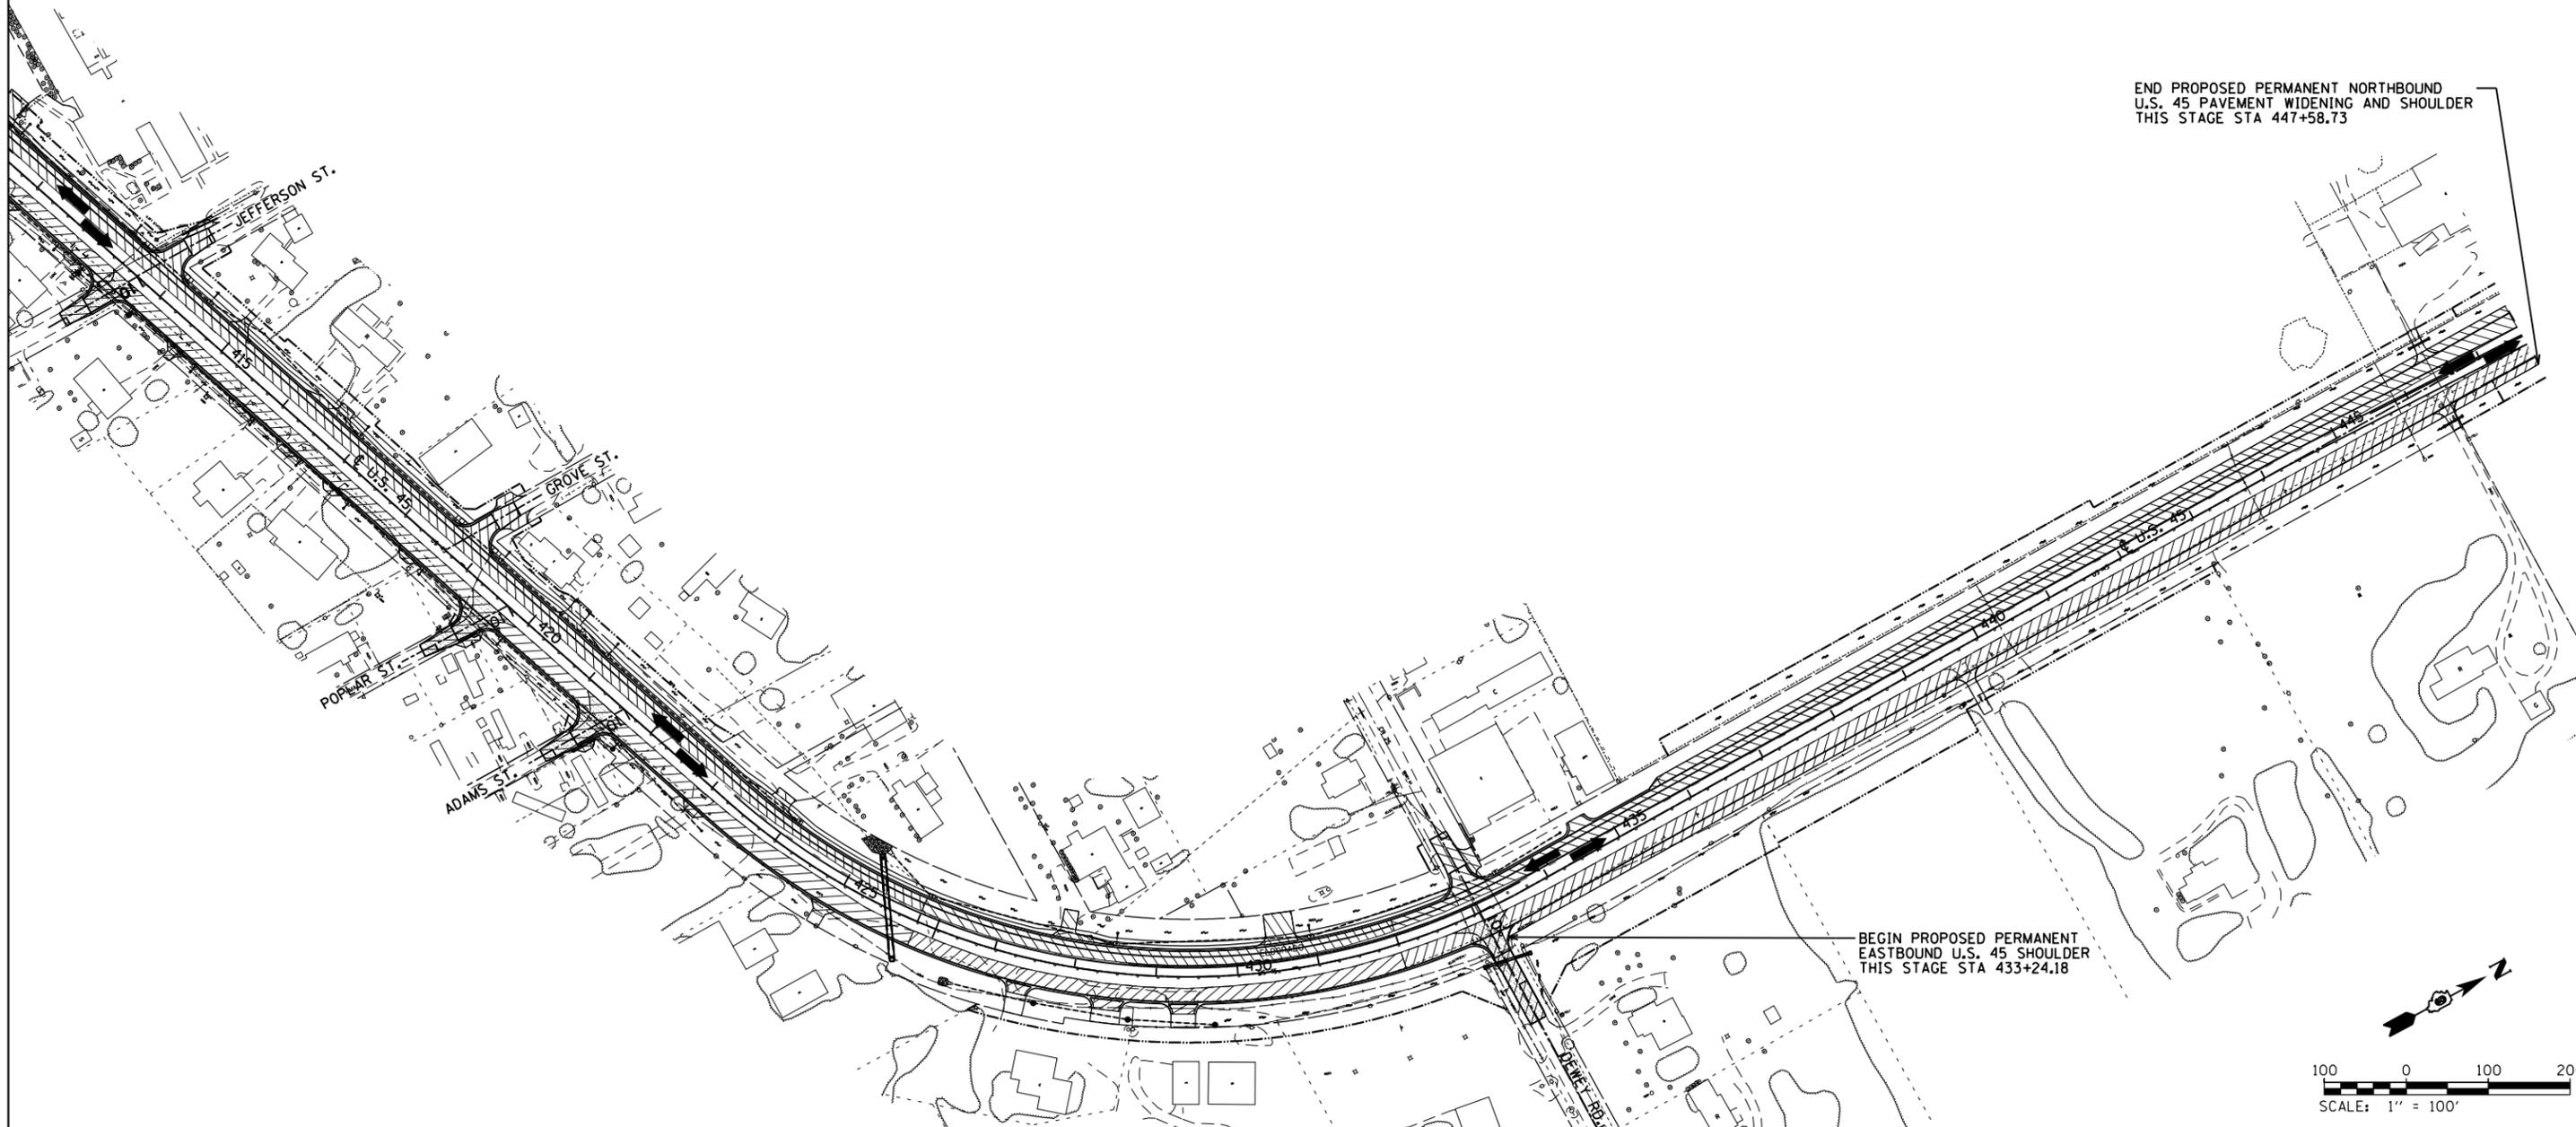

FILE NAME =	USER NAME = bemory	DESIGNED -	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	CONSTRUCTION STAGING PLAN STAGE 1B				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
P:\Projects\2011 Projects\11297 - IDOT US 45 Ph2\CV\CADD Sheets\0978077-sht-Stage1B.dwg		DRAWN -	REVISED -		332	(29,30)R-1	SALINE	745	246				
Default	PLOT SCALE = 200.0000' / in.	CHECKED -	REVISED -		CONTRACT NO. 78077								
	PLOT DATE = 4/30/2014	DATE -	REVISED -		ILLINOIS FED. AID PROJECT								
