


**MAINTENANCE OF TRAFFIC
TYPICAL SECTION - STAGE 1
I-74**
 STA 511+25 TO STA 556+50
 OMIT STA 539+00 TO STA 541+10
 OMIT STA 549+40 TO STA 551+10
 12' LANES - STA 511+25 TO STA 537+00
 11' LANES - STA 537+00 TO STA 556+50
 11' LANES - STA 589+09 TO STA 595+00

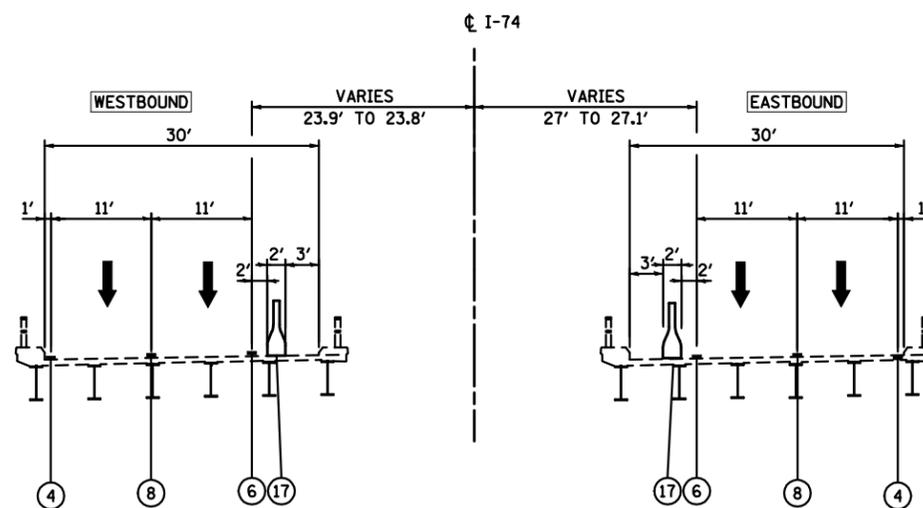

**MAINTENANCE OF TRAFFIC
TYPICAL SECTION - STAGE 1
I-74 OVER I-155**
 STA 539+00 TO STA 541+10

- LEGEND:**
- ① EXISTING PAVEMENT MARKING
 - ② TEMPORARY PAVEMENT MARKING FROM PREVIOUS STAGE
 - ③ PROPOSED PAVEMENT MARKING IN PLACE
 - ④ PAVEMENT MARKING, 4" SOLID WHITE
 - ⑤ PAVEMENT MARKING, 8" SOLID WHITE
 - ⑥ PAVEMENT MARKING, 4" SOLID YELLOW
 - ⑦ PAVEMENT MARKING, 4" DOTTED WHITE (3' SKIP, 9' DASH)
 - ⑧ PAVEMENT MARKING, 4" SKIP-DASH WHITE (30' SKIP, 10' DASH)
 - ⑨ DRUMS WITH STEADY BURNING WARNING LIGHTS AT 25' CENTERS
 - ⑩ DRUMS WITH STEADY BURNING WARNING LIGHTS AT 50' CENTERS
 - ⑪ DRUMS WITH STEADY BURNING WARNING LIGHTS AT 100' CENTERS
 - ⑫ DRUMS WITH STEADY BURNING WARNING LIGHTS 1000' CENTERS
 - ⑬ PAVEMENT MARKING, 4" SOLID DOUBLE YELLOW
 - ⑭ VERTICAL DELINEATOR PANELS
 - ⑮ TEMPORARY GEOTEXTILE RETAINING WALL
 - ⑯ PROPOSED CONCRETE BARRIER
 - ⑰ TEMPORARY CONCRETE BARRIER
 - ⑱ GLARE SCREEN
 - ▨ PROPOSED PAVEMENT CONSTRUCTION
 - ▩ TEMPORARY PAVEMENT CONSTRUCTION
 - ⊙ ON-GOING EARTHWORK FOR PROPOSED PAVEMENT

FILE NAME =	DESIGNED - HTL	REVISED -
D468620-sh-t-typico102-01.dgn	DRAWN - KV/JP	REVISED -
USER NAME = TERRA	CHECKED - DA/LVA	REVISED -
PLOT DATE = 7/16/2012	DATE - 7/20/2012	REVISED -



STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

MAINTENANCE OF TRAFFIC STAGE 1 - TYPICAL SECTIONS - I-74	
SCALE:	TO STA.
SHEET NO. 4 OF 52 SHEETS	STA. TO STA.

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90-[14R(14HB-4,14,14HB)BR]	TAZEWELL	ILLINOIS	2433	327
CONTRACT NO. 68620			ILLINOIS FED. AID PROJECT	
