


**SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL SCHEDULE**


LOCATION	STATION	TO	STATION	SUBBASE GRANULAR MATERIAL, TYPE B, 4"	PAVEMENT REMOVAL	SHORT TERM PAVEMENT MARKING	WORK ZONE PAVEMENT MARKING REMOVAL	TEMPORARY CONCRETE BARRIER	RELOCATE TEMPORARY CONCRETE BARRIER	IMPACT ATTENUATORS, TEMPORARY (FULLY REDIRECTIVE, NARROW), TEST LEVEL 2	IMPACT ATTENUATORS, TEMPORARY (FULLY REDIRECTIVE, NARROW), TEST LEVEL 3	IMPACT ATTENUATORS, RELOCATE (FULLY REDIRECTIVE, NARROW), TEST LEVEL 2	IMPACT ATTENUATORS, RELOCATE (FULLY REDIRECTIVE, NARROW), TEST LEVEL 3	PAVEMENT MARKING REMOVAL	TEMPORARY CONCRETE BARRIER (SPECIAL)	TEMPORARY PAVEMENT	TEMPORARY EPOXY PAVEMENT MARKING - LINE 4"	TEMPORARY EPOXY PAVEMENT MARKING - LINE 5"	TEMPORARY EPOXY PAVEMENT MARKING - LINE 8"	TEMPORARY EPOXY PAVEMENT MARKING - LINE 12"	
				SO YD	SO YD	FOOT	SO FT	FOOT	FOOT	FOOT	EACH	EACH	EACH	EACH	SO FT	FOOT	SO YD	FOOT	FOOT	FOOT	FOOT
	1	TO		138	-	11,624	-	975.0	-	1	-	-	-	-	-	138	5,812	-	-	-	
	2	TO		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
LOCAL ROADS - STAGES 2A-2B																					
	1	TO		-	-	12,194	1,942	525.0	975.0	-	-	1	-	1,942	737.5	-	6,097	-	-	37	
	2	TO		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
LOCAL ROADS - STAGSE 3A-3C																					
	1	TO		-	138	9,502	1,012	-	637.5	-	-	1	-	1,012	-	-	4,751	-	-	37	
	2	TO		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
SUBTOTAL																					
<b>TOTAL</b>																					
				138	138	81,616	16,603	6,213.0	6,662.5	1	14	2	14	9,919	737.5	138	51,433	5,982	7,592	2,204	

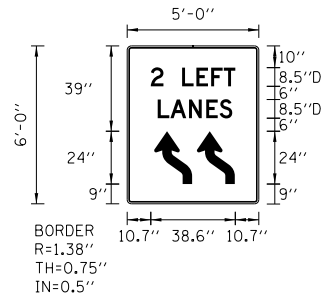

SIGN NUMBER	Lane Shift
WIDTH x HGHT.	5'-0" x 6'-0"
BORDER WIDTH	0.75"
CORNER RADIUS	1.38"
MOUNTING	Ground
BACKGROUND	TYPE: Reflective COLOR: Yellow
LEGEND/BORDER	TYPE: Reflective COLOR: Black/Black

SYMBOL	ROT	X	Y	WID	HT
W1_4RA	180	12.3	9	17.3	24.1
W1_4RA	180	31.8	9	17.3	24.1

LETTER POSITIONS (X)						LENGTH	SERIESSIZE
2	L	E	F	T			D 2000
10.7	16.5	25	31.6	38.3	44.1	38.6	8.5
L	A	N	E	S			D 2000
13.9	19.7	28.2	36	42.1		34	8.5



SIGN NUMBER	Lane Shift
WIDTH x HGHT.	4'-0" x 2'-0"
BORDER WIDTH	0.75"
CORNER RADIUS	1.38"
MOUNTING	Ground
BACKGROUND	TYPE: Reflective COLOR: Orange
LEGEND/BORDER	TYPE: Reflective COLOR: Black/Black

SYMBOL	ROT	X	Y	WID	HT

LETTER POSITIONS (X)						LENGTH	SERIESSIZE
2	L	E	F	T			D 2000
10.4	14.5	20.5	25.1	29.8	33.9	27.2	6
L	A	N	E	S			D 2000
12.5	16.6	22.6	28.1	32.4		24	6

FILE PATH = ...



DI60W26-sht-Staging-Schedule-02  
 USER NAME = pimsarno  
 PLOT SCALE = 50.0000' / in.  
 PLOT DATE = 9/15/2013

DESIGNED - OPS  
 DRAWN - OPS  
 CHECKED - DBM  
 DATE - 9/15/13

REVISED -  
 REVISED -  
 REVISED -  
 REVISED -

**STATE OF ILLINOIS  
 DEPARTMENT OF TRANSPORTATION**

**SUGGESTED STAGES OF CONSTRUCTION AND TRAFFIC CONTROL PLAN  
 SCHEDULES**

SCALE: SHEET 2 OF 2 SHEETS STA. TO STA.

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90/94/290	2013-008R	COOK	559	64A
CONTRACT NO. 60W26				
ILLINOIS FED. AID PROJECT				
