


**MAINTENANCE OF TRAFFIC
TYPICAL SECTION - PRE-STAGE SUB STAGE B
I-74**


STA 461+70 TO STA 516+00 WB
STA 469+85 TO STA 500+00 EB
(SEE PROPOSED SHOULDER DETAIL)

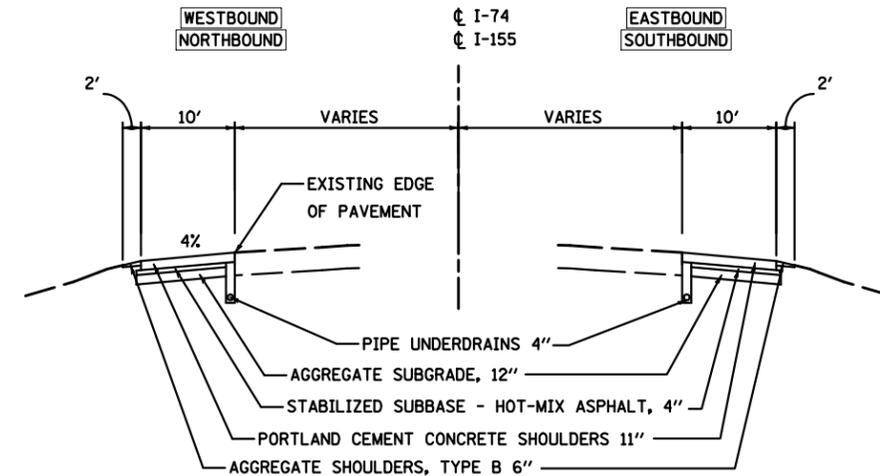

PROPOSED SHOULDER DETAIL


PRE STAGE SUB STAGE A - I-74 STA 461+70 TO STA 464+55 WB
PRE STAGE SUB STAGE B - I-155 STA 35+90 TO STA 43+50 SB

PRE STAGE SUB STAGE B - I-74 STA 455+04 TO STA 473+00 EB
PRE STAGE SUB STAGE B - I-155 STA 35+90 TO STA 37+13 NB

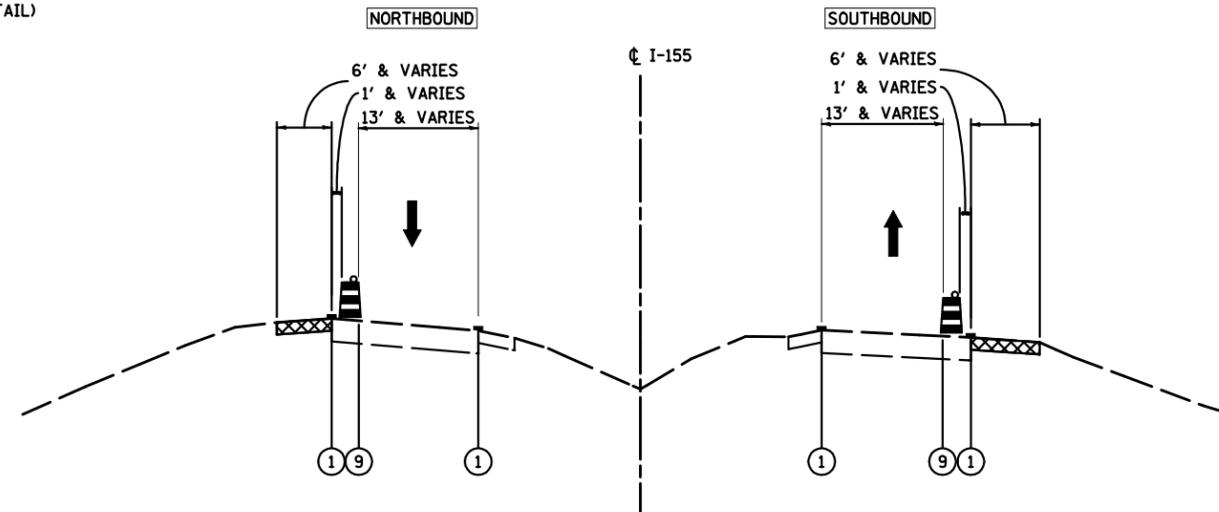

**MAINTENANCE OF TRAFFIC
TYPICAL SECTION - PRE-STAGE
I-155**

STA 9+70 TO STA 13+86 & STA 14+96 TO STA 37+13 NB
STA 11+09 TO STA 18+50 & STA 15+86 TO STA 43+50 SB

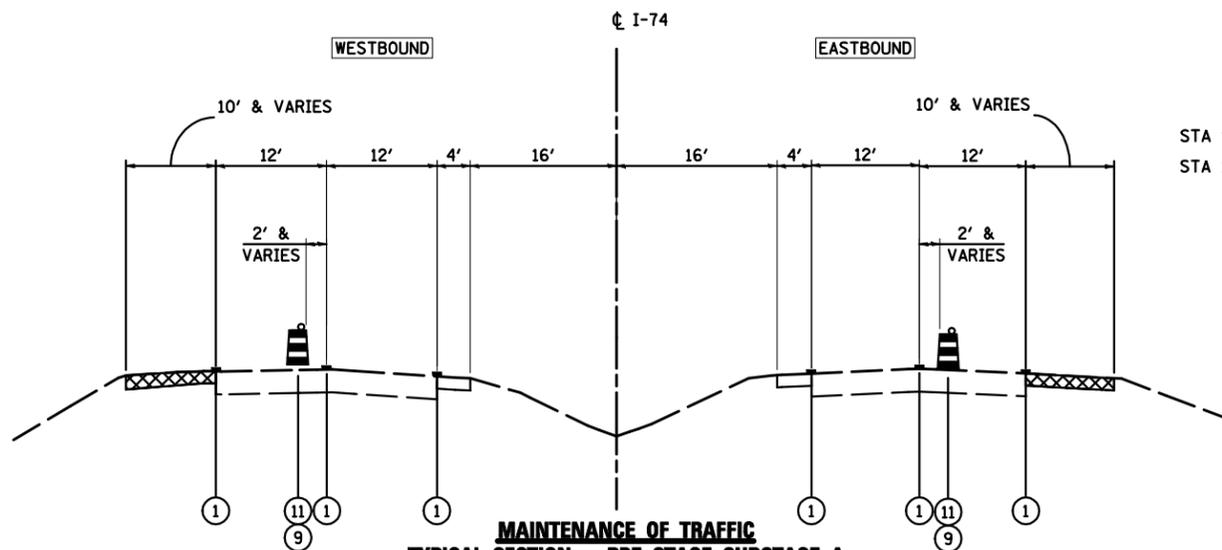

**MAINTENANCE OF TRAFFIC
TYPICAL SECTION - PRE-STAGE SUBSTAGE A
I-74**

STA 516+00 TO STA 609+00 WB
STA 500+00 TO STA 619+35 EB

LEGEND:

- ① EXISTING PAVEMENT MARKING
- ② TEMPORARY PAVEMENT MARKING FROM PREVIOUS STAGE
- ③ PROPOSED PAVEMENT MARKING IN PLACE
- ④ PAVEMENT MARKING, 4" SOLID WHITE
- ⑤ PAVEMENT MARKING, 8" SOLID WHITE
- ⑥ PAVEMENT MARKING, 4" SOLID YELLOW
- ⑦ PAVEMENT MARKING, 4" DOTTED WHITE (3' SKIP, 9' DASH)
- ⑧ PAVEMENT MARKING, 4" SKIP-DASH WHITE (30' SKIP, 10' DASH)
- ⑨ DRUMS WITH STEADY BURNING WARNING LIGHTS AT 25' CENTERS
- ⑩ DRUMS WITH STEADY BURNING WARNING LIGHTS AT 50' CENTERS
- ⑪ DRUMS WITH STEADY BURNING WARNING LIGHTS AT 100' CENTERS
- ⑫ DRUMS WITH STEADY BURNING WARNING LIGHTS 1000' CENTERS
- ⑬ PAVEMENT MARKING, 4" SOLID DOUBLE YELLOW
- ⑭ VERTICAL DELINEATOR PANELS
- ⑮ TEMPORARY GEOTEXTILE RETAINING WALL
- ⑯ PROPOSED CONCRETE BARRIER
- ⑰ TEMPORARY CONCRETE BARRIER
- ⑱ GLARE SCREEN
- ▨ PROPOSED PAVEMENT CONSTRUCTION
- ▩ TEMPORARY PAVEMENT CONSTRUCTION
- ⊙ ON-GOING EARTHWORK FOR PROPOSED PAVEMENT

FILE NAME = D468620-sh-typical01-00.dgn	DESIGNED - HTL	REVISED -
USER NAME = TERRA	DRAWN - KV/JP	REVISED -
PLOT DATE = 7/16/2012	CHECKED - DA/LVA	REVISED -
	DATE - 7/20/2012	REVISED -



**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

MAINTENANCE OF TRAFFIC PRE STAGE - TYPICAL SECTIONS - I-74	
SCALE:	SHEET NO. 3 OF 50 SHEETS STA. TO STA.

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
90-[14R(14HB-4,14,14HV)BR]	TAZEWELL	ILLINOIS FED. AID PROJECT	2433	276
CONTRACT NO. 68620				
