

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

ROUTE NO.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.	SHEET NO.
FAS 1190	(125BY)BR	KNOX	94	47	20 SHEETS
FED. ROAD DIST. NO. 7	ILLINOIS	FED. AID PROJECT			

Contract No. 68087

EAST EDGE OF SHOULDER

Location	Station	Offset	Theoretical Grade Elevations
N. end of N. appr. slab	149+81.83	-18.00	721.14
A	149+91.83	-18.00	721.32
B	150+01.83	-18.00	721.51
S. end of N. appr. slab	150+11.83	-18.00	721.71

EAST EDGE OF PAVEMENT

Location	Station	Offset	Theoretical Grade Elevations
N. end of N. appr. slab	149+82.88	-12.00	721.29
A	149+92.88	-12.00	721.47
B	150+02.88	-12.00	721.66
S. end of N. appr. slab	150+12.88	-12.00	721.85

☉ ROADWAY, PG. & STAGE CONSTRUCTION JOINT


Location	Station	Offset	Theoretical Grade Elevations
N. end of N. appr. slab	149+85.00	0.00	721.51
A	149+95.00	0.00	721.69
B	150+05.00	0.00	721.88
S. end of N. appr. slab	150+15.00	0.00	722.08

WEST EDGE OF PAVEMENT

Location	Station	Offset	Theoretical Grade Elevations
N. end of N. appr. slab	149+87.12	12.00	721.36
A	149+97.12	12.00	721.55
B	150+07.12	12.00	721.74
S. end of N. appr. slab	150+17.12	12.00	721.94

WEST EDGE OF SHOULDER

Location	Station	Offset	Theoretical Grade Elevations
N. end of N. appr. slab	149+88.17	18.00	721.26
A	149+98.17	18.00	721.44
B	150+08.17	18.00	721.63
S. end of N. appr. slab	150+18.17	18.00	721.84

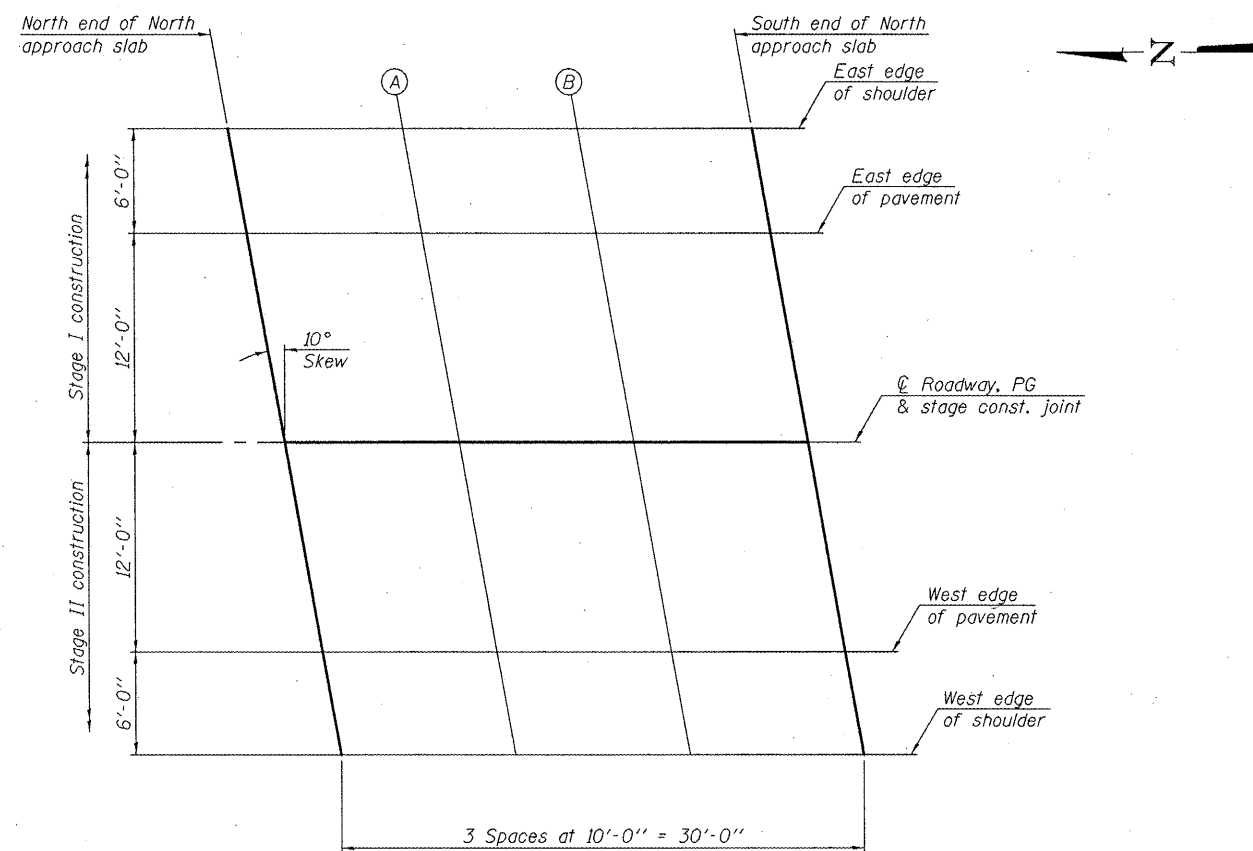

PLAN

DESIGNED	SMR
CHECKED	FT
DRAWN	MBM
CHECKED	SMR/FT

US ROUTE 150 OVER HENDERSON CREEK
F.A.S. ROUTE 1190 - SEC. (125BY)BR
KNOX COUNTY
STATION 150+71.00
STRUCTURE NO. 048-0088
**TOP OF NORTH APPROACH
SLAB ELEVATIONS**
