



FAH. NO.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
1380	00-00084-00-PV	DUPAGE	93	13
STA.		TO STA.		
		SURFACE TRANSPORTATION FUNDING		


CONTRACT NUMBER 83993

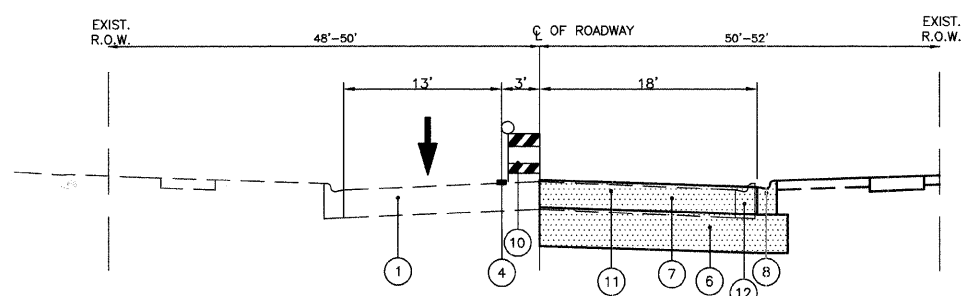


FULLERTON AVENUE - PHASE 1
STA. 188+64 TO STA. 221+25

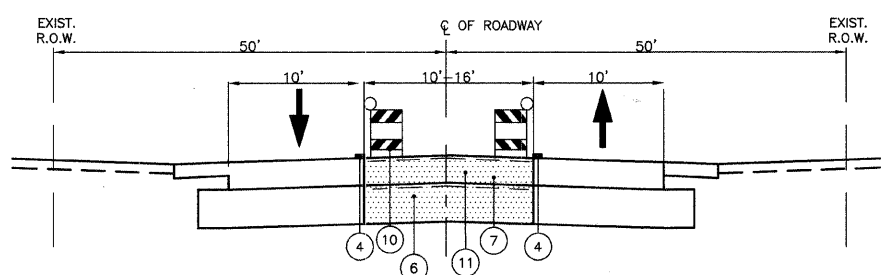


FULLERTON AVENUE - PHASE 3
STA. 222+08 TO STA. 225+42

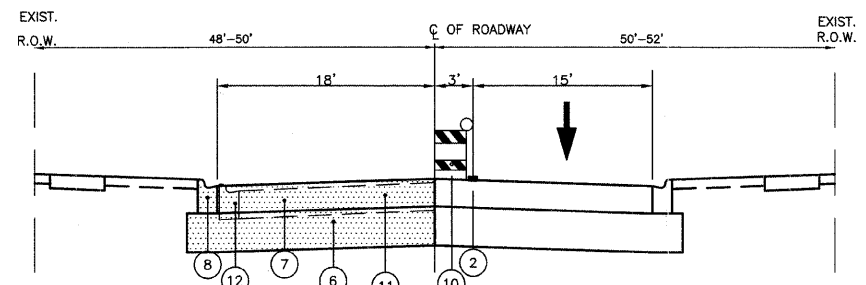


FULLERTON AVENUE - PHASE 2
STA. 188+64 TO STA. 221+25

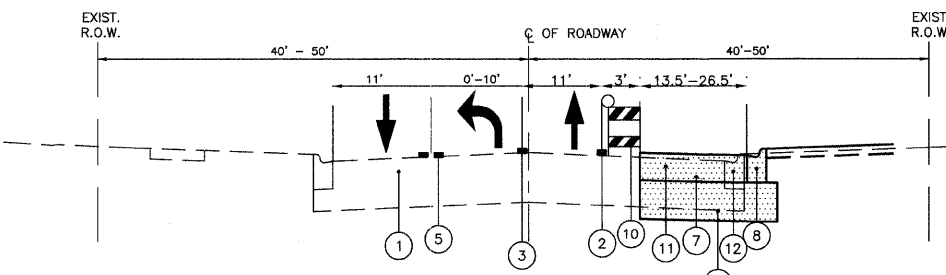


VILLA AVENUE - PHASE 1
STA. 507+10.7 TO STA. 519+26.5

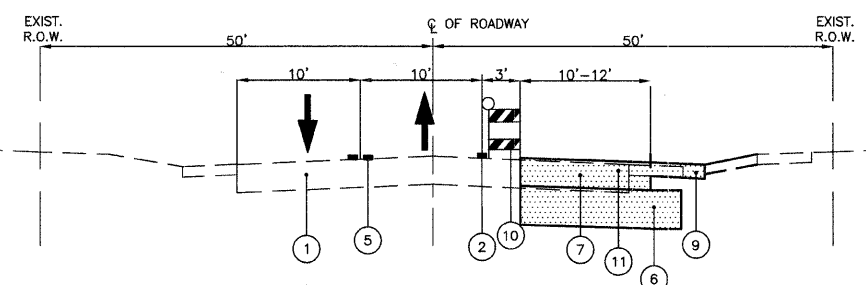


FULLERTON AVENUE - PHASE 1
STA. 221+85 TO STA. 225+42

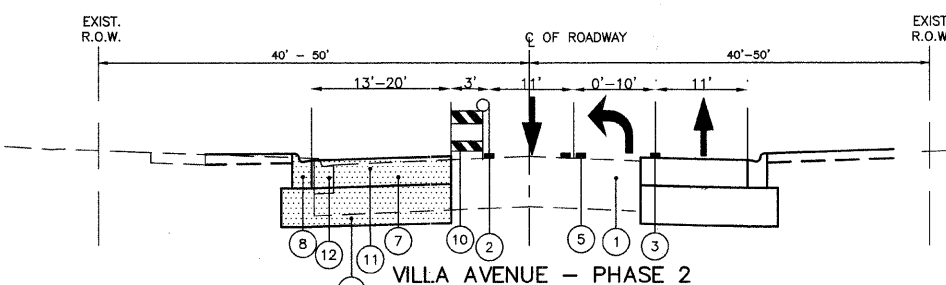

VILLA AVENUE - PHASE 2
STA. 507+10.7 TO STA. 519+26.5

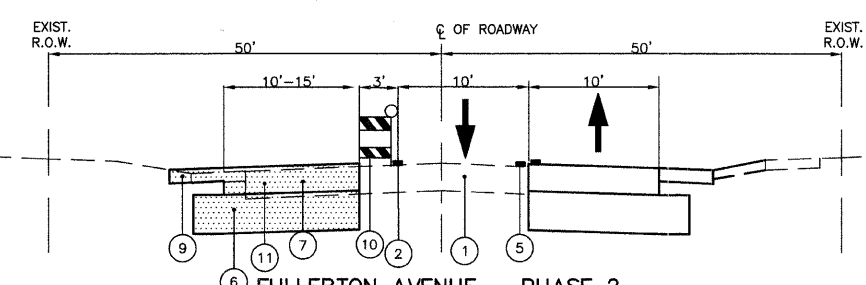

FULLERTON AVENUE - PHASE 2
STA. 221+85 TO STA. 225+42

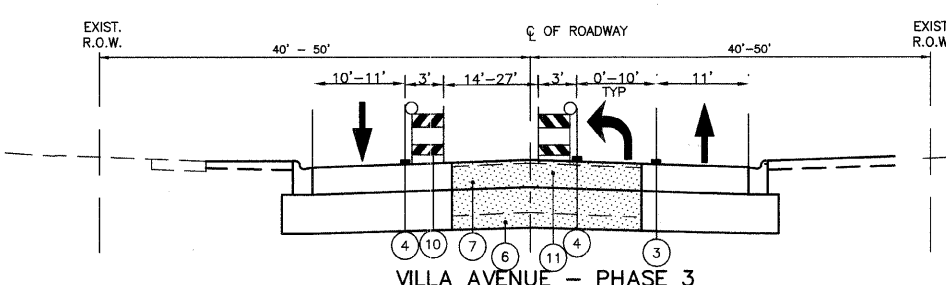

VILLA AVENUE - PHASE 3
STA. 507+10.7 TO STA. 519+26.5

- | | |
|--|--|
| ① EXISTING BITUMINOUS PAVEMENT | ⑦ PROP. HOT-MIX ASPHALT BINDER COURSE, IL-19, N70 |
| ② PROP. TEMPORARY PAVEMENT MARKING (4" WHITE LINE) | ⑧ PROP. COMB. CONCRETE CURB & GUTTER, TYPE B-6.18 |
| ③ PROP. TEMPORARY PAVEMENT MARKING (6" WHITE LINE) | ⑨ PROP. AGGREGATE SHOULDERS, TYPE A, 8" |
| ④ PROP. TEMPORARY PAVEMENT MARKING (4" YELLOW LINE) | ⑩ TYPE II OR TYPE II BARRICADE (NON-METALLIC) W/ STEADY-BURN LIGHT |
| ⑤ PROP. TEMPORARY PAVEMENT MARKING (2-4" YELLOW LINES @ 11" CTRS.) | ⑪ PAVEMENT REMOVAL |
| ⑥ PROP. AGGREGATE SUBGRADE, 12" | ⑫ COMBINATION CURB & GUTTER REMOVAL |

- LEGEND**
- ➔ DIRECTION OF SINGLE LANE OF THRU TRAFFIC DURING STAGE
 - * [Hatched Box] PERMANENT CONSTRUCTION DURING STAGE
 - *SEE TYPICAL SECTIONS AND PLAN AND PROFILE SHEETS

- CONSTRUCTION SEQUENCE**
- PRE-PHASE 1**
- ERECT ALL ADVANCED CONSTRUCTION SIGNING.
 - ERECT DETOUR SIGNS AND ACTIVATE DETOUR.
 - TURN OFF AND COVER TRAFFIC SIGNALS AT THE FULLERTON AVENUE AND VILLA AVENUE INTERSECTION, AND INSTALL TEMPORARY TRAFFIC SIGNALS AND LIGHTING.
 - REMOVE CONFLICTING PAVEMENT MARKINGS AND PLACE TEMPORARY MARKINGS, ERECT BARRICADES AND TEMPORARY TRAFFIC SIGNS AND SHIFT TRAFFIC.
 - IMPLEMENT SOIL & SEDIMENT EROSION CONTROL PLAN.
- PHASE 1A AND 1B**
- REMOVE CONFLICTING TREES, EXISTING PAVEMENT, AND CURB AND GUTTER ON SOUTH SIDE OF FULLERTON AVENUE AND EAST SIDE OF VILLA AVENUE.
 - CONSTRUCT BIO-SWALE OUTFALL TO SALT CREEK.
 - INSTALL DRAINAGE STRUCTURES, MAIN STORM SEWER, & STORM SEWER LATERALS ON SOUTH SIDE OF FULLERTON AVENUE AND EAST SIDE OF VILLA AVENUE. REPLACE WATER MAINS.
 - CONSTRUCT BASE COURSE, BINDER COURSE, CURB AND GUTTER, DRIVEWAYS AND SIDEWALKS ON SOUTH SIDE OF FULLERTON AVENUE AND EAST SIDE OF VILLA AVENUE.
 - REMOVE CONFLICTING PAVEMENT MARKINGS AND PLACE TEMPORARY MARKINGS, RELOCATE BARRICADES, ADJUST TEMPORARY SIGNING, TEMPORARY TRAFFIC SIGNALS, AND SHIFT TRAFFIC ON FULLERTON AVENUE AND VILLA AVENUE.
 - BEGIN INSTALLATION OF PERMANENT TRAFFIC SIGNALS AND ROADWAY LIGHTING.
- PHASE 2A AND 2B**
- REMOVE CONFLICTING TREES, EXISTING PAVEMENT AND CURB AND GUTTER ON NORTH SIDE OF FULLERTON AVENUE AND WEST SIDE OF VILLA AVENUE.
 - CONSTRUCT ALL REMAINING STORM SEWERS ON NORTH SIDE OF FULLERTON AVENUE AND WEST SIDE OF VILLA AVENUE.
 - CONSTRUCT BASE COURSE, BINDER COURSE, CURB AND GUTTER, DRIVEWAYS AND SIDEWALKS ON NORTH SIDE OF FULLERTON AVENUE AND WEST SIDE OF VILLA AVENUE.
 - REMOVE CONFLICTING PAVEMENT MARKINGS AND PLACE TEMPORARY MARKINGS, RELOCATE BARRICADES, ADJUST TEMPORARY SIGNING, TEMPORARY TRAFFIC SIGNALS, AND SHIFT TRAFFIC ON VILLA AVENUE AND FULLERTON AVENUE (EAST OF INTERSECTION.)
 - REMOVE CONFLICTING PAVEMENT MARKINGS ON FULLERTON AVENUE (BETWEEN ADDISON ROAD AND VILLA AVENUE), AND PLACE TEMPORARY MARKINGS, PLACE PERMANENT SIGNING, REMOVE ALL BARRICADES AND TEMPORARY TRAFFIC SIGNS AND OPEN LANES TO TRAFFIC ON FULLERTON AVENUE.
- PHASE 3**
- CONSTRUCT BASE COURSE AND BINDER COURSE IN THE LEFT-TURN LANES AND MEDIAN ON FULLERTON AVENUE AND VILLA AVENUE.
- PHASE 4 (NOT ILLUSTRATED)**
- PLACE SURFACE COURSE TO FINISHED GRADE ON FULLERTON AVENUE AND VILLA AVENUE, MAINTAINING TRAFFIC AS PER STANDARD 701501, AND PLACE SHORT TERM PAVEMENT MARKING TAPE AS REQUIRED.
 - COMPLETE AND ACTIVATE ALL PERMANENT TRAFFIC SIGNAL INSTALLATIONS AND REMOVE TEMPORARY SIGNALS AT FULLERTON AVENUE AND VILLA AVENUE.
 - COMPLETE ROADWAY LIGHTING INSTALLATION.
 - REMOVE ALL CONFLICTING PAVEMENT MARKINGS, PLACE SHORT-TERM MARKINGS AND PERMANENT SIGNING, REMOVE ALL BARRICADES AND TEMPORARY TRAFFIC SIGNS.
 - COMPLETE ALL REMAINING LANDSCAPING AND CLEAN-UP WORK.

REVISIONS	
NAME	DATE

VILLAGE OF ADDISON
SUGGESTED CONSTRUCTION PROCEDURE
 TYPICAL SECTION & CONSTRUCTION PROCEDURE
FULLERTON AVENUE & VILLA AVENUE
 NOT TO SCALE
 DATE: 11/26/2007
 DESIGNED BY: LAS
 TECHNICIAN: JRR
 CHECKED BY: RTM
