

RTE	SECTION	COUNTY	TOTAL SHEETS	SHEET NO
344	(46-1S&47)WRS-2	LAKE	234	135
STA.		TO STA.		
FED. ROAD DIST. NO. 7		ILLINOIS FED. AID PROJECT		
CONTRACT NO. 60956				






THE CONTRACTOR SHALL BE RESPONSIBLE FOR PERFORMING ALL NECESSARY EQUIPMENT AND PHASING CHANGES TO THE INSTALLATION TO COVER THE DIFFERENT SIGNAL HEAD REQUIREMENTS AND SIGNAL PHASING BETWEEN MOT STAGE II AND MOT STAGE III. THE COST OF THIS WORK WILL BE INCLUDED IN THE COST OF TEMPORARY TRAFFIC SIGNAL INSTALLATION.

MAINTENANCE OF TRAFFIC STAGE I

MAINTENANCE OF TRAFFIC STAGE II

MAINTENANCE OF TRAFFIC STAGE III

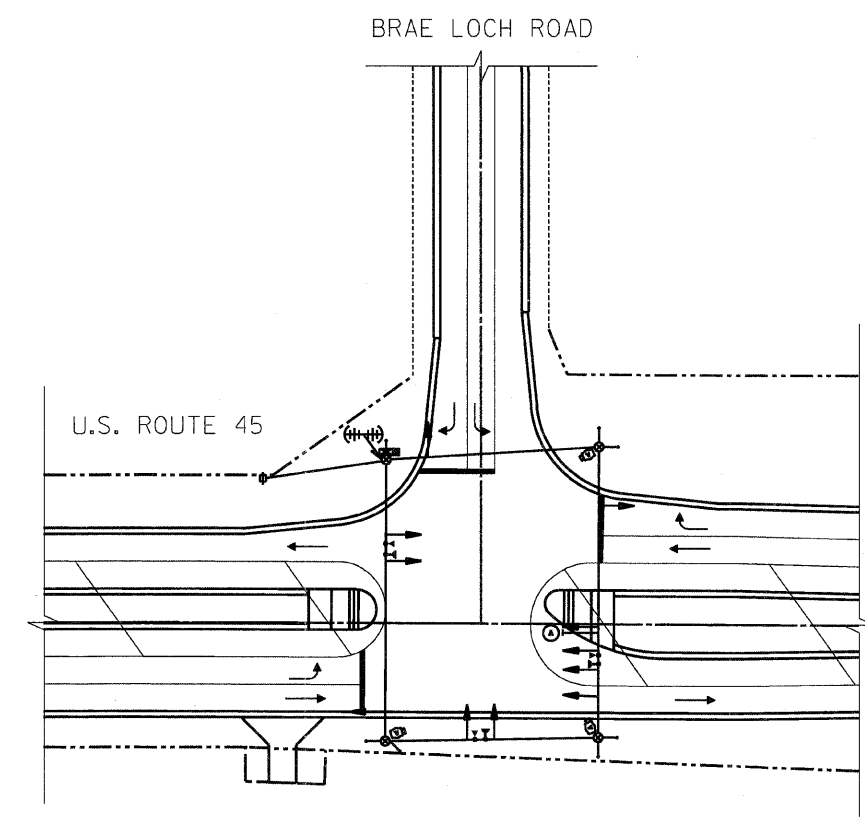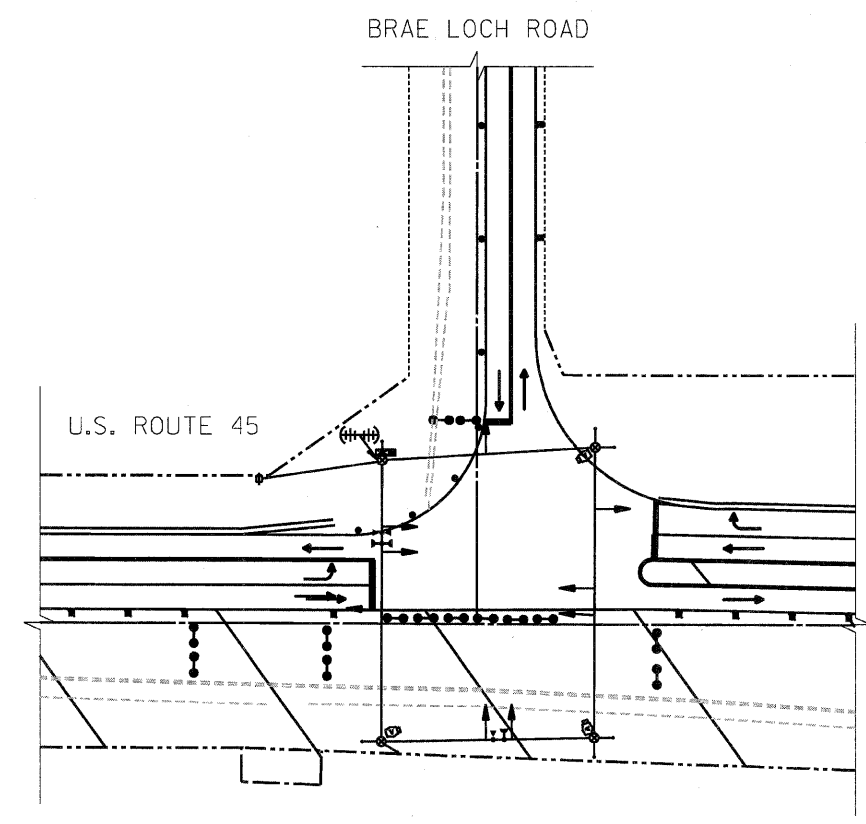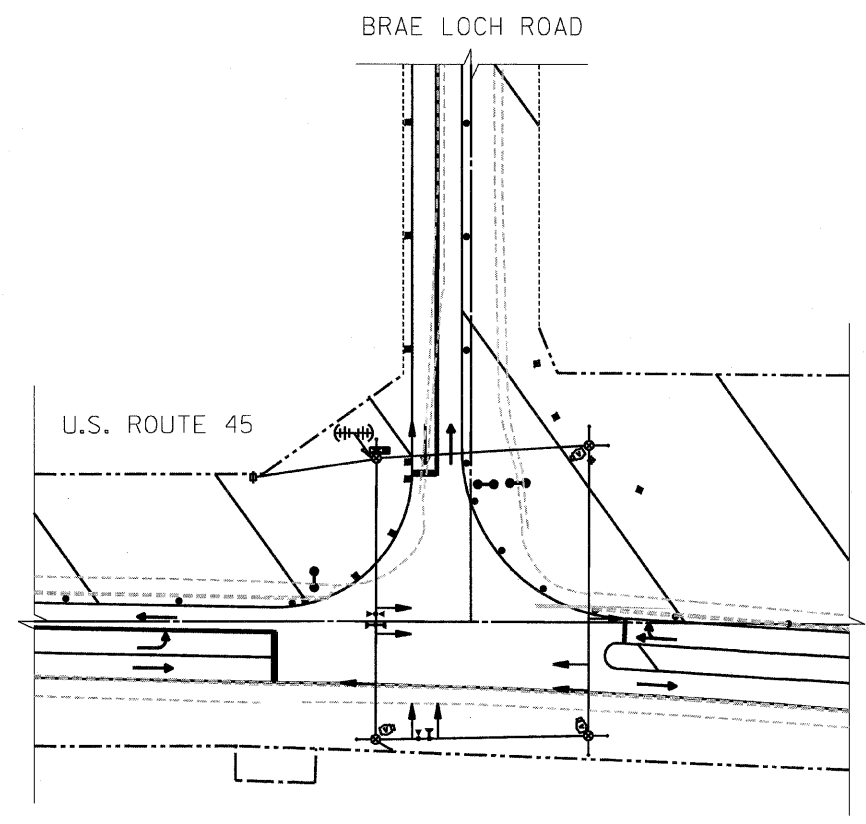

12/14/09 - e:\401\2000\00005302\work\shon\118\p1\delocb - s10090.dwg

- TEMPORARY TRAFFIC SIGNAL LEGEND**
- TEMPORARY TRAFFIC SIGNAL HEAD SPAN WIRE MOUNTED ORIGINAL LOCATION
  - TEMPORARY TRAFFIC SIGNAL HEAD SPAN WIRE MOUNTED SECONDARY LOCATION
  - TEMPORARY WOOD POLE (CLASS 5 OR BETTER) 45 FOOT (13.7m) MINIMUM
  - TEMPORARY CONTROLLER CABINET
  - TEMPORARY SPAN WIRE, TETHER WIRE, AND CABLE
  - TEMPORARY SERVICE INSTALLATION
  - EMERGENCY VEHICLE SYSTEM DETECTOR
  - CONFIRMATION BEACON
  - CONDUIT IN TRENCH OR PUSHED
  - HEAVY DUTY HANDHOLE
  - TEMPORARY UPS
  - VIDEO DETECTOR
  - RADIO INTERCONNECT ANTENNA

- EXISTING EQUIPMENT TO BE REMOVED LEGEND**
- EXISTING SIGNAL HEAD TO BE REMOVED
  - EXISTING SERVICE INSTALLATION TO BE REMOVED
  - EXISTING SIGNAL POST AND FOUNDATION TO BE REMOVED
  - EXISTING CONTROLLER AND FOUNDATION TO BE REMOVED
  - EXISTING HANDHOLE TO BE REMOVED
  - EMERGENCY VEHICLE LIGHT DETECTOR TO BE REMOVED
  - EXISTING HEAVY-DUTY HANDHOLE TO BE REMOVED
  - EXISTING ALUMINUM MAST ARM POLE AND FOUNDATION TO BE REMOVED

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

**TEMPORARY TRAFFIC SIGNAL INSTALLATION**  
U.S. ROUTE 45 & BRAE LOCH ROAD  
STAGES I, II & III

HORIZ. 20 0 20  
SCALE IN FEET

DATE 12/14/09  
DRAWN BY MB/AJP  
CHECKED BY KMM
