

**ROAD WORK
AHEAD
EXPECT DELAYS**

SEE IDOT
DISTRICT 1
DETAIL TC-22

W21-I115(O)-3618
R2-1-3648
R10-19dP-3618
R21-I106-3618
W20-I103(O)-48

ADVANCE SIGNING

(SPACING MAY VARY DUE TO FIELD CONDITIONS)
TWO SIGNS REQUIRED AT EACH LOCATION;
ONE SIGN REQUIRED BEHIND RIGHT CURB AND
ONE SIGN IN THE MEDIAN

RIGHT TURN LANE TO REMAIN OPEN
IN ACCORDANCE WITH IDOT DISTRICT 1
DETAIL TC-14

TWO RIGHT THROUGH LANES SHALL BE CLOSED, THIS STAGE,
IN ACCORDANCE WITH IDOT STANDARD 701601 WITH A 1000'
TANGENT SECTION BETWEEN EACH LANE CLOSURE.
RELOCATE ADVANCE SIGNING ACCORDINGLY OR AS OTHERWISE
DIRECTED BY THE ENGINEER.

WORK
ZONE
SPEED
LIMIT
35
PHOTO
ENFORCED
\$375 FINE
MINIMUM

W20-I103(O)-48
M6-1-2115

END
WORK ZONE
SPEED LIMIT
G20-I103(O)-6036

FOX VALLEY CENTER DR.

W20-I103(O)-48
M6-1-2115


JCT
ILLINOIS
59
M2-1-2115
M1-I100-24

W1-4L(O)-48
W13-1P(O)-24
30
MPH

R3-8-3630

STOP R1-1-30
ONLY R3-5R-2430

MATCH LINE STA. 97+00

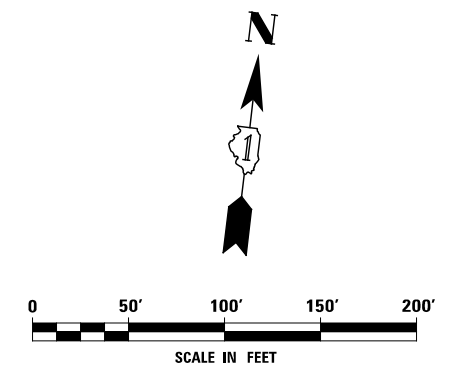

DESIGNED	PJO	REVISED	-
DRAWN	KES	REVISED	-
CHECKED	JCM	REVISED	-
DATE	12/14/2012	REVISED	-

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**MAINTENANCE OF TRAFFIC - STAGE 2A
NEW YORK STREET**

SCALE: AS SHOWN SHEET NO. 107 OF 195 SHEETS STA. 85+00 TO STA. 97+00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
338	(112 & 113) WRS-7	DUPAGE	1156	198
CONTRACT NO. 60R30				
ILLINOIS FED. AID PROJECT				
