


DATE	BY
REVISIONS	PLANNED
NO.	NO.

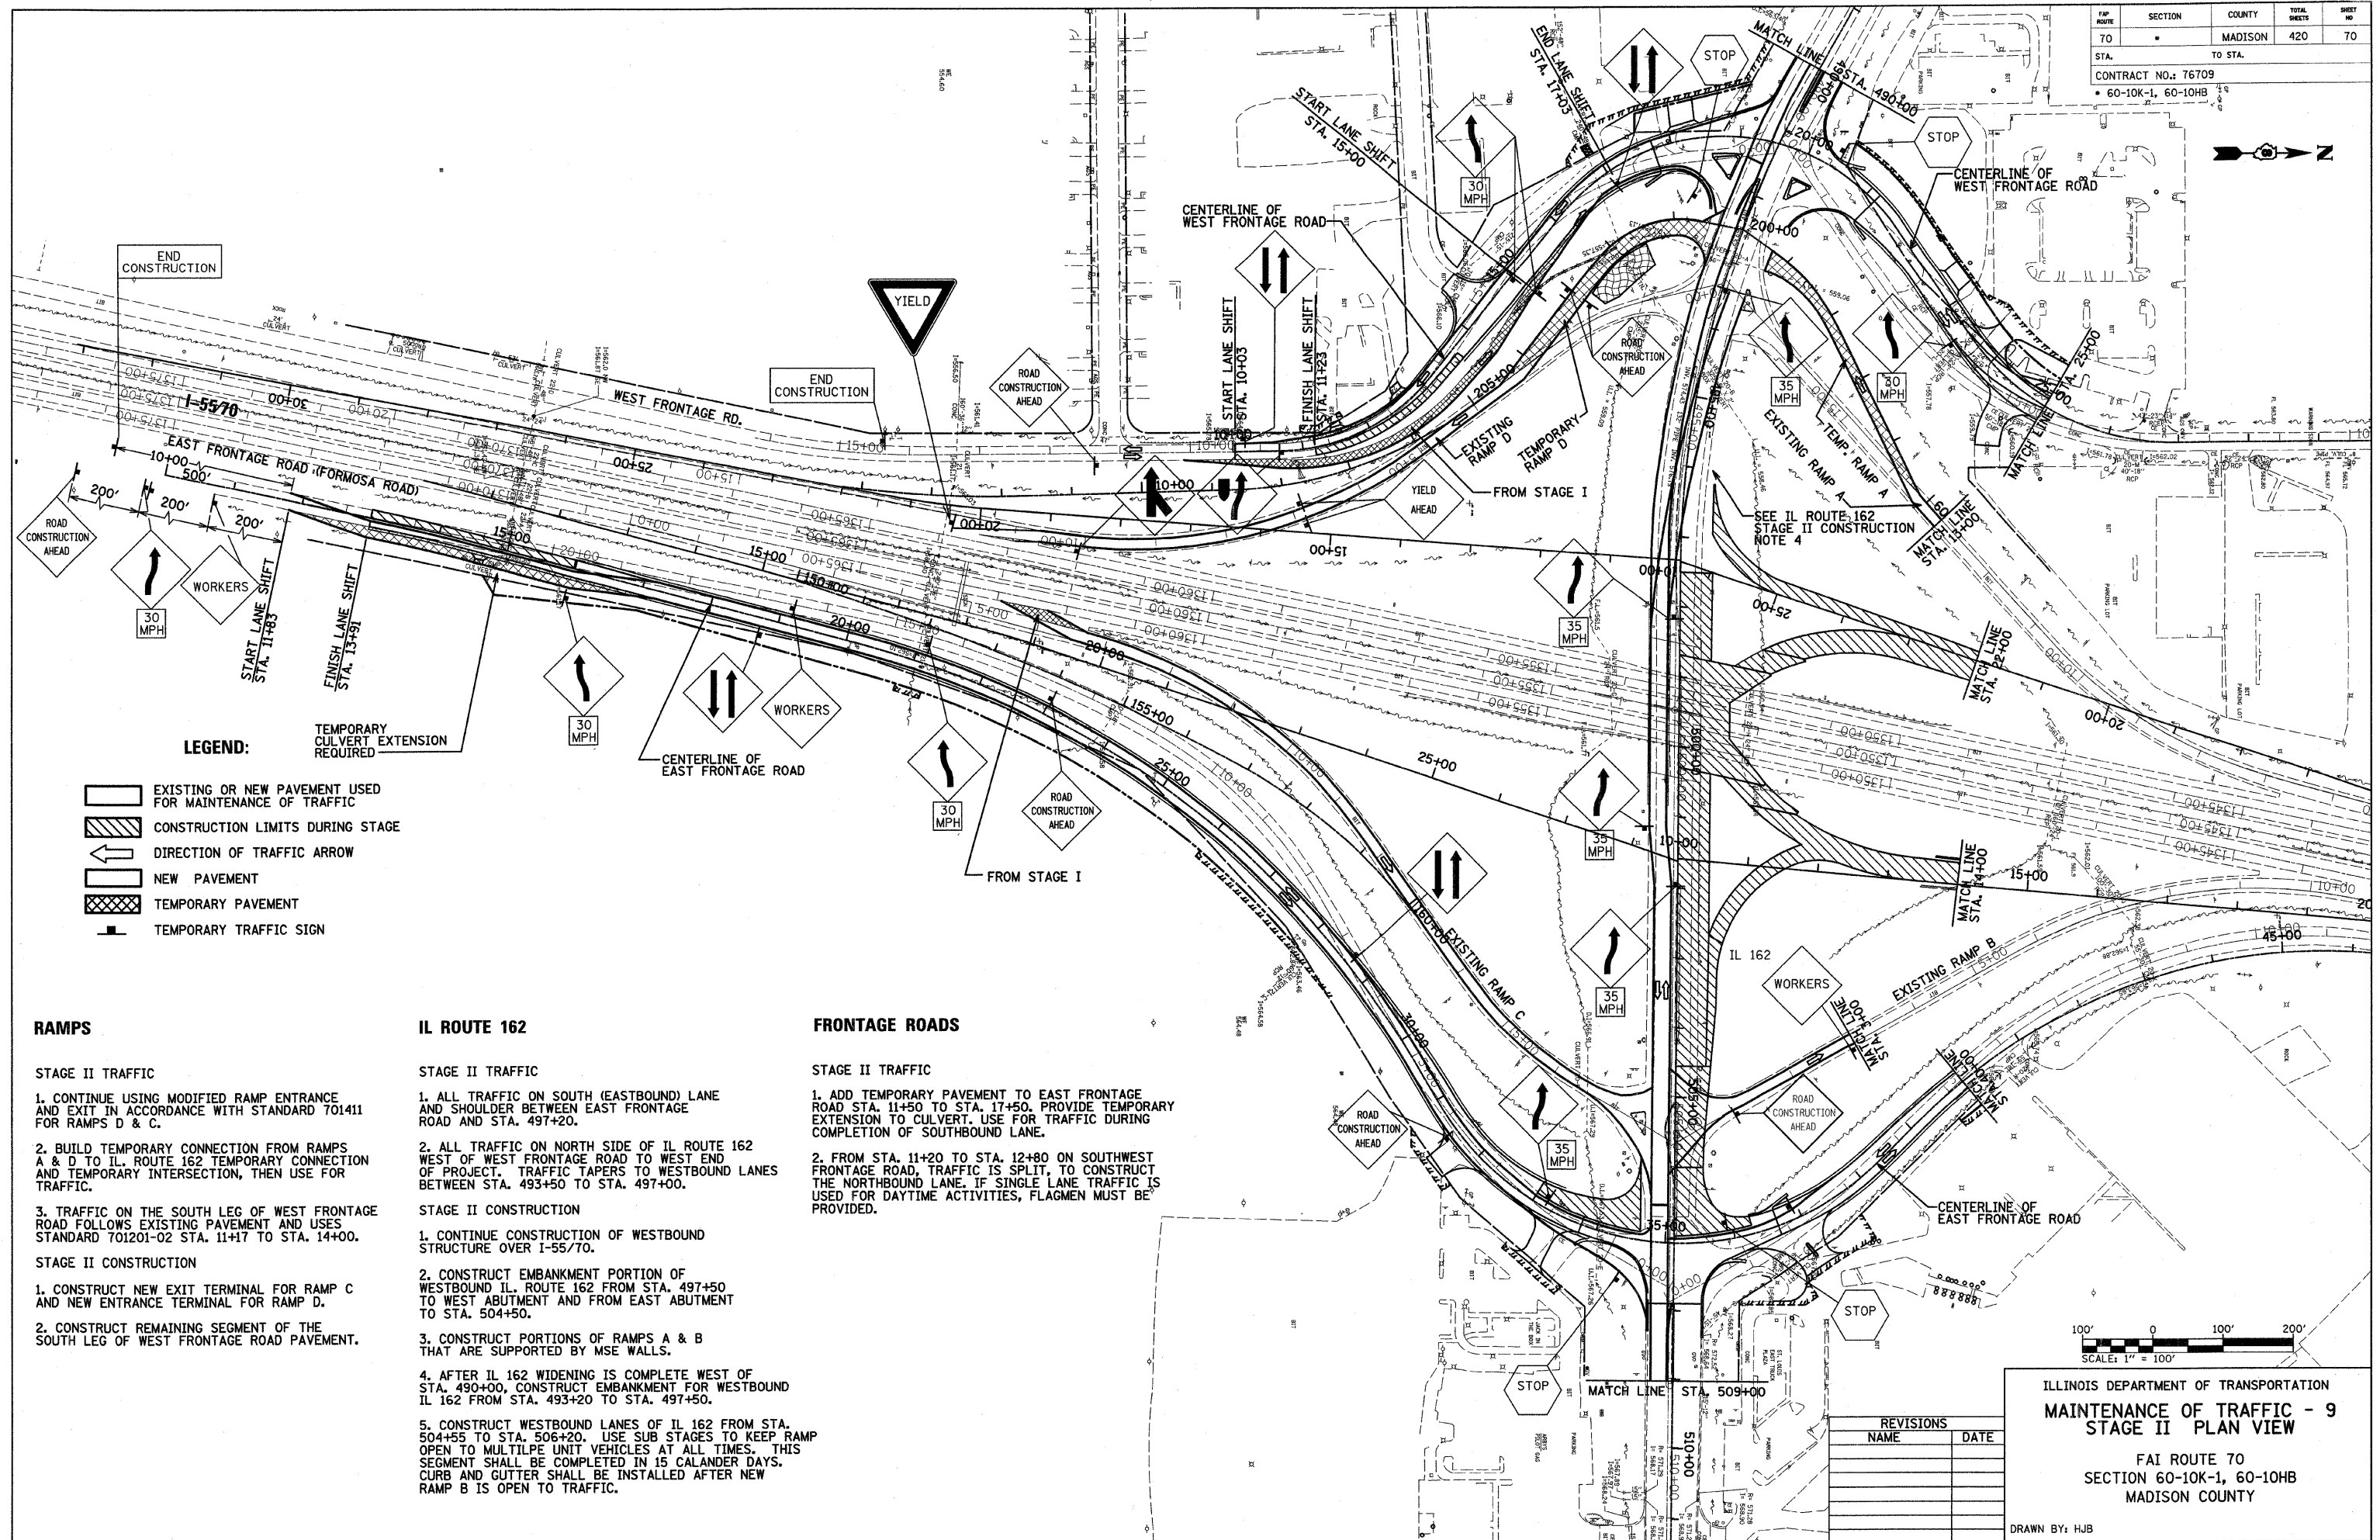


LEGEND:
 TEMPORARY CULVERT EXTENSION REQUIRED

- EXISTING OR NEW PAVEMENT USED FOR MAINTENANCE OF TRAFFIC
- CONSTRUCTION LIMITS DURING STAGE
- DIRECTION OF TRAFFIC ARROW
- NEW PAVEMENT
- TEMPORARY PAVEMENT
- TEMPORARY TRAFFIC SIGN

- RAMPS**
- STAGE II TRAFFIC**
1. CONTINUE USING MODIFIED RAMP ENTRANCE AND EXIT IN ACCORDANCE WITH STANDARD 701411 FOR RAMPS D & C.
 2. BUILD TEMPORARY CONNECTION FROM RAMPS A & D TO IL ROUTE 162 TEMPORARY CONNECTION AND TEMPORARY INTERSECTION, THEN USE FOR TRAFFIC.
 3. TRAFFIC ON THE SOUTH LEG OF WEST FRONTAGE ROAD FOLLOWS EXISTING PAVEMENT AND USES STANDARD 701201-02 STA. 11+17 TO STA. 14+00.
- STAGE II CONSTRUCTION**
1. CONSTRUCT NEW EXIT TERMINAL FOR RAMP C AND NEW ENTRANCE TERMINAL FOR RAMP D.
 2. CONSTRUCT REMAINING SEGMENT OF THE SOUTH LEG OF WEST FRONTAGE ROAD PAVEMENT.

- IL ROUTE 162**
- STAGE II TRAFFIC**
1. ALL TRAFFIC ON SOUTH (EASTBOUND) LANE AND SHOULDER BETWEEN EAST FRONTAGE ROAD AND STA. 497+20.
 2. ALL TRAFFIC ON NORTH SIDE OF IL ROUTE 162 WEST OF WEST FRONTAGE ROAD TO WEST END OF PROJECT. TRAFFIC TAPERS TO WESTBOUND LANES BETWEEN STA. 493+50 TO STA. 497+00.
- STAGE II CONSTRUCTION**
1. CONTINUE CONSTRUCTION OF WESTBOUND STRUCTURE OVER I-55/70.
 2. CONSTRUCT EMBANKMENT PORTION OF WESTBOUND IL ROUTE 162 FROM STA. 497+50 TO WEST ABUTMENT AND FROM EAST ABUTMENT TO STA. 504+50.
 3. CONSTRUCT PORTIONS OF RAMPS A & B THAT ARE SUPPORTED BY MSE WALLS.
 4. AFTER IL 162 WIDENING IS COMPLETE WEST OF STA. 490+00, CONSTRUCT EMBANKMENT FOR WESTBOUND IL 162 FROM STA. 493+20 TO STA. 497+50.
 5. CONSTRUCT WESTBOUND LANES OF IL 162 FROM STA. 504+55 TO STA. 506+20. USE SUB STAGES TO KEEP RAMP OPEN TO MULTIPLE UNIT VEHICLES AT ALL TIMES. THIS SEGMENT SHALL BE COMPLETED IN 15 CALENDAR DAYS. CURB AND GUTTER SHALL BE INSTALLED AFTER NEW RAMP B IS OPEN TO TRAFFIC.

- FRONTAGE ROADS**
- STAGE II TRAFFIC**
1. ADD TEMPORARY PAVEMENT TO EAST FRONTAGE ROAD STA. 11+50 TO STA. 17+50. PROVIDE TEMPORARY EXTENSION TO CULVERT. USE FOR TRAFFIC DURING COMPLETION OF SOUTHBOUND LANE.
 2. FROM STA. 11+20 TO STA. 12+80 ON SOUTHWEST FRONTAGE ROAD, TRAFFIC IS SPLIT. TO CONSTRUCT THE NORTHBOUND LANE. IF SINGLE LANE TRAFFIC IS USED FOR DAYTIME ACTIVITIES, FLAGMEN MUST BE PROVIDED.



REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
MAINTENANCE OF TRAFFIC - 9
STAGE II PLAN VIEW

FAI ROUTE 70
 SECTION 60-10K-1, 60-10HB
 MADISON COUNTY

DRAWN BY: HJB
 PLOT DATE: *DATE-TIME*
