



STAGE I REMOVAL
(Looking North)

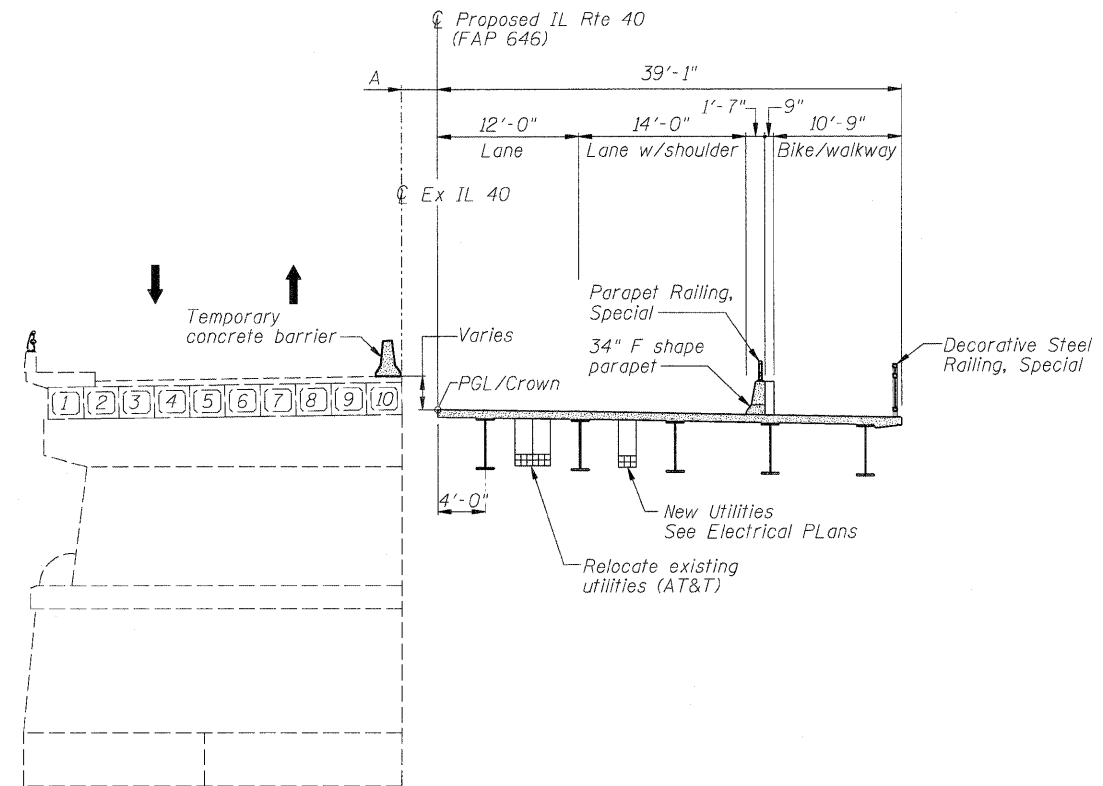

STAGE I CONSTRUCTION
(Looking North)

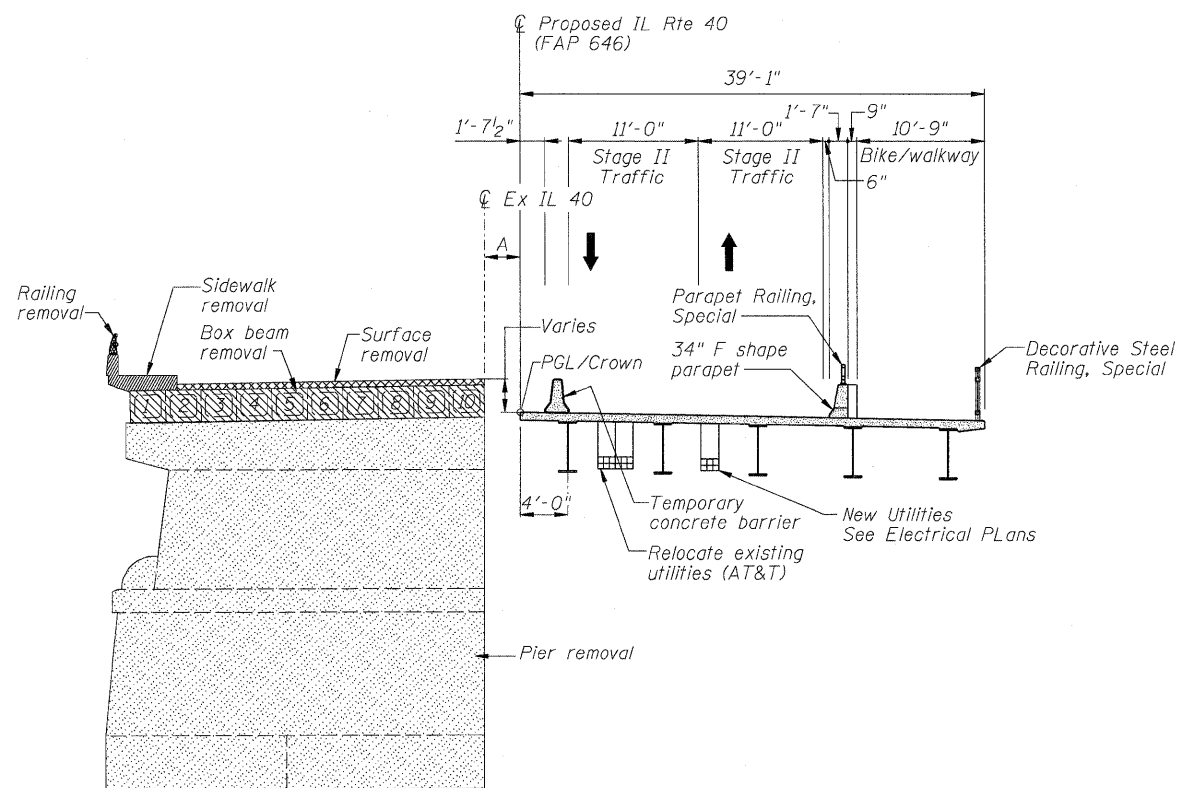

STAGE II REMOVAL

Station	Location	A
734+10.00	Pier 1	2'-9"
733+23.50	Pier 2	3'-2"
732+37.00	Pier 3	3'-7"
731+50.50	Pier 4	4'-0"
730+64.00	Pier 5	4'-5"
729+77.50	Pier 6	4'-10"
728+91.00	Pier 7	5'-2"
728+04.50	Pier 8	5'-6"
727+18.00	Pier 9	5'-9"
726+31.50	Pier 10	6'-3"
725+45.00	Pier 11	6'-8"

NOTES:

The Bridge Removal and Construction Staging Plans are for Information Only and does not relieve the Contractor from responsibility to submit demolition plans according to the contract documents.

The dimension "A" is the approximate distance between the existing and proposed PGL and may not be the exact edge of deck beam 10 due to possible variations of the existing deck beam locations.

All removal items shown are included in Removal of Existing Structures, see special provisions

FILE NAME = 0264880-shr-removalpiers.dgn

USER NAME = dwoznarski

DESIGNED - ACB
CHECKED - JMB

REVISED -
REVISED -
REVISED -
REVISED -

PLOT SCALE = 8.0000' / 1"
PLOT DATE = 7/18/2011

DRAWN - RLK
CHECKED - ACB

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**BRIDGE REMOVAL AND CONSTRUCTION STAGING AT PIERS
STRUCTURE NO. 098-0115**

SHEET NO. 10 OF 103 SHEETS

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
646	IB-2	WHITESIDE	257	113
CONTRACT NO. 64B80			ILLINOIS FED. AID PROJECT	
