


CONTRACT NO. 70519

W1-6L(O)-6030
MOUNTED ON NCHRP-350
APPROVED DEVICE

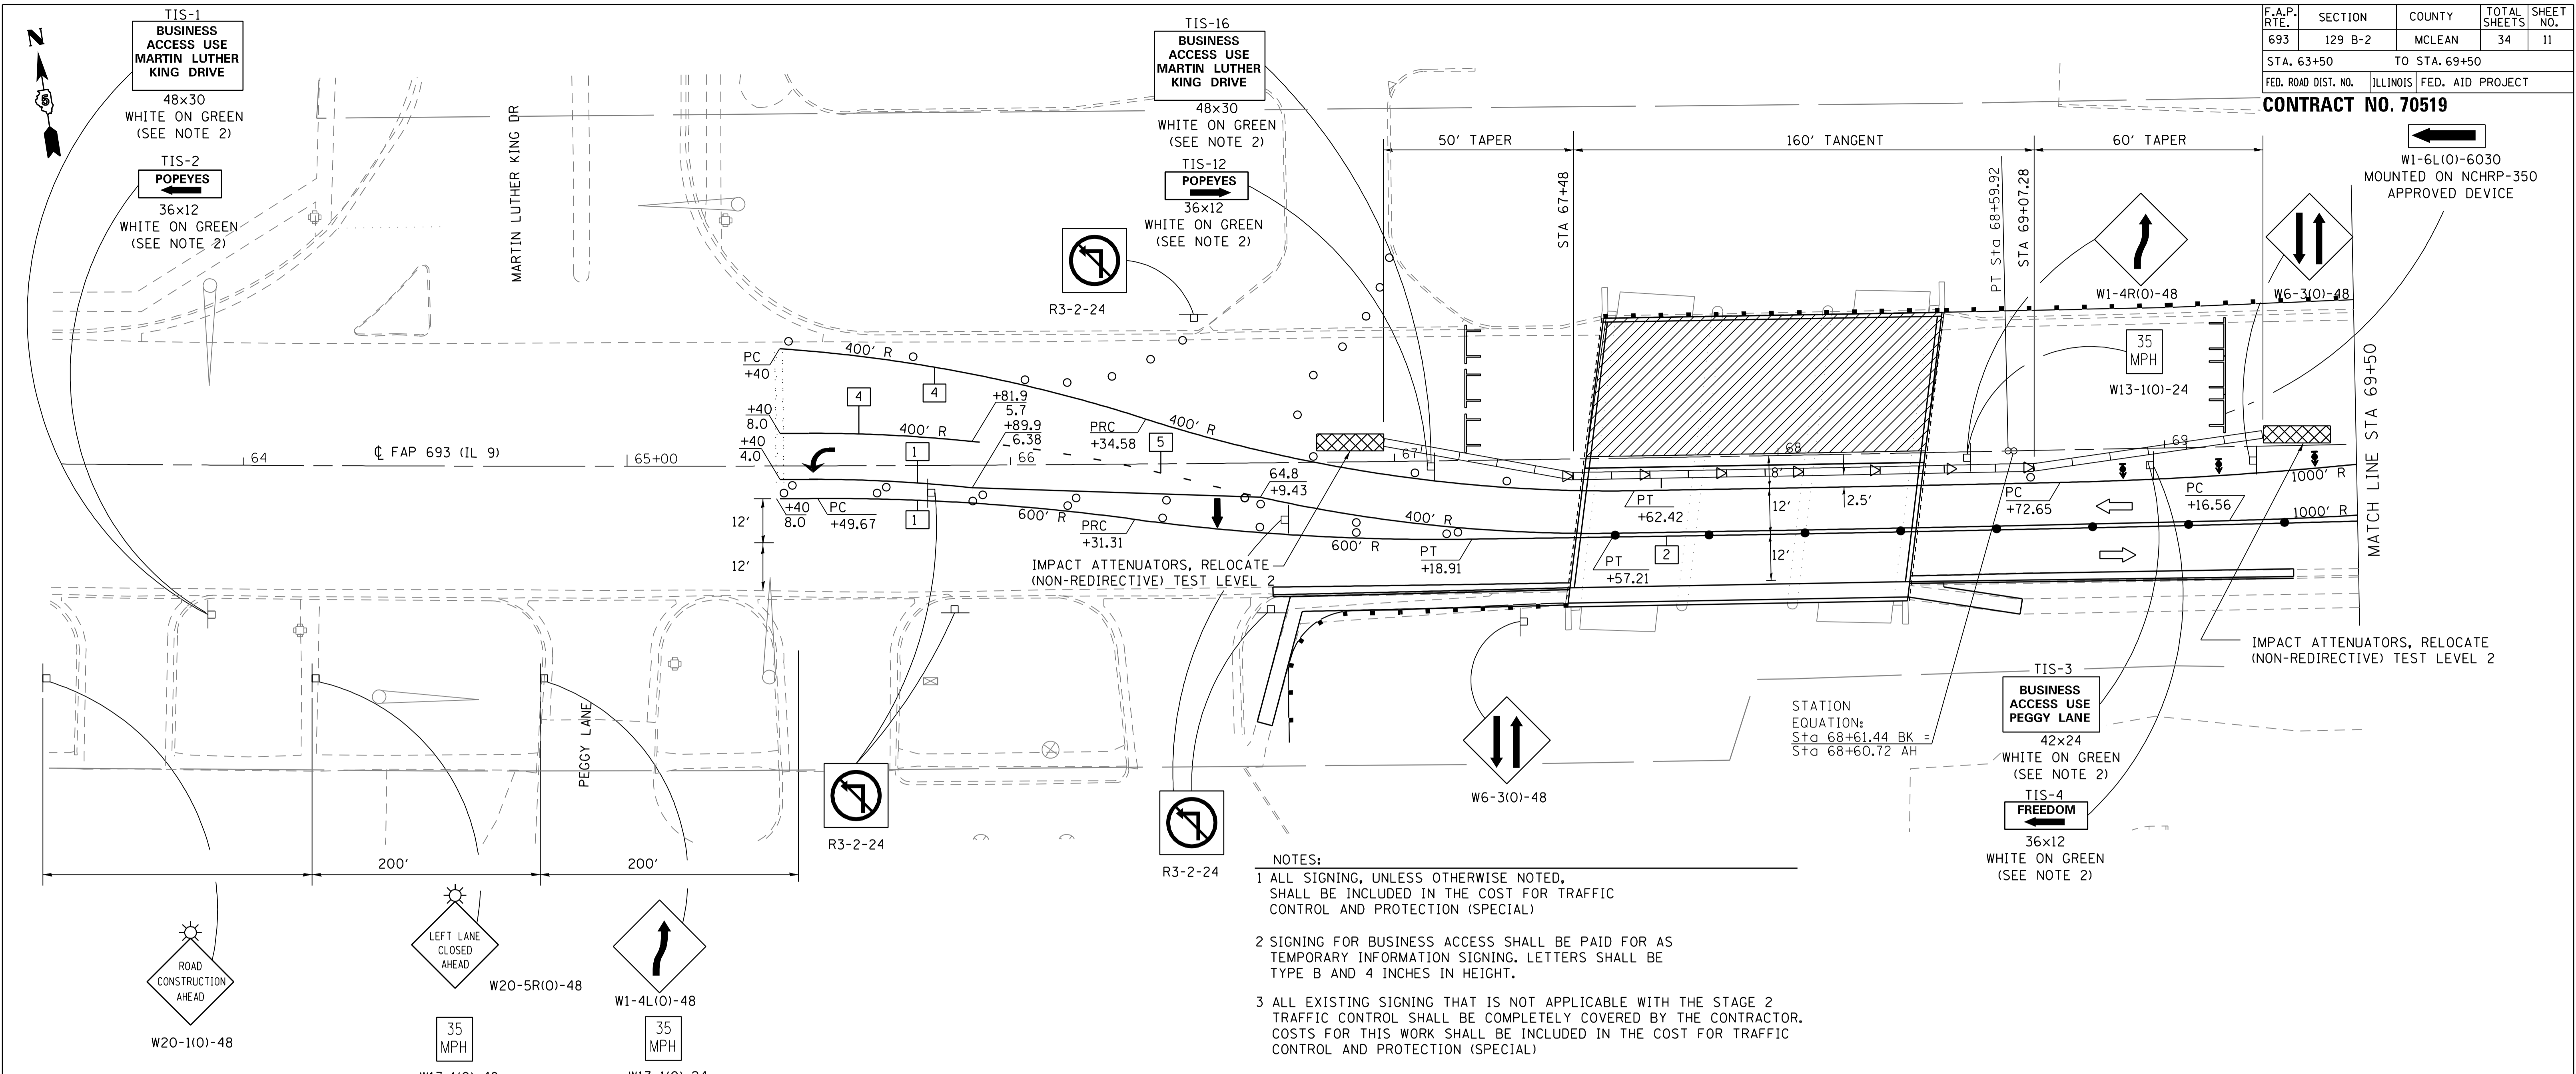

- NOTES:
- 1 ALL SIGNING, UNLESS OTHERWISE NOTED, SHALL BE INCLUDED IN THE COST FOR TRAFFIC CONTROL AND PROTECTION (SPECIAL)
 - 2 SIGNING FOR BUSINESS ACCESS SHALL BE PAID FOR AS TEMPORARY INFORMATION SIGNING. LETTERS SHALL BE TYPE B AND 4 INCHES IN HEIGHT.
 - 3 ALL EXISTING SIGNING THAT IS NOT APPLICABLE WITH THE STAGE 2 TRAFFIC CONTROL SHALL BE COMPLETELY COVERED BY THE CONTRACTOR. COSTS FOR THIS WORK SHALL BE INCLUDED IN THE COST FOR TRAFFIC CONTROL AND PROTECTION (SPECIAL)
 - 4 VERTICAL BARRICADES SHALL BE EQUIPPED WITH MONO-DIRECTIONAL OR BIDIRECTIONAL STEADY BURN LIGHTS AND SHALL BE PLACED AT 25 FOOT INTERVALS ALONG THE WORK ZONE. BARRICADES SHALL BE OMITTED AS DIRECTED BY THE ENGINEER TO ALLOW ACCESS TO COMMERCIAL ENTRANCES.

- SEQUENCE OF OPERATIONS
- STAGE 2:
- 1 RELOCATE TEMPORARY CONCRETE BARRIER AND TRAFFIC CONTROL DEVICES TO CLOSE NORTH SIDE OF BRIDGE
 - 2 REMOVE STAGE 1 TEMPORARY PAVEMENT MARKINGS AND INSTALL STAGE 2 TEMPORARY PAVEMENT MARKINGS
 - 3 RECONSTRUCT STAGE 2 PORTION OF STRUCTURE
 - 4 INSTALL GUARDRAIL AND TERMINALS
 - 5 PLACE HOT-MIX ASPHALT BINDER COURSE ON ABUTMENT FLUSH WITH TOP OF CONCRETE WEARING SURFACE AND EXISTING HOT-MIX ASPHALT
 - 6 BRIDGE DECK GROOVING AND PROTECTIVE COAT

SHEET 1 OF 2

**TRAFFIC CONTROL AND PROTECTION
STAGE 2**

FAP ROUTE 693 (IL 9)
SECTION 129 B-2
MCLEAN COUNTY

CUMMINS ENGINEERING CORPORATION

JOB #: 2114.5
FILE: 2114.5STAGE2
DATE: 12/07/06

TRAFFIC CONTROL LEGEND		TEMPORARY PAVEMENT MARKING LEGEND	
	TYPE III BARRICADE WITH TWO FLASHING LIGHTS		4" SOLID (YELLOW)
	POST MOUNTED SIGN		4" DOUBLE YELLOW (NARROW)
	VERTICAL BARRICADES WITH STEADY BURN MONODIRECTIONAL OR BIDIRECTIONAL LIGHT AT 25 FOOT CENTERS		4" SKIP DASH (WHITE)
	DIRECTION INDICATOR BARRICADES		4" SOLID (WHITE)
	FLASHING LIGHT		4" LANE EXTENSION (WHITE)
	WORK ZONE		LEFT TURN ARROW (WHITE)
	VERTICAL PANEL WITH STEADY BURNING LIGHT AT 20 FOOT CENTERS ON TAPER		
	CRYSTAL MONODIRECTIONAL REFLECTORS AT 20 FOOT CENTERS		
	TEMPORARY CONCRETE BARRIER		
	FLEXIBLE DELINEATORS AT 25 FOOT CENTERS		
	TYPE B ARROW BOARD		

TEMPORARY PAVEMENT MARKING LAYOUT

WESTBOUND LANES			EASTBOUND LANES		
STATION	OUTSIDE EDGE OF PAVEMENT	MEDIAN EDGE OF PAVEMENT	STATION	MEDIAN EDGE OF PAVEMENT	OUTSIDE EDGE OF PAVEMENT
PC +40	-31.03	-8.00	65+40	8.00	EXISTING
65+50	-29.69	-7.98	PC +49.67	8.00	EXISTING
65+75	-26.96	-7.02	65+50	8.00	EXISTING
66+00	-22.07	-4.44	65+75	8.56	EXISTING
66+25	-15.46	-0.22	66+00	10.20	EXISTING
PRC +34.58	-12.46	-	66+25	12.93	EXISTING
PRC +49.92	-	5.67	PRC +31.31	13.79	EXISTING
66+50	-7.74	5.70	66+50	16.16	EXISTING
66+75	-1.45	11.64	66+75	18.44	EXISTING
67+00	3.21	15.97	67+00	19.70	EXISTING
67+25	6.28	18.72	PT +18.91	20.00	EXISTING
67+50	7.80	19.93			EXISTING
PT +57.21	-	20.00	69+00	19.85	EXISTING
PT +62.42	8.00	-	69+25	19.70	EXISTING
			69+50	19.52	EXISTING
PC +72.65	8.00	-			
68+75	7.95	-			
69+00	7.50	-			
PC +16.56	-	20.00			
69+25	6.41	19.70			
69+50	4.70	19.00			
