

SWB+tzf+W
3/29/2007
c:\projects\74160d\shcover.74160.dg

CONTRACT NO. 74160

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
328	(2,3,4)RS-2	EFF./CLAY	17	1

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS

**PROPOSED
HIGHWAY PLANS**

FAP ROUTE 328 (U.S.45)
SECTION (2,3,4)RS-2
RESURFACING (SMART)
EFFINGHAM /CLAY COUNTY

FOR INDEX OF SHEETS, SEE SHEET NO. 2

STATION EQUATIONS

421+55.20 BK = 421+52.02 AH
435+06.06 BK = 435+22.85 AH
444+85.21 BK = 445+26.45 AH
521+00.00 BK = 521+50.74 AH
535+28.70 BK = 544+14.60 AH
650+73.27 BK = 656+42.83 AH
746+35.97 BK = 751+49.07 AH


SAVE & PROTECT MONUMENTS

STA 365+54.27 1.58' LT IP W/CAP
STA 392+24.11 2.49' RT PK NAIL
STA 418+93.27 10.45' LT PK NAIL

BRIDGE OMISSIONS

STA 439+08 TO STA 440+27
STA 503+99 TO STA 506+66
STA 634+52 TO STA 636+39
STA 639+01 TO STA 640+77
STA 806+43 TO STA 806+91

ADT (2006) = 2900




FULL SIZE PLANS HAVE BEEN PREPARED USING STANDARD ENGINEERING SCALES. REDUCED SIZED PLANS WILL NOT CONFORM TO STANDARD SCALES. IN MAKING MEASUREMENTS ON REDUCED PLANS, THE ABOVE SCALES MAY BE USED.

J.U.L.I.E.
JOINT UTILITY LOCATION INFORMATION FOR EXCAVATION
1-800-892-0123

CONTRACT NO. 74160

C-97-066-06

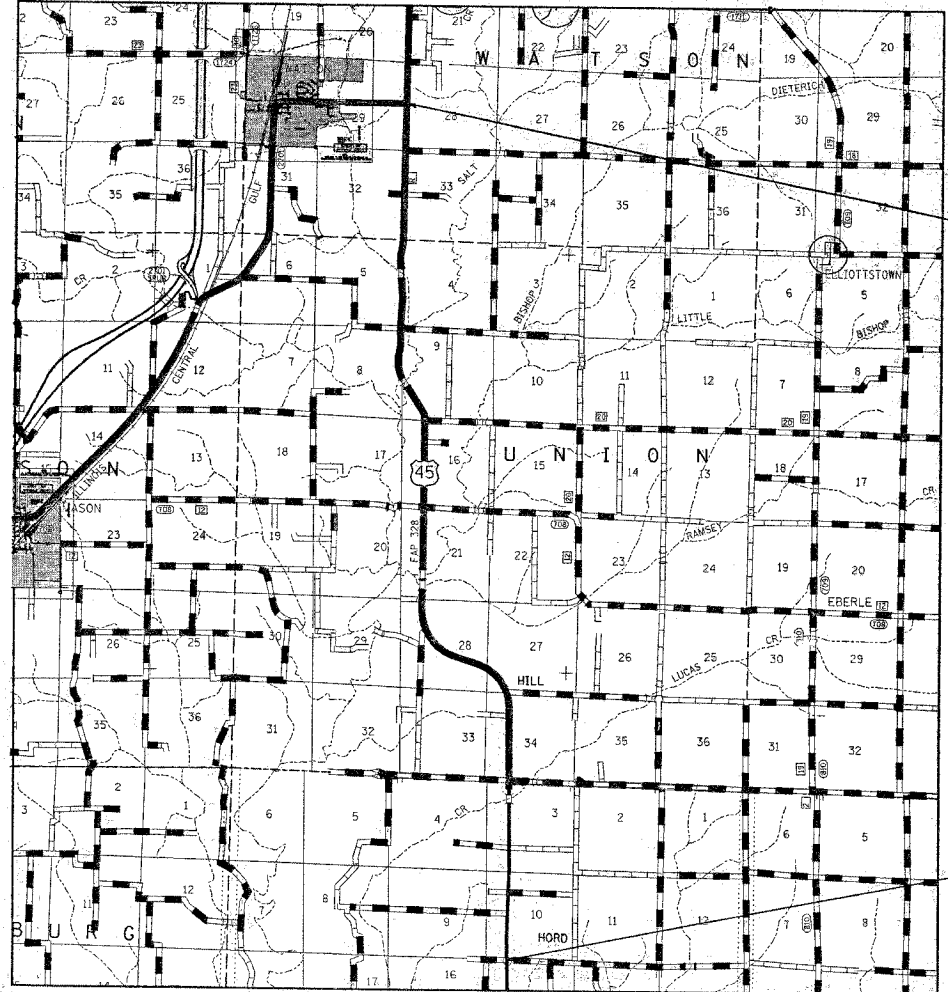

PROJECT BEGINS
STA 349+65



PROJECT ENDS
STA 967+50

GROSS LENGTH = 61785 FEET = 11.70 MILES
NET LENGTH = 58916 FEET = 11.16 MILES

D-97-033-06



LOCATION OF SECTION INDICATED THUS: - ■ -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS

SUBMITTED *March 29th* 2007

Christine M. Reedy
DEPUTY DIRECTOR OF HIGHWAYS, REGION ENGINEER

May 11 2007

Eric E. Harsh
ENGINEER OF DESIGN AND ENVIRONMENT

May 11 2007

Michael S. Sore P.E.
DIRECTOR OF HIGHWAYS, CHIEF ENGINEER

**PRINTED BY THE AUTHORITY
OF THE STATE OF ILLINOIS**

PROJECT ENGINEER: MARK DAUGHERY
SQUAD LEADER: BRIAN LEWIS
DESIGNER: SOLOMON DZAKUMA
TELEPHONE: 217/342-3951 EX 341
