


STANDARD 12'-6" WIDE PANEL LAYOUT FOR ISOLATED PLACEMENT WITH EMBEDDED DOWELS FOR PRECUT WIDE MOUTH SLOTS IN ADJACENT PAVEMENT

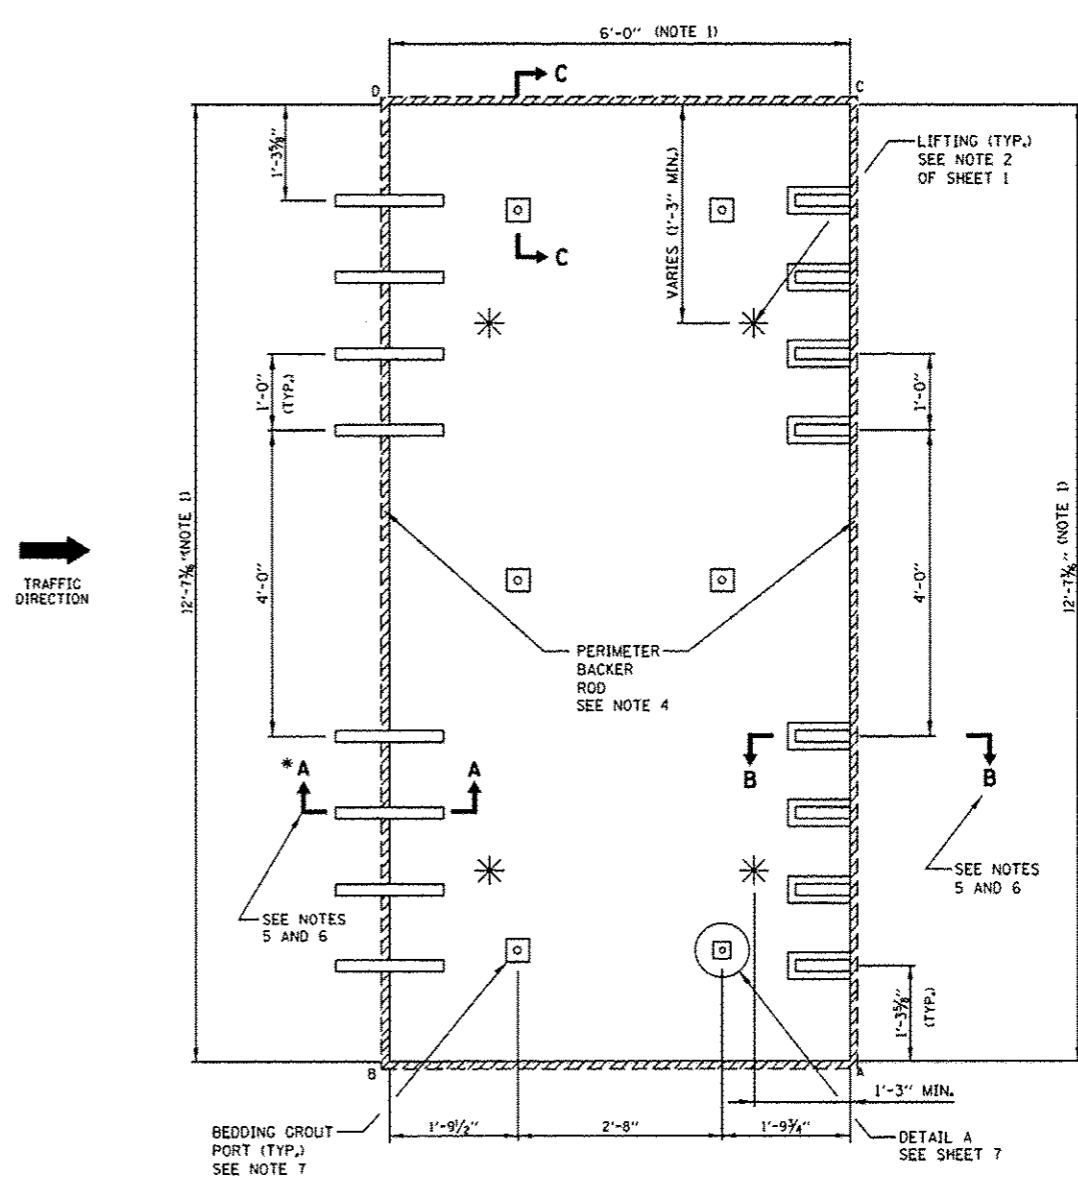

STANDARD 12'-6" WIDE PANEL LAYOUT FOR CONSECUTIVE PLACEMENT

* FOR INTERNAL CONSECUTIVE SLABS, PREFORMED SLOTS IN ACCORDANCE WITH SECTION B-B OF SHEET 4 MAY BE USED IN-PLACE OF EMBEDDED DOWELS OR OF FIELD RETROFITTED DOWEL BARS WITH SAWCUT SLOTS. ALL PREFORMED SLOTS MUST BE FILLED BEFORE BEING OPENED TO TRAFFIC.

NOTES:

1. THE WIDTH AND LENGTH OF PRODUCED SLABS SHALL BE THE INDICATED DIMENSIONS $\pm \frac{1}{8}$ ".
2. FOR MIDDLE LANE SLAB OPENINGS/PATCHES LESS THAN 12'-6" IN WIDTH AND GREATER THAN 11'-6" IN WIDTH, THE STANDARD PERCAST SLAB CAN BE SAW CUT ON-SITE TO FIT THE OPENING AND TO MAINTAIN ALIGNMENT WITH EXISTING LONGITUDINAL JOINTS, OTHERWISE, THE SLAB PATCH LOCATION MUST BE PRESURVEYED BY THE CONTRACTOR AND THE SLAB FABRICATED AS A CUSTOM SLAB.
3. SLAB THICKNESS SHALL BE AS INDICATED IN THE PLANS.
4. A FOAM BACKER ROD SHALL BE PLACED AROUND THE OUTSIDE PERIMETER OF THE SLAB AT THE BOTTOM OF THE JOINTS BEFORE THE SLAB HAS BEEN SET AND BEFORE BEDDING GROUT OR POLYURETHANE LEVELING FILL IS APPLIED. THE BACKER ROD SHALL NOT BE REQUIRED WHEN ANY SLAB IS LEVELLED WITH FLOWABLE FILL.
5. SEE SHEET 7 FOR SECTION DETAILS.
6. IT SHALL BE THE CONTRACTOR'S OPTION TO REPLACE ANY EMBEDDED DOWEL BARS OR PREFORMED SLOTS AS SHOWN ON THESE DRAWINGS WITH FULLY RETROFITTED DOWEL BARS FIELD INSTALLED IN ACCORDANCE WITH 'DETAIL C' OF SHEET 13. THE CONTRACTOR SHALL USE AN APPROVED TEMPLATE TO LOCATE THE SAW CUTS REQUIRED FOR PROPER SPACING AND RETROFITTING OF THE DOWEL BARS IN ACCORDANCE WITH THESE DRAWINGS. DIAMOND BLADED GANG SAWS SHALL BE USED TO MAKE SAW CUTS PERPENDICULAR TO THE TRANSVERSE (NON-SKEWED) JOINT LINE TO ALLOW FOR DOWEL BAR PLACEMENTS WITHIN THE SPECIFIED TOLERANCES.
7. SEE NOTE 8 ON SHEET 1 FOR LOCATING UNDERSEALING GROUT PORTS.

FILE NAME *	USER NAME * PencoPL	DESIGNED - O. PATEL	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	PRECAST CONCRETE PAVEMENT SLABS			F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
st\p\planprep\sqed_2\dearpp\60-56 il	la\jg\quon rd\demond grinding\pcc patching	DRAWN - precast PCC Patching.dgn	REVISED -		575	14-N	WILL	163	113			
PLOT SCALE * 100.0000' / 1"	CHECKED -	REVISED -	REVISED -		BD 57		CONTRACT NO. 60W13					
PLOT DATE * 12/16/2013	DATE - 10-25-2013	REVISED -	REVISED -		SCALE: NONE	SHEET NO. 4 OF 19 SHEETS	STA.	TO STA.	FED. ROAD DIST. NO. 1 ILLINOIS FED. AID PROJECT			
