


TYPICAL SECTION - SUBSTAGE A

RAMP A

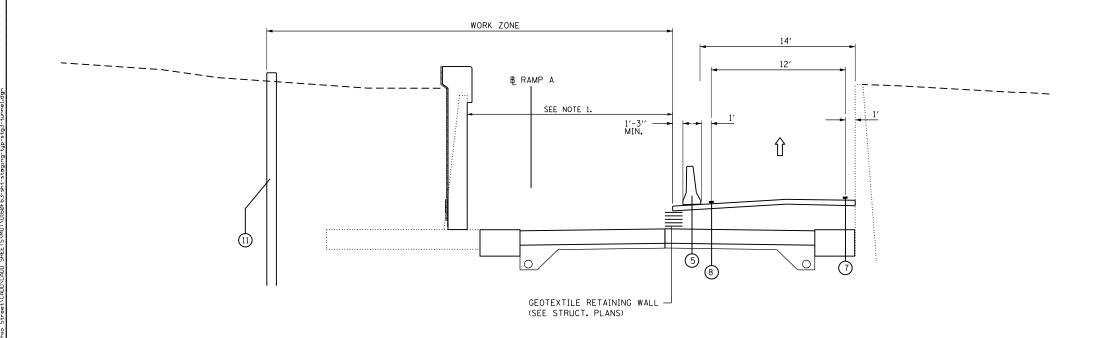

PROPOSED LEGEND:

- 1 TEMPORARY PAVEMENT, 8"
- (2) AGGREGATE SUBGRADE IMPROVEMENT, 4"
- (3) AGGREGATE SHOULDERS, TYPE B, 6"
- (4) TEMPORARY EROSION CONTROL SEEDING
- 5) TEMPORARY CONCRETE BARRIER
- (6) TEMPORARY CONCRETE BARRIER, RELOCATE
- (7) WET REFLECTIVE TEMPORARY TAPE TYPE III LINE 4" WHITE
- 8) WET REFLECTIVE TEMPORARY TAPE TYPE III LINE 4" YELLOW
- (9) WET REFLECTIVE TEMPORARY TAPE TYPE III LINE 4" WHITE (2' DASH 6' SKIP)
- 10) WET REFLECTIVE TEMPORARY TAPE TYPE III LINE 8" WHITE
- (11) TEMPORARY SOIL RETENTION SYSTEM

NOTES:

TO STA.

- 1. SEE STRUCTURAL PLANS FOR LOCATION OF STAGE CONSTRUCTION LINE AND TEMP. SOIL RETENTION DETAILS.
- 2. RAMP C PAVEMENT AND SN 016-2573 SUPERSTRUCTURE OMITTED FOR CLARITY.
- 3. THE TEMPORARY CONCRETE BARRIER SHALL BE SECURED TO THE PAVEMENT USING THREE (3) ANCHORING PINS ON THE TRAFFIC SIDE OF THE BARRIER AT LOCATIONS WHERE A HAZARD OR SLOPE STEEPER THAN 1V:10H EXISTS WITHIN 3 FEET TO THE BARRIER. THE COST OF THIS WORK SHALL BE INCLUDED IN THE CONTRACT UNIT PRICE FOR "TEMPORARY CONCRETE BARRIER", OR "RELOCATE TEMPORARY CONCRETE BARRIER", AS APPLICABLE.
- 4. PRISMATIC BARRIER WALL REFLECTORS SHALL BE INSTALLED ON BOTH THE FACE AND THE TOP OF THE WALL ADJACENT TO TRAFFIC. THE COLOR OF THE REFLECTORS SHALL MATCH THE COLOR OF THE EDGELINES. SEE TRAFFIC CONTROL AND PROTECTION (EXPRESSWAY) SPECIAL PROVISION.

COLLINS ENGINEERS

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

TYPICAL SECTION - SUBSTAGE B

RAMP A

STAGING AND TRAFFIC CONTROL
RAMP A TYPICAL SECTIONS
STAGE III

SHEET NO. OF SHEETS STA.
