


### SIGN SCHEDULE

SIGN	MUTCD DESIGNATION	SIZE	QUANTITY
	M4-9	30in X 24in	10
	M4-9L	30in X 24in	4
	M4-9R	30in X 24in	4
	SPECIAL **	84in X 24in	9
	W20-2	48in X 48in	2
	M3-2	24in X 12in	8
	M3-4	24in X 12in	10
	SPECIAL **	36in X 12in	29
	M4-8A	30in X 24in	2
	W20-3(0)	36in X 36in	6
	SPECIAL **	36in X 36in	4
	SPECIAL **	84in X 24in	2
	SPECIAL **	84in X 24in	5
	SPECIAL **	36in X 36in	5
	R11-4	60in X 30in	1
	SPECIAL **	48in X 48in	1
	SPECIAL **	84in X 36in	2

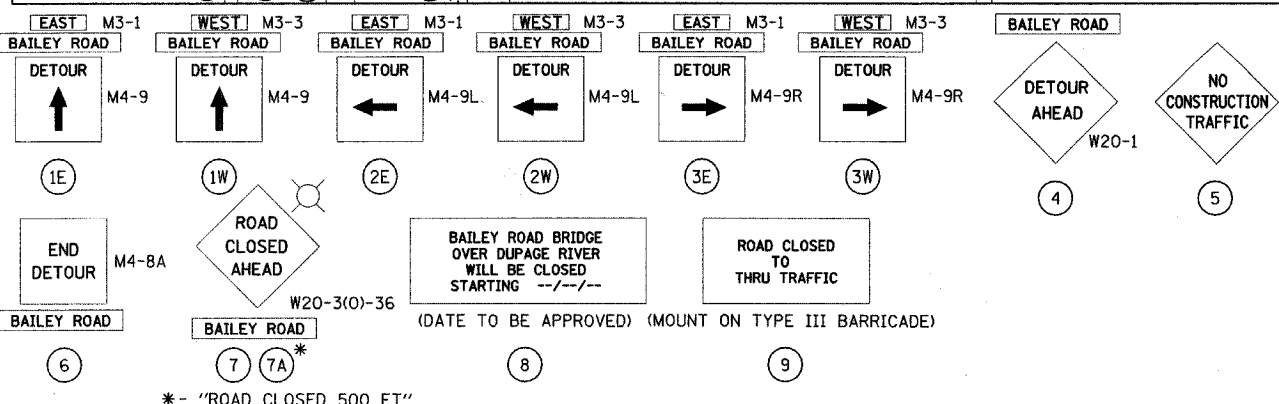

- NOTES:**
- ALL DETOUR SIGNS SHALL BE IN ORANGE COLOR BACKGROUND WITH BLACK LETTERS.
  - FOLLOW LATEST MUTCD MANUAL AND IDOT STANDARDS FOR DETOUR SIGNS AND MAINTENANCE OF TRAFFIC SIGNS.
  - THE DETOUR SIGNING SHALL BE PAID AS TRAFFIC CONTROL AND PROTECTION FOR TEMPORARY DETOUR.
  - SIDEWALK CLOSURE SIGNING SHALL BE PER STANDARD 701801, AND INCLUDED IN THE COST OF TRAFFIC CONTROL AND PROTECTION FOR TEMPORARY DETOUR.
  - MAINTAIN ACCESS TO ALL DRIVEWAYS AT ALL TIMES.
  - SEE MAINTENANCE OF TRAFFIC DUPAGE RIVER TRAIL CLOSURE DETAILS.

\*\* - SPECIAL CUSTOM SIGNS SHALL BE PAID FOR AS TEMPORARY INFORMATION SIGNING.

<b>REVISIONS</b> NAME      DATE		BRIDGE REHABILITATION BAILEY ROAD OVER WEST BRANCH OF THE DUPAGE RIVER <b>MAINTENANCE OF TRAFFIC          DETOUR - STAGE 2</b>	City of  <b>Naperville</b>
CONSULTANT <b>TYLIN INTERNATIONAL</b>			
DRAWN: RTM CHECKED: SP APPROVED: DATE: JULY 13, 2007 SCALE: NONE		SHEET NO. <h1 style="text-align: center;">11</h1>	
JOB NO.: C-91-062-04		PROJECT NO.: BHM-8003(343)	

\* - "ROAD CLOSED 500 FT"
