


WI-4L-48

NOTES

- BRIDGE REHABILITATION WORK TO BE COMPLETED UTILIZING STAGE CONSTRUCTION WITH TWO LANES OF EB I-72 REMAINING OPEN TO TRAFFIC ON BRIDGE. SEE SPECIAL PROVISIONS FOR DETAILS.
- THIS SHEET TO BE USED IN CONJUNCTION WITH TRAFFIC CONTROL & PROTECTION STANDARD 701400, 701402, 701411, AND 701451.
- UPON COMPLETION, REMOVE ALL TRAFFIC CONTROL ITEMS IN ACCORDANCE WITH THE STANDARD SPECIFICATIONS.
- THE USE OF METAL SIGNS ON TYPE III BARRICADES SHALL NOT BE ALLOWED, AS IT IS NOT COMPLIANT WITH NCHRP 350.

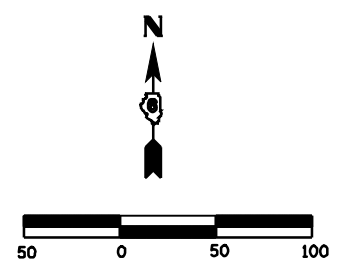

LEGEND

- WORK AREA
- DIRECTION OF TRAFFIC
- TEMPORARY PAVEMENT MARKING TAPE, TYPE 3
- TEMPORARY CONCRETE BARRIER WITH BARRIER WALL REFLECTORS AND VERTICAL PANELS PER STD. 701402
- TYPE I BARRICADE DRUM W/ STEADY BURN MONO DIRECTIONAL LIGHT @ 50' CENTERS U.N.O.
- TYPE III BARRICADE

URETHANE PAVEMENT MARKING - LINE 5"

| LOCATION | YELLOW SOLID (FOOT) | WHITE SOLID (FOOT) | WHITE SKIP-DASH (FOOT) |
|-------------------------------------|---------------------|--------------------|------------------------|
| I-72 EB STA 663+10 TO STA 680+10 | 1700 | 1693 | 425 |
| TOTAL | | | 3,818 |

URETHANE PAVEMENT MARKING - LINE 6"

| LOCATION | WHITE SOLID (FOOT) |
|--|--------------------|
| I-72 EB ENT RAMP GORE STA 671+02 TO STA 672+73 | 344 |
| I-72 EB EXIT RAMP GORE STA 671+02 TO STA 672+73 | 557 |
| TOTAL | 901 |

TEMPORARY RAISED REFLECTIVE PAVEMENT MARKERS @ 50' CENTERS

INSTALL ADVANCE SIGNS AND BARRICADES SEE STD. 701400 AS DIRECTED BY ENGINEER

WORK AREA SN 084-0077

EXIT OPEN AHEAD D4-I102(G)

SEE STAGE II SHEET 9 OF 16

SEE SHEET X OF X FOR DETAILS

TEMPORARY PAVEMENT MARKING TAPE, TYPE 3 FOR INFORMATION ONLY

| STATION TO | STATION | FOOT |
|------------|--------------|-------------|
| 670+10.00 | 678+10.00 | 200 |
| 670+10.00 | 678+10.00 | 800 |
| 670+10.00 | 677+65.00 | 755 |
| 675+05.00 | 676+54.00 | 38 |
| 676+54.00 | 678+10.00 | 156 |
| 676+54.00 | 677+67.00 | 113 |
| | TOTAL | 2062 |

RELOCATE TEMPORARY CONCRETE BARRIER

| STATION TO | STATION | FOOT |
|------------|-----------|-------|
| 671+23.55 | 675+10.00 | 387.5 |


TEMPORARY RAISED REFLECTIVE MARKER

| STATION TO | STATION | EACH |
|------------|-----------|------|
| 671+18.00 | 676+68.00 | 12 |

IMPACT ATTENUATOR, RELOCATE (FULLY REDIRECTIVE), TEST LEVEL 3

| STATION | EACH |
|-----------|------|
| 671+23.35 | 1 |

- ① TEMP. PAVT. MARKING TAPE, TYPE 3, YELLOW
- ② TEMP. PAVT. MARKING TAPE, TYPE 3, WHITE
- ③ TEMP. PAVT. MARKING TAPE, TYPE 3, WHITE (10' DASH, 30' SKIP)
- ④ TEMP. PAVT. MARKING TAPE, TYPE 3, WHITE (2' DASH, 6' SKIP)

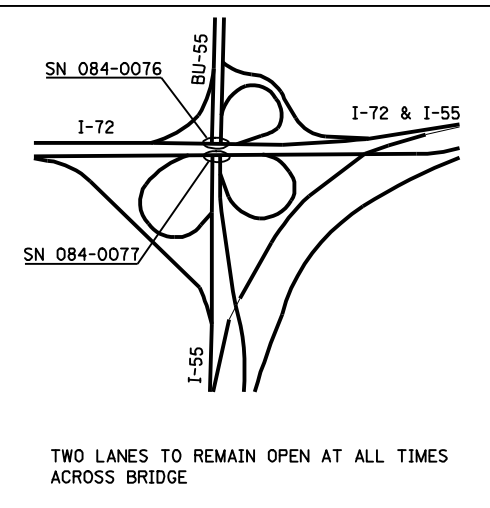

TWO LANES TO REMAIN OPEN AT ALL TIMES ACROSS BRIDGE

KEY MAP

STANDARD 701402 (SPECIAL)
