


GENERAL NOTES		WATER LEVEL DATA	
Begin Drilling	05-03-2001	While Drilling	4.20 ft
Complete Drilling	05-03-2001	At Completion of Drilling	1.50 ft
Drilling Contractor	Windy City Drilling Drill Rig CME 45	Time After Drilling	24 hours
Driller	Gabriel Logger T. Chen	Depth to Water	NA
Checked by	P. Wang	The stratification lines represent the approximate boundary between soil types; the actual transition may be gradual.	
Drilling Method	3.25" ID HSA; backfilled w/ bentonite chip.		



GENERAL NOTES		WATER LEVEL DATA	
Begin Drilling	05-03-2001	While Drilling	6.00 ft
Complete Drilling	05-03-2001	At Completion of Drilling	3.20 ft
Drilling Contractor	Windy City Drilling Drill Rig CME 45	Time After Drilling	24 hours
Driller	Gabriel Logger T. Chen	Depth to Water	NA
Checked by	P. Wang	The stratification lines represent the approximate boundary between soil types; the actual transition may be gradual.	
Drilling Method	3.25" ID HSA; backfilled w/ bentonite chip.		

SOIL BORING LOGS-I  
 STRUCTURE NO. 049-W019

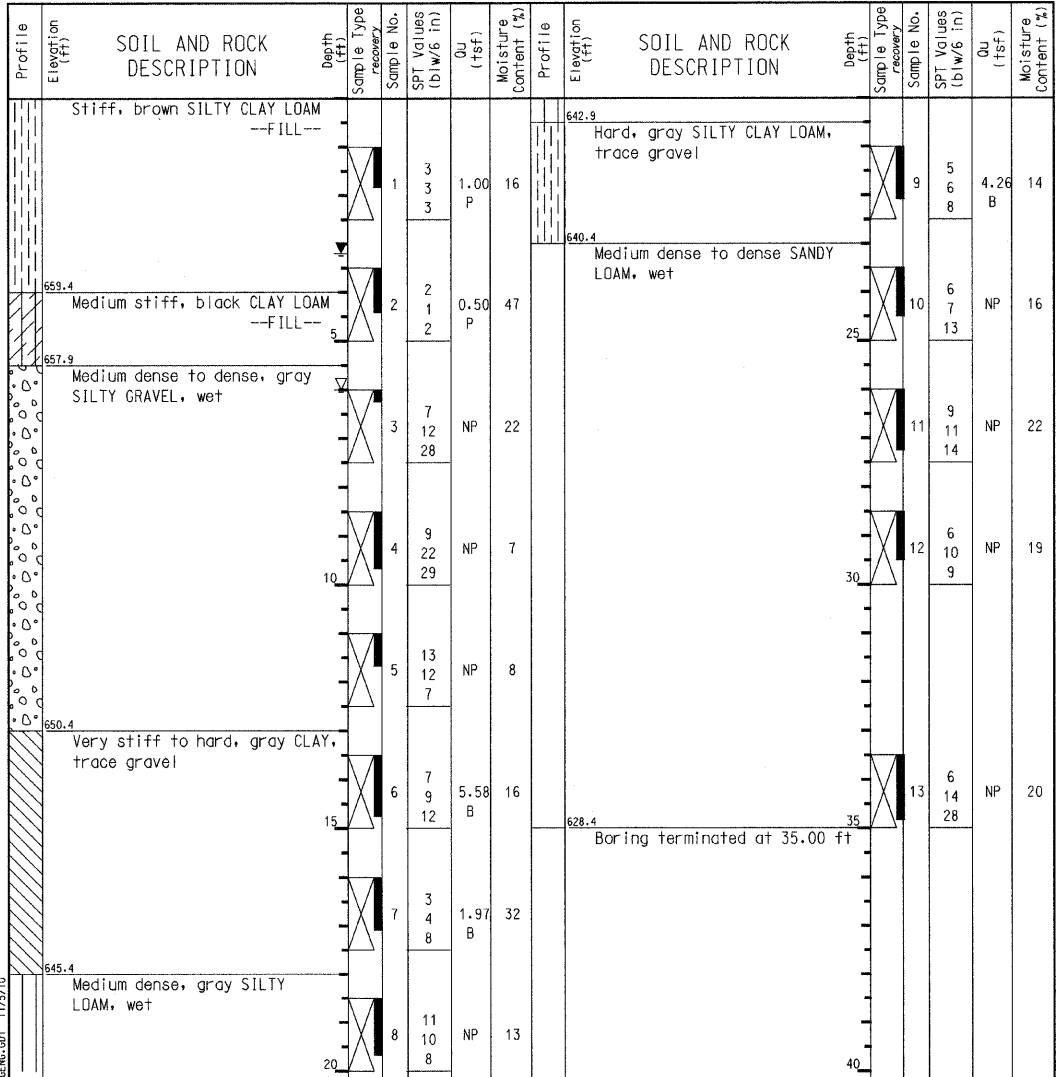

FILE NAME = D:\68963-07-boring_logs-1.dgn	USER NAME =	DESIGNED - J.C.N./B.N.S.	REVISED -
		CHECKED - B.N.S.	REVISED -
		DRAWN - F.M.	REVISED -
		CHECKED - B.N.S./J.C.N.	REVISED -

STATE OF ILLINOIS  
 DEPARTMENT OF TRANSPORTATION

SOIL BORING LOGS-I  
 STRUCTURE NO. 049-W019  
 SHEET NO. S3-7 OF S3-9 SHEETS

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
330	128R-3	LAKE	518	307
CONTRACT NO. 60953				
ILLINOIS FED. AID PROJECT				
