

F.A.S. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
642	99-00124-01-PV	COLES	157	17
STA.		TO STA.		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

**CULVERT SCHEDULE**

SIDE	STATION	REMARKS	RCCP, TYPE 1				RCCP, TYPE 2	RCCP, TYPE 7	CSCP, TYPE 1			TEMP. PIPE CULVERT CLASS D, TYPE 1		METAL END SECTION			PRC FLARED END SECTION					INLET, TYPE A, TYPE 8 GRATE, TEMP.	TRENCH BACKFILL	
			15"	18"	24"	36"	ELP. EQUIV. 36"	36"	36"	ARCH EQUIV. 18"	ARCH EQUIV. 24"	ARCH EQUIV. 36"	12"	24"	EQUIV. 18"	EQUIV. 24"	EQUIV. 36"	15"	18"	24"	36"	EQUIV. 36"	EACH	CU. YD.
LT	102+81	FIELD ENTRANCE								45					2									
RT	103+01	FIELD ENTRANCE								43					2									
	103+50	ACROSS ROAD					64														2			
LT	107+05	FIELD ENTRANCE								43					2									
	118+00	ACROSS ROAD							160											2				
	120+78	ACROSS ROAD			128																			
	123+05	ACROSS ROAD			168															2			7.5	
	125+00	ACROSS ROAD (TEMPORARY)										68											2.0	
	138+00	ACROSS ROAD (TEMPORARY)											70										23.0	
	138+00	ACROSS ROAD							75															
LT	138+00	OULET FROM MANHOLE							23															
LT	144+00	ACROSS ROAD (TEMPORARY)										30									1		0.7	
	148+00	ACROSS ROAD					64														1		3.7	
LT	148+00	TEMPORARY EXTENSION					12														1			
RT	149+48	COMMERCIAL ENTRANCE		56															2					
LT	149+50	ACROSS ROAD (TEMPORARY)										24										1	0.9	
LT	150+63	FIELD ENTRANCE									53				2									
RT	152+64	COMMERCIAL ENTRANCE		72															2					
LT	154+27	PRIVATE ENTRANCE									43				2									
LT	156+70	FIELD ENTRANCE									50				2									
LT	158+00	158+00 LT TO 159+00 LT										100											3.2	
RT	158+40	LOGAN STREET				80														2				
LT	163+00	FIELD ENTRANCE									49				2									
RT	163+00	FIELD ENTRANCE										55			2									
JUGHANDLE																								
	104+98	ACROSS ROAD					56														2			
LT	114+26	DETENTION OUTLET		16															2					
	115+85	ACROSS ROAD					96														2			
MASTERFOODS, USA																								
LT	23+84	EXTEND CULVERT	8																1					
TOTALS			8	144	296	80	292	98	160	43	283	55	222	70	2	12	2	1	6	4	6	8	1	41.0

**GUARDRAIL MARKER SCHEDULE**


LOCATION	GUARDRAIL MARKERS TYPE A	MONODIRECTIONAL PRISMATIC BARRIER REFLECTOR
	EACH	EACH
108+57, RT	1	
109+37, RT	1	
110+17, RT	1	
110+81, LT	1	
110+97, RT	1	
111+77, RT	1	
112+57, RT	1	
114+81, LT	1	
116+57, RT	1	
118+81, LT	1	
120+57, RT		1
122+81, LT		1
124+57, RT	1	
126+81, LT		1
128+57, RT	1	
130+81, LT		1
131+61, LT		1
132+41, LT		1
132+57, RT	1	
133+21, LT		1
134+01, LT		1
134+81, LT	1	
136+57, RT	1	
TOTALS	15	8

**EXPLORATION TRENCH 52" DEPTH SCHEDULE**

STATION TO STATION	LENGTH
	LIN FT
100+00 TO 120+45	2045
122+75 TO 135+50	1275
137+75 TO 151+65	1390
155+25 TO 157+45	220
159+65 TO 166+00	635
TOTAL	5565

**DELINEATOR SCHEDULE**

LOCATION	DELINEATOR
	EACH
100+95 LT & RT	2
102+20 - 109+35 LT & RT	24
@ 65" SPACING	
110+60 LT & RT	2
112+50 LT & RT	2
114+50 LT & RT	2
TOTAL	32

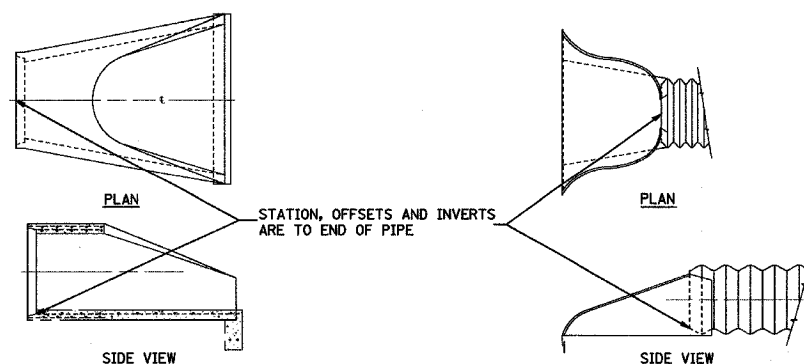

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

**SCHEDULES**

SCALE: VERT.  
HORIZ.  
DATE 04/08/2005

DRAWN BY RLH  
CHECKED BY MED
