

ROUTE NO.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
FAU 7432	*	MACON	47	19
FED. ROAD DIST. NO.	ILLINOIS	PROJECT		

• 08-00602-00-BR

WEST CURB LINE

Location	Station	Offset	Theoretical Grade Elevations
Back N. Abut	10+72.27	-15.00	638.82
A	10+82.27	-15.00	638.74
B	10+92.27	-15.00	638.62
End of North appr pavement	11+02.27	-15.00	638.52

WEST EDGE OF PAVEMENT

Location	Station	Offset	Theoretical Grade Elevations
Back N. Abut	10+73.08	-12.00	638.85
A	10+83.08	-12.00	638.78
B	10+93.08	-12.00	638.71
End of North appr pavement	11+03.08	-12.00	638.63

☉ PROFILE GRADE LINE

Location	Station	Offset	Theoretical Grade Elevations
Back N. Abut	10+76.29	0.00	639.03
A	10+86.29	0.00	638.97
B	10+95.29	0.00	638.89
End of North appr pavement	11+06.29	0.00	638.81

STAGE CONSTRUCTION JOINT


Location	Station	Offset	Theoretical Grade Elevations
Back N. Abut	10+75.90	-1.46	639.01
A	10+85.90	-1.46	638.95
B	10+95.90	-1.46	638.87
End of North appr pavement	11+05.90	-1.46	638.79

EAST EDGE OF PAVEMENT

Location	Station	Offset	Theoretical Grade Elevations
Back N. Abut	10+79.51	12.00	638.81
A	10+89.51	12.00	638.74
B	10+99.51	12.00	638.66
End of North appr pavement	11+09.51	12.00	638.58

EAST CURB LINE

Location	Station	Offset	Theoretical Grade Elevations
Back N. Abut	10+80.31	15.00	638.77
A	10+90.31	15.00	638.68
B	11+00.31	15.00	638.56
End of North appr pavement	11+10.31	15.00	638.46

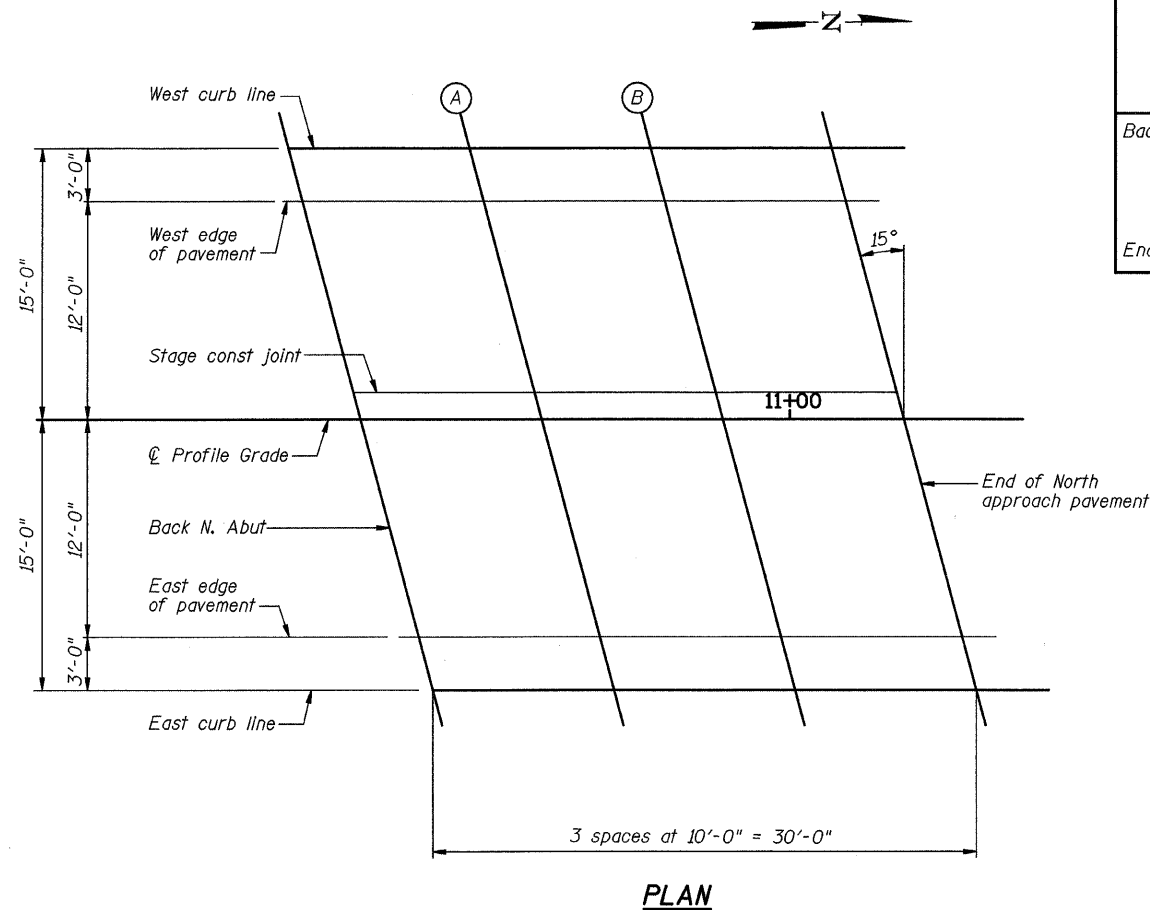

MACARTHUR ROAD (FAU 7432) OVER STEVENS CREEK

TOP OF NORTH APPROACH SLAB ELEVATIONS

REVISIONS	SECTION 08-00602-00-BR	MACARTHUR ROAD (FAU 7432)	DRAWN BY DATE
1	STA 10+00.00	SN 058-6025	R KING 07/09
2		MACON COUNTY	CHECKED BY DATE
3			JMS 07/09
4			BOOK NUMBER
5			486
6			PROJECT No.
7			5307
8			SHEET No.
9			
10			

HOMER L. CHASTAIN & ASSOCIATES, LLP
CONSULTING ENGINEERS
DECATUR CHICAGO
(217) 422-8844 (773) 714-0000
ROCKFORD
(815) 489-0000
184-00177
