


F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
326	*	LIVINGSTON	354	27
STA.		TO STA.		
FED. ROAD DIST. NO.		ILLINOIS	FED. AID PROJECT	
* (123)123XRS-3, (124)IRS-5, (123)BR-3				







INFORMATION BASED ON
REVISED SURVEY 09/03.

OLD PT. NO.	REVISED PT. NO.	STATION	NORTHING	EASTING	ELEVATION
8	10	734+88.06	1540777.463	961871.604	0
9	-	747+29.93	1539535.801	961894.035	0
10	11	757+49.62	1538516.403	961918.888	0
11	-				0
102	-				0
12	-	810+48.73	1533218.577	962035.495	0
105	-				0
13	-	863+41.36	1527926.893	962135.616	0
107	-	876+13.43	1526655.056	962159.476	0
108	-				0
14	-	909+60.75	1523308.317	962222.232	0
15	-	922+60.91	1522008.940	962169.780	0
16	301	943+54.23	1519915.757	962212.118	0
114	-				0
17	14	969+95.26	1517275.254	962264.890	0
115	-	988+01.72	1515469.125	962299.357	0
116	-	1004+11.53	1513859.606	962330.072	0
18	15	1023+57.43	1511914.061	962366.867	0
117	-	1035+85.35	1510686.371	962390.594	0
118	-				0
19	16	1076+42.12	1506630.358	962468.993	0
120	-				0
121	-				0
20	17	1129+35.94	1501337.425	962565.881	0
122	-				0
123	-				0
21	18	1182+25.66	1496048.350	962648.870	0
124	-				0
					0
					0
22	-	1228+27.19	1491447.537	962730.134	0
					0
					0
23	-	1241+73.46	1490101.317	962741.836	0
					0
					0
130	-	1257+88.66	1488486.735	962787.585	0
24	19	1271+95.20	1487080.769	962827.712	0
131A	283	1275+28.95	1486747.129	962836.258	0
133	20	1283+14.30	1485962.047	962856.923	0



REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION
 F.A.P. ROUTE 326 (IL47)
 ALIGNMENT TIE SHEET
 IDOT CONTROL POINTS
 & BENCHMARKS
 SCALE: VERT. DRAWN BY
 HORIZ. CHECKED BY
 DATE

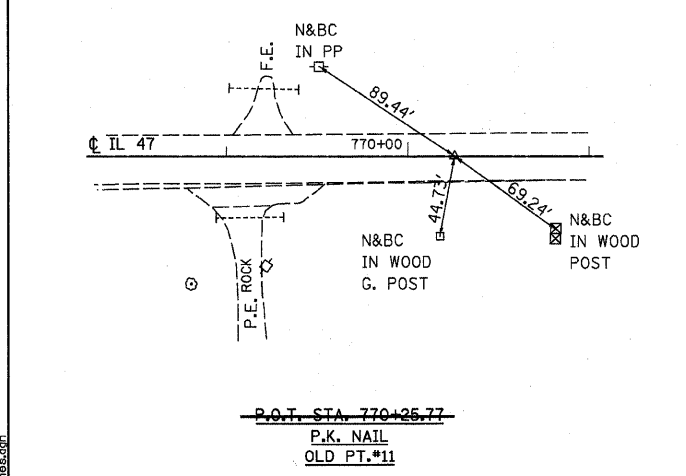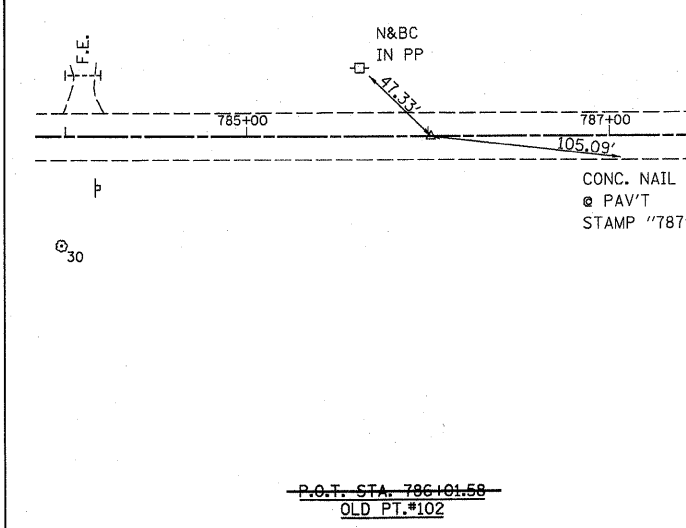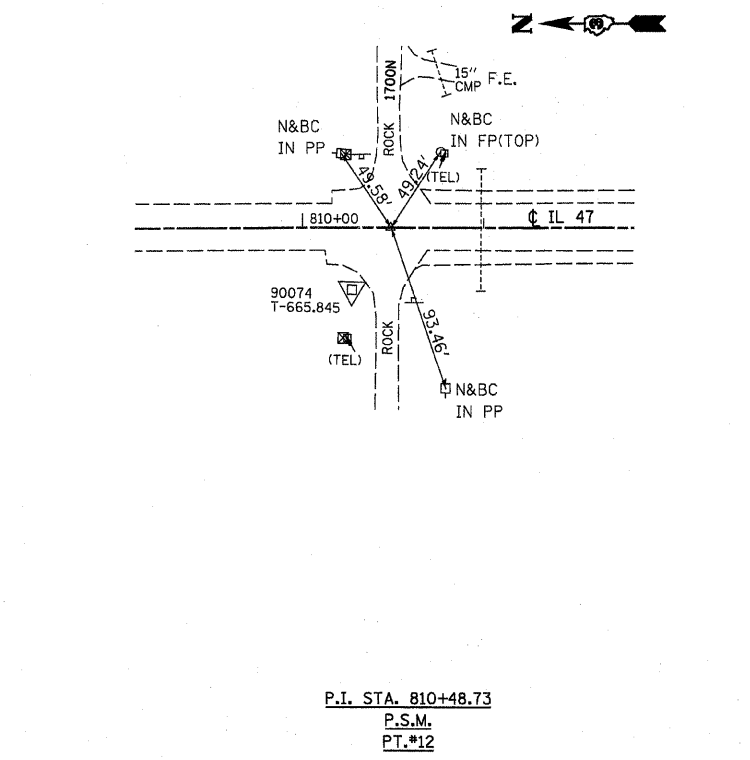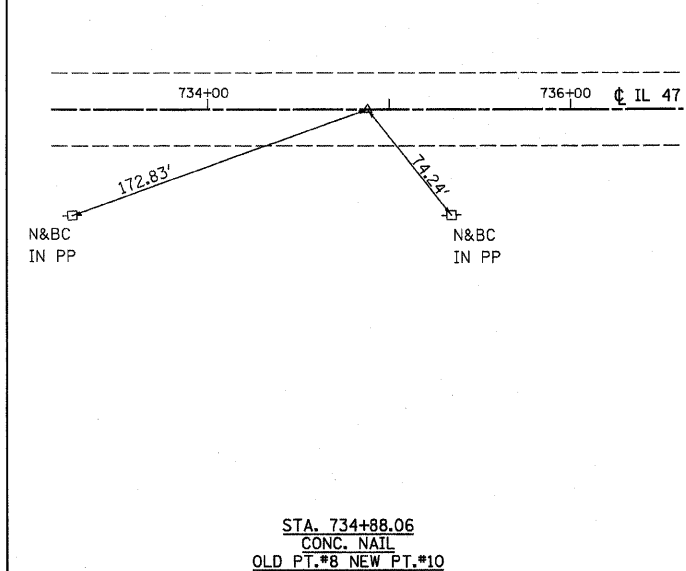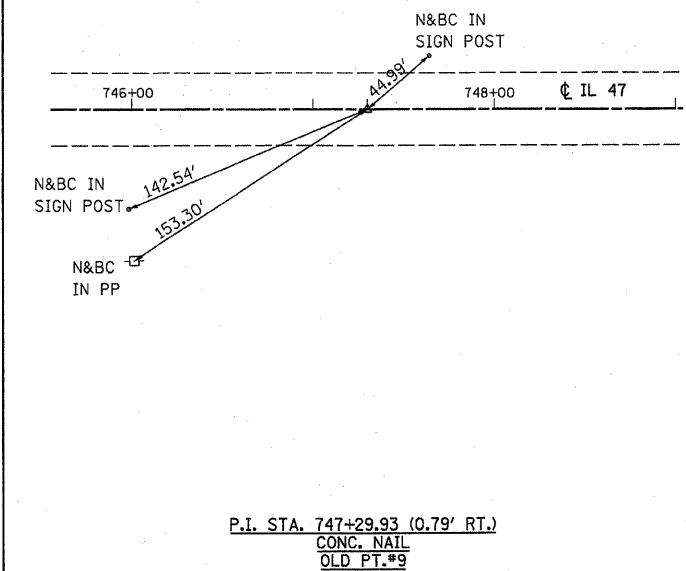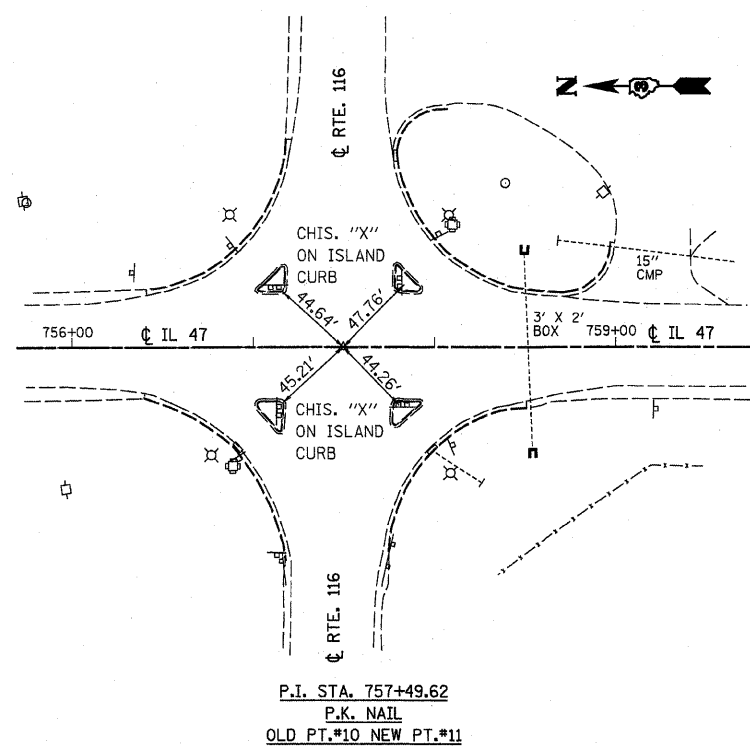

K:\110127\geopak\Ref\Ties&Benchmarks.dgn
